



**Daily Diary Report by Bid Item**

Contract No.: 04-0120F4

Diary #: 070 Const Calendar Day: 854 Date: 10-Jan-2012 Tuesday  
 Inspector Name: Altamirano, Victor Title: Transportation Engineer  
 Inspection Type:  
 Shift Hours: Break: Over Time:  
 Federal ID:  
 Location:  
 Reviewer: Schmitt, Alex Approved Date: Status: Submit

04-0120F4  
 04-SF-80-13.2/13.9  
 Self-Anchored  
 Suspension Bridge

**Weather**

Temperature 7 AM Below 40 12 PM 40 - 50 4PM 40 - 50  
 Precipitation Condition SUNNY

Working Day  If no, explain:

**Diary:**

Dispute

**Cable Hauling**

Cable Operations @ West Loop:

- NDS: Workers removing timber blocks in # 3 slot between divider plates.
- Prepping to float strand # 3.
- Installing adjusting strand jacks for strand # 2.
- @ SDS: Installing come-along on strand # 2.

- Spoke with ABF engineer regarding cross wires near the top slope ends of both North/South deviation saddle. Showed him the location at the location I was concerned about but the engineer was not sure if ABF will fix the crosswire. It was confirmed by management that CT will not direct ABF to fish the wires from strand # 2. Issue resolved.

1:15pm: Floating strand # 3.

1:44pm: Floating completed and installation started.

- Removed torpedo clamp.
- Apply knife plates on the North side of the jacking saddle on the # 3 strand.

2:42pm: MCM work - a steel stand flung over from MCM project and landed on the wood platform near NDS. No injuries reported and management is aware of the issue.

3:40pm: Workers continued chasing wires with knife plates on strand.

4:30pm: Workers are working on removing twist from strand.

Hours Worked: 11 hours total including 3 hours OT.

04-0120F4 Bid Item: 067 C-PWS-001.067 Install & Adjust PWS 1-5  
 AMERICAN BRIDGE/FLUOR, A JV

**Labor**

Trade	Class	Name	RT Hrs	OT Hrs	DT Hrs	Total	Remarks	Dispute
<b>Contractor:</b> AMERICAN BRIDGE/FLUOR, A JV								
Ironworker	FOR	JAMES BENNINGHOVE	8.00	2.00	0.00	10.00		<input type="checkbox"/>
Ironworker	JNM	MICHAEL PORTILLO	8.00	2.00	0.00	10.00		<input type="checkbox"/>
Ironworker	APP	Tony Miranda	8.00	2.00	0.00	10.00		<input type="checkbox"/>
Ironworker	APP	RYAN EVANCHIK	8.00	2.00	0.00	10.00		<input type="checkbox"/>
Ironworker	JNM	MICHAEL DRAPER	8.00	2.00	0.00	10.00		<input type="checkbox"/>
Ironworker	APP	RYAN NASH	8.00	2.00	0.00	10.00		<input type="checkbox"/>



## Daily Diary Report by Bid Item

**Job Name:** 04-0120F4    **Inspector Name** Altamirano, Victor    **Diary #:** 070    **Date:** 10-Jan-2012    **Tuesday**

Ironworker	FOR	JERRY KUBALA	8.00	2.00	0.00	10.00	<input type="checkbox"/>
Ironworker	JNM	RIGOVERTO GARCIA	8.00	2.00	0.00	10.00	<input type="checkbox"/>
Ironworker	APP	JONATHAN CANITES	8.00	2.00	0.00	10.00	<input type="checkbox"/>
Ironworker	JNM	JOSEPH STONE	8.00	2.00	0.00	10.00	<input type="checkbox"/>

**Attachment**



MCM post-tensioning: Strand that fell onto West End near NDS



Forming Strand # 3 @ SDS



Strand # 3 Installation @ jacking Saddle

Floating @ South Side Span

Circumferential Line on Strand # 3 @ Jacking Saddle

MCM post-tensioning: Strand that fell onto West End near NDS



## Daily Diary Report by Bid Item

Job Name: 04-0120F4

Inspector Name Altamirano, Victor

Diary #: 070

Date: 10-Jan-2012


Tuesday



Floating @ North Side Span



Twist in Strand # 3 after hauling east of 1st Torpedo Clamp

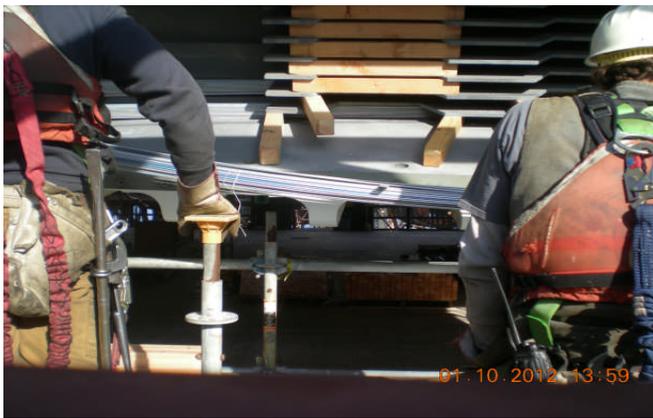

Using knife plates prior to forming strand into rectangular shape

MCM post-tensioning: Strand that fell onto West End near NDS
