



SAS Superstructure

Location: 04-SF-80-13.2 / 13.9

Client Name: CalTrans

Run date 22-Nov-14

Time 1:17 AM

Daily Diary Report by Bid Item

Contract No.: 04-0120F4

Diary #: 148 Const Calendar Day: 907 Date: 03-Mar-2012 Saturday

Inspector Name: Liu, Tai-Lin Title: Transportation Engineer

Inspection Type: Continuous

Shift Hours: 07:00 AM 14:30 PM Break: 00:30 Over Time: 07:00

Federal ID:

Location:

Reviewer: Schmitt, Alex Approved Date: Status: Submit

04-0120F4
04-SF-80-13.2/13.9
Self-Anchored
Suspension Bridge

Weather

Temperature 7 AM 48 12 PM 58 4PM 54

Precipitation Condition Sunny

Working Day If no, explain:

Diary:

Dispute

Cable Hauling

East End – North Side area
Tai-Lin Liu; Diary on 03/03/12, Saturday - Sunny (46 – 63 F)
From 0700 AM to 1200 AM

- Arrived at office at 0700AM. Checked e-mail, reviewed Bob's Log sheet for strand operation & went to field.

- In this morning, crew completed strand #73 installation and completed strand hauling on strand # 75 & started hauling for strand #76 also crew installed strand #77 into swift. I checked strand #73 socket to anchor rod connection and cutting knives. See Bob's log sheet for detail.

- At 1030 AM, went in back of anchorage area to check newly installed jam nuts and drawn lines.

- Forman Fish adjusted divider plate (# W142) at north side.

- Performed checking strand twist on # 74 with Daryoush.

- ABF Eric performed strand adjustment this morning.

Total 9 strands adjusted on 3/3/12, as listed below:

Adjusted Seq.	Strand #	Adjusted Amount
1	N68	7W
2	N70	52W
3	N72	48W
4	N69	16W
5	N71	41W
6	S69	23W
7	S70	59W
8	S71	51W
9	S72	39W

- At 1200 PM, handed the log to Bob and left bridge back to office.

- Performed paper work including time sheet and car log and left office at 1430.

- Refer to Bob's strand operation log sheet for tracking times of hauling operation. Labor worked hours were based on the information provided by all east end team members. OT = 7 hrs today.

04-0120F4 Bid Item: 067 C-PWS-051.067 Install & Adjust PWS 51-55

AMERICAN BRIDGE/FLUOR, A JV

Labor

Trade	Class	Name	RT Hrs	OT Hrs	DT Hrs	Total	Remarks	Dispute
Contractor: AMERICAN BRIDGE/FLUOR, A JV								



Daily Diary Report by Bid Item

Job Name: 04-0120F4 **Inspector Name** Liu, Tai-Lin **Diary #:** 148 **Date:** 03-Mar-2012 **Saturday**

Ironworker	JNM	LANCE CARLSON	0.00	8.00	2.00	10.00		<input type="checkbox"/>	
Ironworker	JNM	ROBERT RUSSELL	0.00	8.00	2.00	10.00		<input type="checkbox"/>	
Ironworker	APP	ROBERT MARTELL	0.00	8.00	2.00	10.00		<input type="checkbox"/>	
Ironworker	APP	JOSHUA JACKS	0.00	8.00	2.00	10.00		<input type="checkbox"/>	
Ironworker	JNM	JAMES WILKERSON	0.00	8.00	2.00	10.00		<input type="checkbox"/>	
Ironworker	FOR	JAMES STURGEON	0.00	8.00	2.00	10.00		<input type="checkbox"/>	
Ironworker	JNM	DANIEL MARTINEZ	0.00	8.00	2.00	10.00		<input type="checkbox"/>	
Ironworker	GEN	DANIEL DUNN	0.00	0.00	0.00	0.00		<input type="checkbox"/>	
Ironworker	JNM	DANIEL HUGHES	0.00	8.00	2.00	10.00		<input type="checkbox"/>	
Ironworker	APP	PATRICK OLEARY	0.00	8.00	2.00	10.00		<input type="checkbox"/>	
Ironworker	APP	LUIS PLANCARTE	0.00	8.00	2.00	10.00		<input type="checkbox"/>	
Ironworker	FOR	KEVIN KARBER	0.00	8.00	2.00	10.00		<input type="checkbox"/>	
Engineer		ADAM REEVE	0.00	8.00	0.00	8.00		<input type="checkbox"/>	
Engineer		ANKUR SINGH	0.00	0.00	0.00	0.00		<input type="checkbox"/>	
Engineer		ERIC BLUE	0.00	8.00	0.00	8.00		<input type="checkbox"/>	
Engineer		ADAM ROEBUCK	0.00	8.00	0.00	8.00		<input type="checkbox"/>	
Ironworker	APP	ANTHONY SMALER	0.00	8.00	2.00	10.00		<input type="checkbox"/>	
Operator	APP	SCOTT ROSS	0.00	8.00	2.00	10.00		<input type="checkbox"/>	
Mechanic	FOR	GENE PRATT	0.00	0.00	0.00	0.00		<input type="checkbox"/>	
Ironworker	APP	JEREMY PERALTA	0.00	0.00	0.00	0.00		<input type="checkbox"/>	
Ironworker	APP	JUN PERALTA	0.00	8.00	2.00	10.00		<input type="checkbox"/>	
Ironworker	APP	GREG WIEDER	0.00	8.00	2.00	10.00		<input type="checkbox"/>	
Ironworker	JNM	RICHARD DAMBOISE	0.00	8.00	2.00	10.00		<input type="checkbox"/>	
Operator	OTH	THEODORE ROHR	0.00	0.00	0.00	0.00		<input type="checkbox"/>	
Ironworker	JNM	JIMMY OSBURN	0.00	8.00	2.00	10.00		<input type="checkbox"/>	
Operator	OTH	KEVIN ALGER	0.00	8.00	2.00	10.00		<input type="checkbox"/>	
Ironworker	FOR	AARON KENT	0.00	8.00	2.00	10.00		<input type="checkbox"/>	
Operator	OTH	WILLIAM ALGER	0.00	8.00	2.00	10.00		<input type="checkbox"/>	
Operator	OTH	RYAN OKU	0.00	8.00	2.00	10.00		<input type="checkbox"/>	
Ironworker	APP	BRADLEY WHITBURN	0.00	8.00	2.00	10.00		<input type="checkbox"/>	
Ironworker	FOR	MATTHEW CHAMBERLAIN	0.00	8.00	2.00	10.00		<input type="checkbox"/>	
Ironworker	JNM	BARRY ROTHMAN	0.00	8.00	2.00	10.00		<input type="checkbox"/>	
Ironworker	APP	HENRY HERNANDEZ	0.00	8.00	2.00	10.00		<input type="checkbox"/>	
Electrician	GEN	RON KNARR	0.00	0.00	0.00	0.00		<input type="checkbox"/>	
Operator	JNM	JOHN GAGNON	0.00	0.00	0.00	0.00		<input type="checkbox"/>	
Equipment							Rental Company		
Equipment ID	Description		RT Hrs	OT Hrs	ST Hrs	IT Hrs	Remarks	Dispute	
Contractor:	AMERICAN BRIDGE/FLUOR, A JV								
*E0150583							No		
			0.00	0.00	0.00	0.00		<input type="checkbox"/>	
04-0120F4	Bid Item: 068	0-000-000.068	FURNISH SUSPENDER SYSTEM						
AMERICAN BRIDGE/FLUOR, A JV									

Attachment



Daily Diary Report by Bid Item


Job Name: 04-0120F4

Inspector Name Liu, Tai-Lin

Diary #: 148

Date: 03-Mar-2012


Saturday

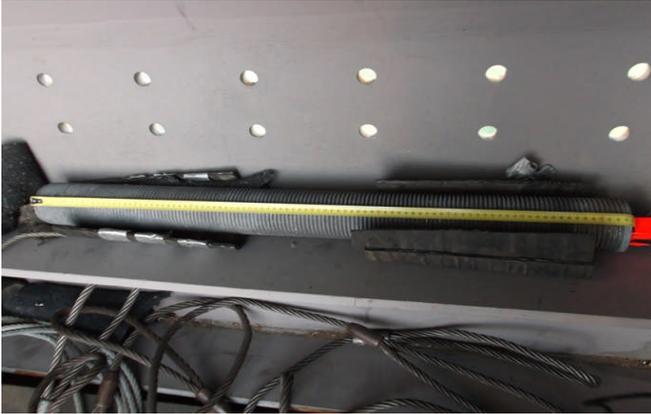

Extension rod for strand #90 - around 740 mm



Back of anchorage with the new installed jam nuts

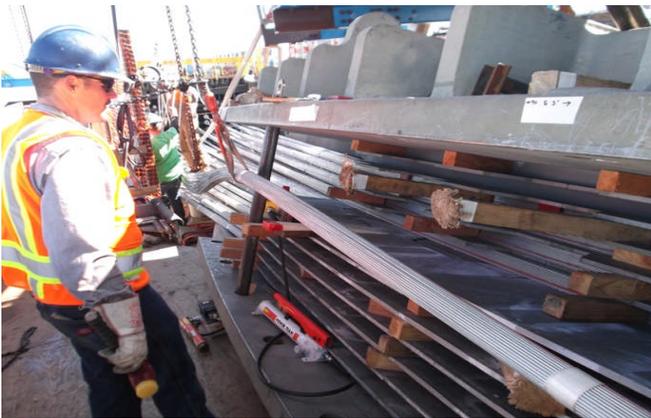

Fish adjusted divider plate on # 142



Perform checking strand twist on strand #74



Coupling for extension rod for using spair strand due to strand damaged by fire (#90)
