



SAS Superstructure

Location: 04-SF-80-13.2 / 13.9

Client Name: CalTrans

Run date 22-Nov-14

Time 1:15 AM

Daily Diary Report by Bid Item

Contract No.: 04-0120F4

Diary #: 152 Const Calendar Day: 911 Date: 07-Mar-2012 Wednesday

Inspector Name: Liu, Tai-Lin Title: Transportation Engineer

Inspection Type: Continuous

Shift Hours: 09:00 AM 19:30 PM Break: 00:30 Over Time: 02:00

Federal ID:

Location:

Reviewer: Schmitt, Alex Approved Date: Status: Submit

04-0120F4
04-SF-80-13.2/13.9
Self-Anchored
Suspension Bridge

Weather

Temperature 7 AM 40 12 PM 59 4PM 49
Precipitation Condition Sunny

Working Day [checked] If no, explain:

Diary:

Dispute

Cable Hauling

East End - North Side area

Tai-Lin Liu; Diary on 03/07/12, Wednesday - Sunny (38 - 64 F)

- Arrived at office at 0845 AM. Checked e-mail then went to field.
- Bob gave the log sheet to me at 0910 AM.
- Today, crew installed strand # 80 & 81, completed hauling on strand # 82, 83 & 84 (See Bob's log sheet for detail).
- Crew installed two divider plates today.
- After finished hauling on strand # 83, the strand still sit on the roller and suddenly the strand moving toward to the tower and damaged the one of the support roller (hit by cable clamps) at north side of east end due to tower taking out the twist (see picture).
- Rob took out the twist on strand # 82 between anchorage and saddle.
- Jimmy and Rob installed strand #S2 (spair strand for replacement of damaged strand # 82) socket to extension rod this afternoon,
- Contractor worked 10 hours instead of 12 hours today.
- I left bridge at 1715 PM.
- Performed paper works at office.
- Refer to Bob's strand operation log sheet for tracking times of hauling operation. Labor worked hours were based on the information provided by all east end team members. OT = 2 hrs today.

[checkbox]

04-0120F4 Bid Item: 067 C-PWS-051.067 Install & Adjust PWS 51-55

AMERICAN BRIDGE/FLUOR, A JV

Labor

Table with columns: Trade, Class, Name, RT Hrs, OT Hrs, DT Hrs, Total, Remarks, Dispute. Rows list laborers like LANCE CARLSON, ROBERT RUSSELL, etc.



## Daily Diary Report by Bid Item

**Job Name:** 04-0120F4    **Inspector Name** Liu, Tai-Lin    **Diary #:** 152    **Date:** 07-Mar-2012    **Wednesday**

Engineer		ADAM REEVE	0.00	0.00	0.00	0.00	<input type="checkbox"/>
Engineer		ANKUR SINGH	8.00	0.00	0.00	8.00	<input type="checkbox"/>
Engineer		ERIC BLUE	8.00	0.00	0.00	8.00	<input type="checkbox"/>
Engineer		ADAM ROEBUCK	8.00	0.00	0.00	8.00	<input type="checkbox"/>
Ironworker	APP	ANTHONY SMALER	8.00	2.00	0.00	10.00	<input type="checkbox"/>
Operator	APP	SCOTT ROSS	8.00	2.00	0.00	10.00	<input type="checkbox"/>
Mechanic	FOR	GENE PRATT	0.00	0.00	0.00	0.00	<input type="checkbox"/>
Ironworker	APP	JEREMY PERALTA	0.00	0.00	0.00	0.00	<input type="checkbox"/>
Ironworker	APP	JUN PERALTA	8.00	2.00	0.00	10.00	<input type="checkbox"/>
Ironworker	APP	GREG WIEDER	2.00	2.00	0.00	4.00	<input type="checkbox"/>
Ironworker	JNM	RICHARD DAMBOISE	0.00	0.00	0.00	0.00	<input type="checkbox"/>
Operator	OTH	THEODORE ROHR	0.00	0.00	0.00	0.00	<input type="checkbox"/>
Ironworker	JNM	JIMMY OSBURN	8.00	2.00	0.00	10.00	<input type="checkbox"/>
Operator	OTH	KEVIN ALGER	8.00	2.00	0.00	10.00	<input type="checkbox"/>
Ironworker	FOR	AARON KENT	8.00	2.00	0.00	10.00	<input type="checkbox"/>
Operator	OTH	WILLIAM ALGER	8.00	2.00	0.00	10.00	<input type="checkbox"/>
Operator	OTH	RYAN OKU	8.00	2.00	0.00	10.00	<input type="checkbox"/>
Ironworker	APP	BRADLEY WHITBURN	2.00	2.00	0.00	4.00	<input type="checkbox"/>
Ironworker	FOR	MATTHEW CHAMBERLAIN	8.00	2.00	0.00	10.00	<input type="checkbox"/>
Ironworker	JNM	BARRY ROTHMAN	0.00	0.00	0.00	0.00	<input type="checkbox"/>
Ironworker	APP	HENRY HERNANDEZ	8.00	2.00	0.00	10.00	<input type="checkbox"/>
Electrician	GEN	RON KNARR	0.00	0.00	0.00	0.00	<input type="checkbox"/>
Operator	JNM	JOHN GAGNON	0.00	0.00	0.00	0.00	<input type="checkbox"/>

**Equipment**

**Rental Company**

Equipment ID	Description	RT Hrs	OT Hrs	ST Hrs	IT Hrs	Remarks	Dispute
<b>Contractor:</b>	AMERICAN BRIDGE/FLUOR, A JV						
	*E0150583					No	
		0.00	0.00	0.00	0.00		<input type="checkbox"/>

**04-0120F4    Bid Item: 068    0-000-000.068    FURNISH SUSPENDER SYSTEM**

AMERICAN BRIDGE/FLUOR, A JV

**Attachment**



Crew installed two divider plates today



Damaged roller (at north side of east end) due to tower took out twist on strand # 83 - strand sit on the roller

## Daily Diary Report by Bid Item

Job Name: 04-0120F4

Inspector Name Liu, Tai-Lin


Diary #: 152

Date: 07-Mar-2012

Wednesday



Jimmy & Rob connected spair strand # S2 socket to anchor rod

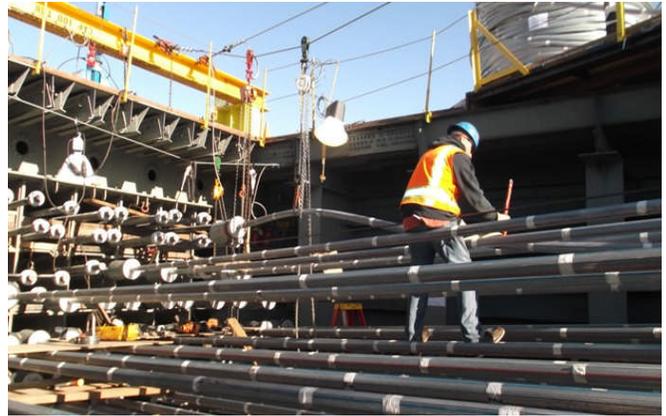

Rob took out twist on strand #82 between anchorage to saddle
