



### SAS Superstructure

Location: 04-SF-80-13.2 / 13.9

Client Name: CalTrans

Run date 22-Nov-14

Time 1:14 AM

## Daily Diary Report by Bid Item

Contract No.: 04-0120F4

Diary #: 153 Const Calendar Day: 912 Date: 08-Mar-2012 Thursday

Inspector Name: Liu, Tai-Lin Title: Transportation Engineer

Inspection Type: Continuous

Shift Hours: 09:00 AM 19:30 PM Break: 00:30 Over Time: 02:00

Federal ID:

Location:

Reviewer: Schmitt, Alex Approved Date: Status: Submit

04-0120F4  
04-SF-80-13.2/13.9  
Self-Anchored  
Suspension Bridge

### Weather

Temperature 7 AM 40 12 PM 59 4PM 49

Precipitation Condition Sunny

Working Day  If no, explain:

### Diary:

Dispute

#### Cable Hauling

East End – North Side area

Tai-Lin Liu; Diary on 03/09/12, Thursday - Sunny (41 – 63 F)

- Arrived at office at 0850 AM. Checked e-mail then went to field.

- Bob gave the log sheet to me at 0915 AM. Bob told me that strand # 88 was dropped when transported from borage to bridge and will be replaced by spare strand # S1.

- Today, crew installed strand # 82 - 85, completed hauling on strand # 85 - 87 (See Bob's log sheet for detail).

- Forman (Fish) fixed roller damaged by cable clamp yesterday.

- I verified strand # 82 screw lengths which was replaced by spare strand and extended anchor rod & coupler. The measured lengths were OK. Jimmy and Rob installed strand #S2 (spare strand for replacement of damaged strand # 82) socket to extension rod yesterday,

- Crew replaced rollers at starting point of track.

- Bob B & Jacks left job site at 1230 PM, they started 0300 AM today - 5 hours double time & 5 hours regular time. . .

- Two new guys, Jacob Stafford & Zach MacDonald joined Fish's group today.

- I left bridge at 1915 PM.

- Performed paper works at office.

- Refer to Bob's strand operation log sheet for tracking times of hauling operation. Labor worked hours were based on the information provided by all east end team members. OT = 2 hrs today.

04-0120F4 Bid Item: 067 C-PWS-051.067 Install & Adjust PWS 51-55

AMERICAN BRIDGE/FLUOR, A JV

### Labor

Trade	Class	Name	RT Hrs	OT Hrs	DT Hrs	Total	Remarks	Dispute
<b>Contractor:</b> AMERICAN BRIDGE/FLUOR, A JV								
Ironworker	JNM	DANIEL HUGHES	8.00	2.00	2.00	12.00		<input type="checkbox"/>
Ironworker	JNM	JIMMY OSBURN	8.00	2.00	2.00	12.00		<input type="checkbox"/>
Ironworker	JNM	ROBERT RUSSELL	5.00	0.00	5.00	10.00		<input type="checkbox"/>
Ironworker	APP	ROBERT MARTELL	8.00	2.00	2.00	12.00		<input type="checkbox"/>
Ironworker	APP	JOSHUA JACKS	5.00	0.00	5.00	10.00		<input type="checkbox"/>
Ironworker	JNM	JAMES WILKERSON	8.00	2.00	2.00	12.00		<input type="checkbox"/>
Ironworker	FOR	JAMES STURGEON	8.00	2.00	2.00	12.00		<input type="checkbox"/>
Ironworker	GEN	DANIEL DUNN	8.00	2.00	2.00	12.00		<input type="checkbox"/>
Ironworker	APP	ANTHONY SMALER	8.00	2.00	2.00	12.00		<input type="checkbox"/>
Ironworker	APP	HENRY HERNANDEZ	8.00	2.00	2.00	12.00		<input type="checkbox"/>
Ironworker	JNM	LANCE CARLSON	8.00	2.00	2.00	12.00		<input type="checkbox"/>



## Daily Diary Report by Bid Item

**Job Name:** 04-0120F4    **Inspector Name** Liu, Tai-Lin    **Diary #:** 153    **Date:** 08-Mar-2012    **Thursday**

Ironworker	APP	LUIS PLANCARTE	8.00	2.00	2.00	12.00	<input type="checkbox"/>
Ironworker	FOR	KEVIN KARBER	8.00	2.00	2.00	12.00	<input type="checkbox"/>
Engineer		ADAM REEVE	0.00	0.00	0.00	0.00	<input type="checkbox"/>
Engineer		ANKUR SINGH	0.00	0.00	0.00	0.00	<input type="checkbox"/>
Engineer		ERIC BLUE	8.00	0.00	0.00	8.00	<input type="checkbox"/>
Engineer		ADAM ROEBUCK	8.00	0.00	0.00	8.00	<input type="checkbox"/>
Ironworker	JNM	DANIEL MARTINEZ	8.00	2.00	2.00	12.00	<input type="checkbox"/>
Operator	OTH	KEVIN ALGER	8.00	2.00	2.00	12.00	<input type="checkbox"/>
Ironworker	JNM	Jacob Stafford	8.00	2.00	2.00	12.00	<input type="checkbox"/>
Electrician	GEN	RON KNARR	0.00	0.00	0.00	0.00	<input type="checkbox"/>
Mechanic	FOR	GENE PRATT	0.00	0.00	0.00	0.00	<input type="checkbox"/>
Ironworker	APP	JEREMY PERALTA	0.00	0.00	0.00	0.00	<input type="checkbox"/>
Ironworker	APP	JUN PERALTA	8.00	2.00	2.00	12.00	<input type="checkbox"/>
Ironworker	APP	GREG WIEDER	8.00	2.00	2.00	12.00	<input type="checkbox"/>
Ironworker	JNM	RICHARD DAMBOISE	8.00	2.00	2.00	12.00	<input type="checkbox"/>
Ironworker	FOR	AARON KENT	8.00	2.00	2.00	12.00	<input type="checkbox"/>
Operator	JNM	JOHN GAGNON	0.00	0.00	0.00	0.00	<input type="checkbox"/>
Ironworker	APP	PATRICK OLEARY	8.00	2.00	2.00	12.00	<input type="checkbox"/>
Operator	APP	SCOTT ROSS	8.00	2.00	2.00	12.00	<input type="checkbox"/>
Operator	OTH	WILLIAM ALGER	8.00	2.00	2.00	12.00	<input type="checkbox"/>
Operator	OTH	RYAN OKU	8.00	2.00	2.00	12.00	<input type="checkbox"/>
Ironworker	APP	BRADLEY WHITBURN	0.00	0.00	0.00	0.00	<input type="checkbox"/>
Ironworker	FOR	MATTHEW CHAMBERLAIN	0.00	0.00	0.00	0.00	<input type="checkbox"/>
Ironworker	JNM	BARRY ROTHMAN	8.00	2.00	2.00	12.00	<input type="checkbox"/>
Ironworker	JNM	Zach MacDonald	8.00	2.00	2.00	12.00	<input type="checkbox"/>
Operator	OTH	THEODORE ROHR	0.00	0.00	0.00	0.00	<input type="checkbox"/>

Equipment		Rental Company				Dispute	
Equipment ID	Description	RT Hrs	OT Hrs	ST Hrs	IT Hrs		Remarks
<b>Contractor:</b> AMERICAN BRIDGE/FLUOR, A JV							
*E0150583						No	
		0.00	0.00	0.00	0.00		<input type="checkbox"/>

**04-0120F4    Bid Item: 068    0-000-000.068    FURNISH SUSPENDER SYSTEM**  
 AMERICAN BRIDGE/FLUOR, A JV

**Attachment**



Fish (forman) fixed roller



Strand dropped to ground during hauling operation

## Daily Diary Report by Bid Item

Job Name: 04-0120F4

Inspector Name Liu, Tai-Lin

Diary #: 153


Date: 08-Mar-2012 Thursday



Roller damaged by cable clamp when slacking on strand #83



Replaced roller at start point of track

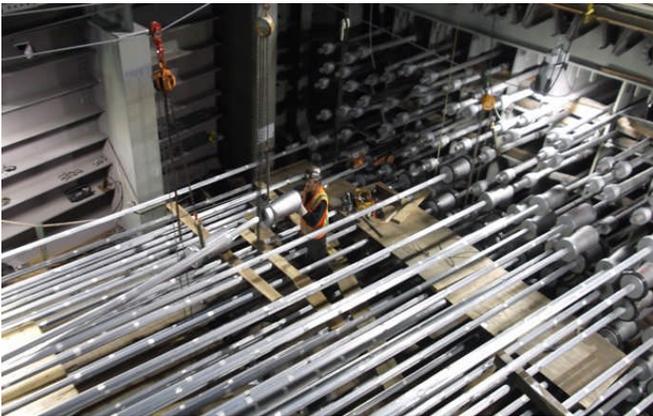

Jimmy cleaned up the socket



Crew picked up dropped down strand from swift
