



**Daily Diary Report by Bid Item**

Contract No.: 04-0120F4

Diary #: 296 Const Calendar Day: 937 Date: 02-Apr-2012 Monday  
 Inspector Name: Iranmanesh, Abbas Title: Transportation Engineer  
 Inspection Type: Continuous  
 Shift Hours: 07:00 am 07:30 pm Break: 00:30 Over Time: 04:00  
 Federal ID:  
 Location:  
 Reviewer: Granados, Roman Approved Date: Status: Submit

04-0120F4  
 04-SF-80-13.2/13.9  
 Self-Anchored  
 Suspension Bridge

**Weather**

Temperature 7 AM 50 - 60 12 PM 4PM 60 - 68  
 Precipitation None Condition Mostly cloudy

Working Day  If no, explain:

**Diary:**

Dispute

**Work description.**

APRIL 2, 2012 Diary

ABF Crews activities at the West Loop:

1. PWS HAULING, FLOATING, FORMING AND INSTALLATING:

•HAULING PWS # 127, PWS #128, PWS #129 and PWS # 130:

HAULING	START	TIME AT N.D.S.	TIME AT S.D.S.	END TIME
PWS # 127	7:12A.M.	7:43A.M.-7:58A.M.	8:10A.M.-8:18A.M.	9:03A.M.
PWS # 128	10:13A.M.	10:48A.M.-10:56A.M.	11:10A.M.-11:20A.M.	0:06P.M.
PWS # 129	2:09P.M.			4:01P.M.
PWS # 130	5:31P.M.			Not
Completed				

N.D.S.= North Deviation Saddle (Transfer of PWS from the Primary Hauling System to the Secondary Hauling System)

S.D.S. = South Deviation Saddle (Transfer of PWS from the Secondary Hauling System to the Primary Hauling System)

•FLOATING PWS # 127, PWS # 128, and PWS #129:

FLOATING D.S.	CLAPM TO N.D.S.F.A	CLAPM TO S.D.S.F.A	FLOATING AT LOOP	FLOATING AT
PWS # 127	9:04A.M.-9:16A.M.	9:04A.M.-9:15A.M	9:16A.M.	9:41A.M.
PWS # 128	0:35P.M.-0:47P.M.	0:35P.M.-0:43P.M.	0:59P.M.	
PWS # 129			In the afternoon	In the afternoon

N.D.S.F.A. = North Deviation Saddle Floating Arm

S.D.S.F.A. = South Deviation Saddle Floating Arm

## Daily Diary Report by Bid Item

Job Name: 04-0120F4 Inspector Name Iranmanesh, Abbas Diary #: 296 Date: 02-Apr-2012 Monday

•FORMING PWS # 127, PWS # 128 and PWS # 129:

FORMING	JACKING SADDLE	NORTH DEVIATIONSADDLE	SOUTH DEVIATION SADDLE
PWS # 127	9:22A.M.-9:42A.M.	9:48A.M.-10:22A.M	10:11A.M.-10:42A.M.
PWS # 128	1:04P.M.-1:26P.M.	2:00P.M.-	2:00P.M.-
PWS # 129	In the afternoon	In the afternoon	In the afternoon

•INSTALING PWS #127, PWS #128 and PWS #129:

INSTALLING	JACKING SADDLE	NORTH DEVIATIONSADDLE	SOUTH DEVIATION SADDLE
PWS # 127	9:50A.M.-10:18A.M.	10:35A.M.-11:02A.M.	10:43A.M.-11:12A.M.
PWS # 128	In the afternoon	In the afternoon	In the afternoon
PWS # 129	In the afternoon	In the afternoon	In the afternoon

•PWS # 127 and PWS # 128 SLACK ADJUSTEMS:

SLACK ADJUSTMENT	SET UP HYDRAULIC PULLING SYSTEM	ADJUSTMENT TIME
PWS # 127	10:43A.M.	11:10A.M.-11:35A.M.
PWS # 128	In the afternoon	In the afternoon

SET UP AT LOWER END OF THE N.D.S.

2. NOTES:

•NOTE-1: PWS # 127 Was checked for quality of installation; the upper wire is buried for 12 feet length at the top, the red wire is buried for 6 feet length at the middle, and the third wire from the top is buried slightly at some distance 12 feet from the top of the S.D.S. Wire number 5 is buried slightly for 6 feet length at the middle of the N.D.S. Pictures are attached for more detail.

•NOTE-2: PWS # 127 and PWS # 128 had 90 degree twist at both the N.D.S. and the S.D.S. which was removed by the Floating Arm clamp.

•NOTE-3: Too much jacking of the divider plates for creating more clearance during PWS installation will damage the array of the wires of the upper strand; pictures are attached to show the condition.

•NOTE-4: The PWS # 127 centerline is off 62 mm to the South with respect to the J.S. centerline.

•NOTE-5: ABF Engineer, Mr. Ankur Singh and ABF superintendent Mr. Scott Smith were present.

•NOTE-6: 2 hours OT

ABF Crews involved at the West loop:

S.D.S.

-Jerry Kubala  
- Rigovertto Garcia  
-Ryan Nash  
-Jonathan Canites  
-Joseph Stone

N.D.S.



-Ryan Evanchick  
-Jim Benninghove  
-Mike Draper  
-Mike Portillo  
-Ronny Chamberlain

## Daily Diary Report by Bid Item

Job Name: 04-0120F4 Inspector Name Iranmanesh, Abbas Diary #: 296 Date: 02-Apr-2012 Monday

J.S. and Slack Adjustment -Matthew Holt -Jonathon Biskner -Lonny Candelaria -Andy Zhen -Eduardo Jimenez Padilla			
04-0120F4	Bid Item: 067	C-PWS-096.067	Install & Adjust PWS 96-100
AMERICAN BRIDGE/FLUOR, A JV			
04-0120F4	Bid Item: 067	C-PWS-101.067	Install & Adjust PWS 101-105
AMERICAN BRIDGE/FLUOR, A JV			
04-0120F4	Bid Item: 067	C-PWS-106.067	Install & Adjust PWS 106-110
AMERICAN BRIDGE/FLUOR, A JV			
04-0120F4	Bid Item: 067	C-PWS-111.067	Install & Adjust PWS 111-115
AMERICAN BRIDGE/FLUOR, A JV			
04-0120F4	Bid Item: 067	C-PWS-125.067	Install & Adjust PWS 125-130
AMERICAN BRIDGE/FLUOR, A JV			

### Attachment

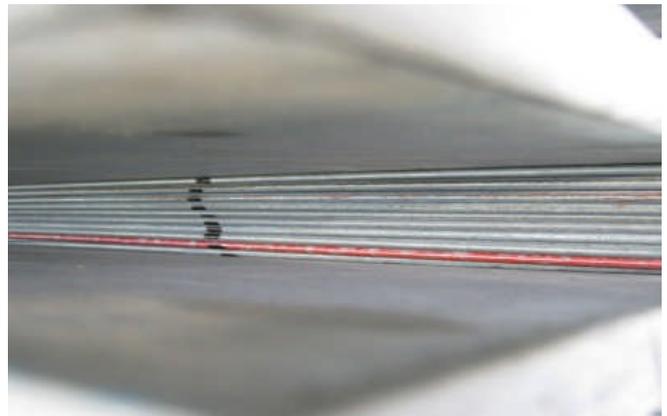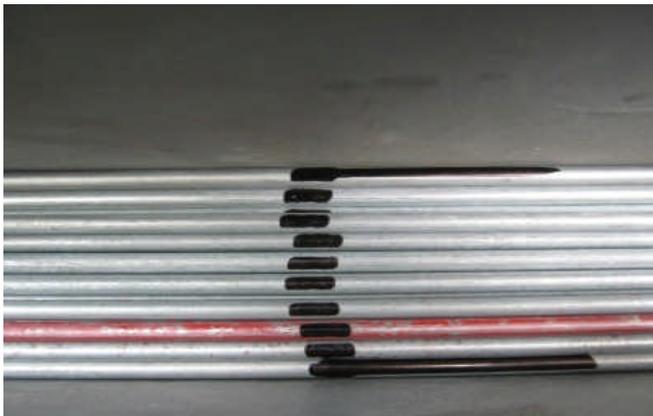

# Daily Diary Report by Bid Item



Job Name: 04-0120F4

Inspector Name Iranmanesh, Abbas

Diary #: 296

Date: 02-Apr-2012

Monday

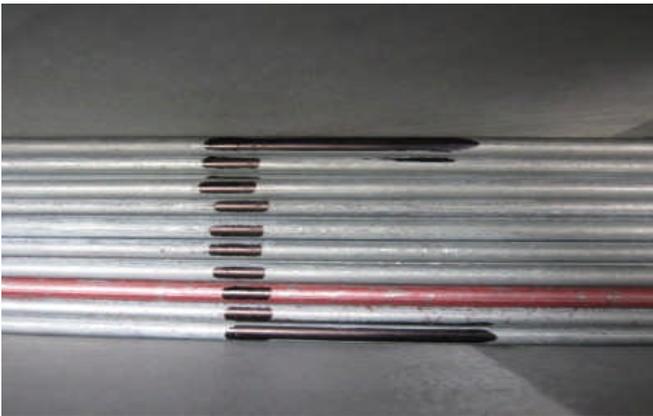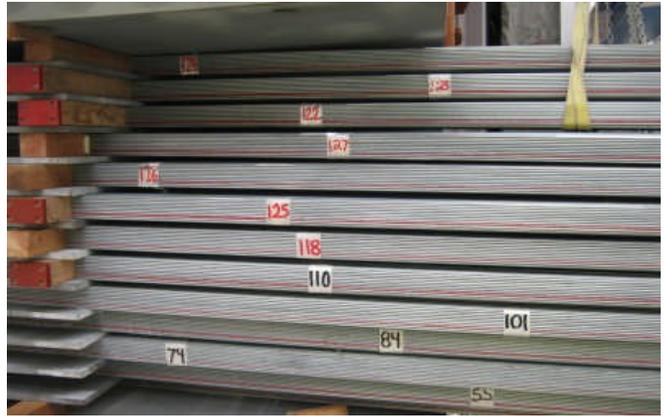

---

**Daily Diary Report by Bid Item**

Job Name: 04-0120F4

Inspector Name Iranmanesh, Abbas

Diary #: 296

Date: 02-Apr-2012

Monday

---

