



Daily Diary Report by Bid Item

Contract No.: 04-0120F4

Diary #: 168 Const Calendar Day: 175 Date: 26-Nov-2012 Monday
 Inspector Name: Liu, Tai-Lin Title: Transportation Engineer
 Inspection Type: Intermittent
 Shift Hours: 07:00 AM 04:30 PM Break: 00:30 Over Time: 01:00
 Federal ID:
 Location:
 Reviewer: Schmitt, Alex Approved Date: Status: Submit

04-0120F4
 04-SF-80-13.2/13.9
 Self-Anchored
 Suspension Bridge

Weather

Temperature 7 AM 48 12 PM 61 4PM 62
 Precipitation Condition Overcast & Foggy

Working Day If no, explain:

Diary:

Dispute

Cable Wrapping



11/26/12, Monday, Foggy and Overcast (From 7:00 am – 12:00 pm), 45-60 °F
 -06:50 am arrived at office, 07:10 am at job site.
 -7:30 am saw two labors (Hector Limon / Juan Hernandez), and one IRW (Tony) at Catwalk. At 08:00 am, crew (Jason, Tony, Alex, Scott, and Barry at Tower controlling high line) started jumping pull wrapping machine from S30W to S32W (from 08:00 – 09:45 am). Forman Brian showed up around 08:20 am.
 -Brian, Alex and Tony – Changing S-Wire from Bobbin (2) on Push Wrapping Machine (S32E from 09:15 to 09:50 am).
 -Two labors applied Zinc Paste at upper half bay area (between S34 and S32), Jason, Alex and Tony Performed S-wire splices at pull wrapping machine started from 09:30 to 10:00 am.
 - At 10:00 am, crew took a break until 10:15 am.
 -After break, crew spliced s-wires on Push wrapping machines. Both pull & push machines were operated around 10:50 am.
 -Again, the push wrapping machine operation was much smoother than the pull wrapping machine, it wrapped around 2.5 meters and cut out twice of cable strips and pull machine just wrapped less than 1 meter of length. ABF's Photographer Joe was there (11:25 am) taking pictures on wrapping operation. At 12:00, operation stopped, I left site around 12:15 pm and saw Brian Wolcott at skyway parking lot. Talked to him about field status and came back office around 12:35 pm.
 -Had lunch at 12:55 pm. Afternoon, checked e-mail, documented pictures and paper work (check list & diary) and left office around 04:30 PM.

Attachment



Daily Diary Report by Bid Item

Job Name: 04-0120F4

Inspector Name Liu, Tai-Lin

Diary #: 168

Date: 26-Nov-2012

Monday


Jumping Pull Wrapping Machine



Changing S-Wire Bobbin on Push Wrapping Machine



Splicing S-Wire for Pull Machine

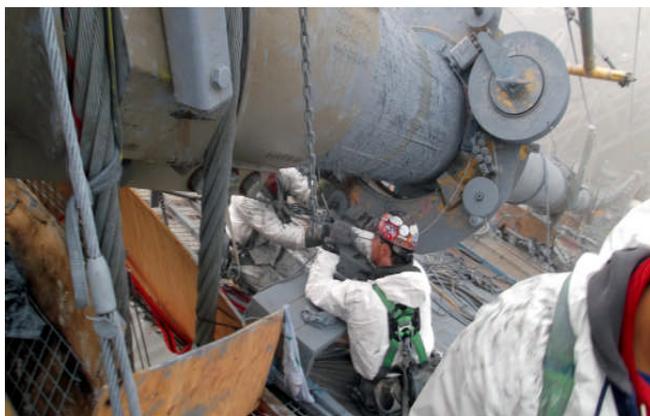

Splicing S-Wire for Pull Machine
