



Daily Diary Report by Bid Item

Contract No.: 04-0120F4

Diary #: 174 Const Calendar Day: 184 Date: 05-Dec-2012 Wednesday

Inspector Name: Liu, Tai-Lin Title: Transportation Engineer

Inspection Type: Continuous

Shift Hours: 07:00 AM 05:30 PM Break: 00:30 Over Time: 01:00

Federal ID:

Location:

Reviewer: Schmitt, Alex Approved Date: Status: Submit

04-0120F4
 04-SF-80-13.2/13.9
 Self-Anchored
 Suspension Bridge

Weather

Temperature 7 AM 52 12 PM 63 4PM 65
 Precipitation Condition Overcast

Working Day If no, explain:

Diary:


Dispute

Cable Wrapping

12/05/12, Wednesday, Overcast (Shift from 12:30 to 17:30), 52 - 66 F

- 07:00 to 11:00 performed paper work at office.
- 11:30 lunch and talked to Brian for field status.
- 12:15 at deck, 12:30 at Catwalk, saw Brian Wocott at tower elevator.
- Crew: Hector, Curtis, Alex, Brian, Tony, Barry & Jason.
- Push machine was wrapping at the location around 4.5 meter from S40E, pull machine completed wrapping at S38W area.
- Push machine stopped wrapping for removing seizing bands, and labors applied zinc paste accordingly.
- Restarted push machine and stopped again for bobbin out of s-wires.
- Crew performed anchoring s-wire, cut the sires changed s-wire spool and spliced s-wires ready to restart.
- Jason, Tony & Scott performed cleaning, at 2:25 pm push machine restarted.
- Alex S and Joe (Photographer) were here this afternoon.
- At 03:45 pm, push machine stopped and completed wrapping at this Bay (S38 - S40).
- Brian & Barry left site around 4:00 PM, the rest of crew were ready to remove push machine away from SSS.
- See picture, the crew completed removing push machine around 04:50 pm, and pull machine also been moved to bay between S38 to S40.
- Crew left, and I left job site as well.

Attachment

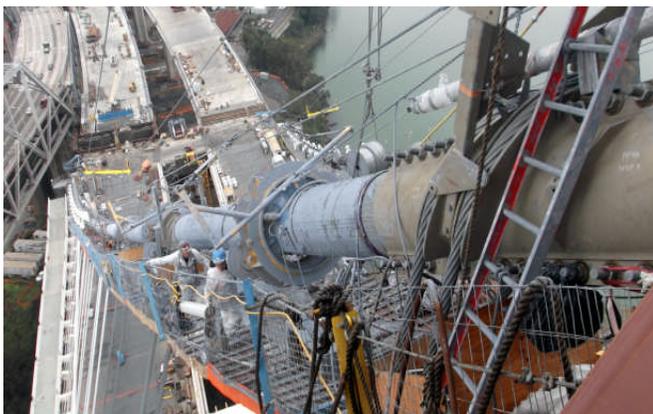

Daily Diary Report by Bid Item

Job Name: 04-0120F4 Inspector Name Liu, Tai-Lin

Diary #: 174 Date: 05-Dec-2012 Wednesday

Crew changed s-wire spool into bobbin



Restarted push wrapping machine



Tony anchored S-Wire on Push Machine due to out of S-wire



Removed stanchion post for jumping the pull machine



Push machine completed wrapping IW anchor the S-wire



Performed splicing s-wires

Daily Diary Report by Bid Item

Job Name: 04-0120F4

Inspector Name Liu, Tai-Lin

Diary #: 174

Date: 05-Dec-2012

Wednesday



Crew removed push machine from the cable



Forman Brian & Hector removed seizing bands
