



**SAS Superstructure**

Location: 04-SF-80-13.2 / 13.9

Client Name: CalTrans

Run date 22-Nov-14

Time 9:32 AM

**Daily Diary Report by Bid Item**

Contract No.: 04-0120F4

Diary #: 183 Const Calendar Day: 276 Date: 07-Mar-2013 Thursday

Inspector Name: Liu, Tai-Lin Title: Transportation Engineer

Inspection Type: Continuous

Shift Hours: 07:00 AM 04:00 PM Break: 00:30 Over Time:

Federal ID:

Location:

Reviewer: Soheilifard, Saman Approved Date: Status: Submit

04-0120F4  
04-SF-80-13.2/13.9  
Self-Anchored  
Suspension Bridge

**Weather**

Temperature 7 AM 42 12 PM 55 4PM 50  
Precipitation 70% Condition Overcast

Working Day  If no, explain:

**Diary:**

Dispute

**Paint Cable System**

03-07-13, Thursday, Overcast, 41-56 F - Cable Suspender Rope Paint (North/South Main Span)



- Arrived office around 07:20, checked e-mail and attending safety meeting from 08:00 - 09:15 AM.
- Laraine told me, she will cover afternoon 3:30 to 5:30 PM work at field and asked me to cover from 12:45 to 3:30 PM work.
- Performed paper work & checked ABF final CB bolt tensioning spreadsheets until 11:30 AM.
- Had lunch and went to field around 12:50 AM.
- Laraine told me that DTM on S48 is OK. N50 - N60 suspender rope ready for Pegalike paint. N84 & N86 were OK for SP1, and N88 was still under cleaning.
- At 1:15 PM, saw crew just finishing N88 rope steam cleaning.
- Went to south cable, QA/QC were checking punchlist items at S30 & S32.
- METS (Rex) with painter were checking seperators at south side span area (S28).
- Saw Samam, Alex with Donna, sami, Robert & Abass.
- At 2:00 PM, two painters performed water rinse on N56. Talked to one of the painter, he told me that they already rinsed 4 suspender ropes (N50 - N54) this morning and plan to finish upto N60 today and ready to do the Pegalink paint tomorrow morning.
- Saw Rex at S46 checking seperator paint from basket listed from tower crane and came down to the North Deck @ 02:20 PM.
- Talked to Rex, he told me that so far he checked S38, S40, S44 & S46 top 4 seperators (Prep./Pegalink paint) & NW S44 & SE S38 touch up (Blue Tape still on the ropes), he was going to check S44 & S46 second tier seperator paint.
- Rope rinse up to N60 completed around 3:00 PM. Painter told me that they will performe pegalink painting tomorrow morning.
- Laraine showed up in field, talked to her and John Lyonon as well.
- Left job site around 03:40 PM.
- Labor & Equipment will be tracked by Laraine.
- No OT today (03/07/13).

**Attachment**



## Daily Diary Report by Bid Item

Job Name: 04-0120F4

Inspector Name Liu, Tai-Lin

Diary #: 183

Date: 07-Mar-2013


Thursday



Crew performed suspender rope rinse at N56



@ 1:20 PM, QC/QA checked punchlist items @ S30 & S32

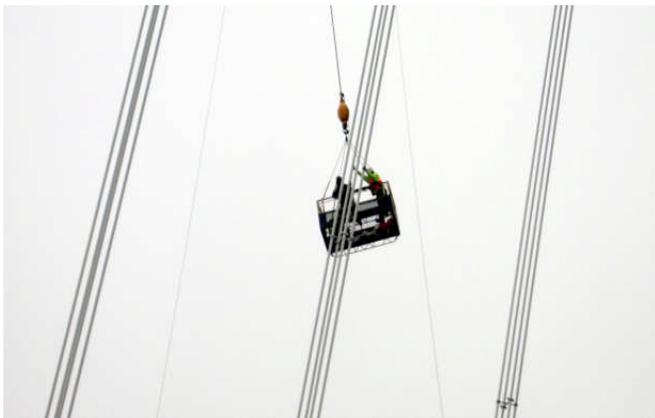

METS (Rex) checked separator Prep./Pegalink



METS (Rex) checked separator paint at S46 - second tier



Two painters performed suspender rinse at N58
