



SAS Superstructure

Location: 04-SF-80-13.2 / 13.9

Client Name: CalTrans

Run date 22-Nov-14

Time 9:28 AM

Daily Diary Report by Bid Item

Contract No.: 04-0120F4

Diary #: 200 Const Calendar Day: 298 Date: 29-Mar-2013 Friday
Inspector Name: Liu, Tai-Lin Title: Transportation Engineer
Inspection Type: Continuous
Shift Hours: 07:00 AM 03:30 PM Break: 00:30 Over Time:

04-0120F4
04-SF-80-13.2/13.9
Self-Anchored
Suspension Bridge

Federal ID:

Location:

Reviewer: Soheilifard, Saman Approved Date: Status: Submit

Weather

Temperature 7 AM 50 12 PM 68 4PM 64

Precipitation Condition Mostly Cloudy - Heavy Fog at early morning

Working Day If no, explain:

Diary:

Dispute

Paint Cable System

03-29-13, Friday, Mostly Cloudy- Heavy Fog at early morning, 48-79 F, Humidity 63% - Cable Suspender Rope Paint (North Main Span) & Separator Installation / Painting



- * Weather was foggy in early morning. Went to field around 08:35 AM, bridge deck was wet. Saw three painters cleaning the equipment waiting for QA/QC checking DTM painted yesterday. No QA/QC was on the field at the time.
- * Went to connex talking to METS Rex about the work status.
- * Rex told me there will be holidays & paint crack (due to applied thicker film) at the 2nd DTM on the ropes. Heavy fog at the moment that the painted area can not be inspected.
- * Went to tower with Laraine to see the cable painting operation.
- * At 09:50 AM, saw QC-Fred & QA - Rex at the NMS N62 area ready to take mem-basket checking the 2nd DTM coating between N62 to N74 area.
- * QA/QC performed DTM coating checking started at 09:55 AM and ended at 11:15 AM, results showed that CCC need hand touch ropes on N64 - SW, N70 - NE & N74 - SW at the area below 60' back area, Rex also mentioned that lots paint area having crack due to thicker film been spraied. QA said that the craking paint area was due to high wind during the painting operation. Leo asked painters to prepared the hand touch operation for above mentioned three ropes.
- * Mahmoud was there, he will be inspecting the work. Left job site & came back to office around 12:25 PM.
- * Performed paperwork afternoon.
- * No OT today 0329-13

Attachment



Daily Diary Report by Bid Item

Job Name: 04-0120F4

Inspector Name Liu, Tai-Lin


Diary #: 200

Date: 29-Mar-2013


Friday



QA/QC performed checking 2nd DTM coating at N62 area

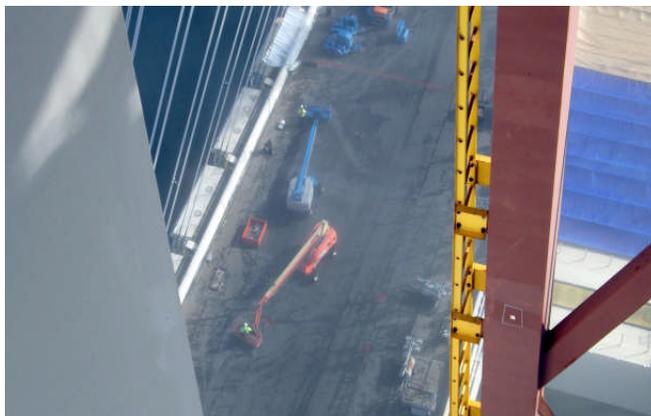

At 09:50 AM, QC-Fred & QA -Rex were ready to check 2nd DTM coating at N62 to N74 area.

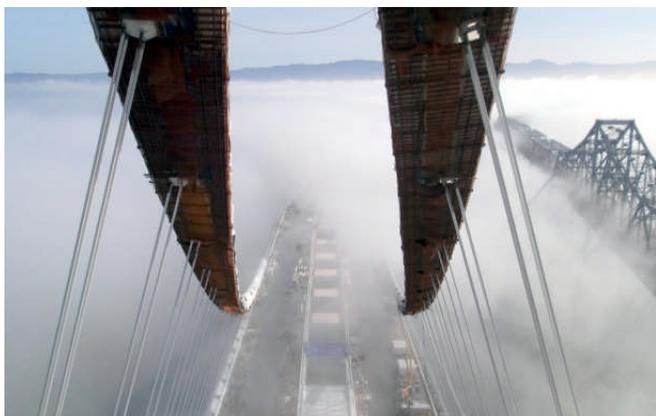

Heavy fog at field in early morning
