



**Daily Diary Report by Bid Item**

Contract No.: 04-0120F4

Diary #: 209 Const Calendar Day: 323 Date: 23-Apr-2013 Tuesday  
 Inspector Name: Liu, Tai-Lin Title: Transportation Engineer  
 Inspection Type: Continuous  
 Shift Hours: 07:00 AM 05:30 PM Break: 00:30 Over Time: 02:00

04-0120F4  
 04-SF-80-13.2/13.9  
 Self-Anchored  
 Suspension Bridge

Federal ID:

Location:

Reviewer: Ku, Stanley Approved Date: 20-Nov-14 Status: Approved

**Weather**

Temperature 7 AM 58 12 PM 76 4PM 74  
 Precipitation Condition Clear

Working Day  If no, explain:

**Diary:**

Dispute

**Tower Activities**

04-23-13, Tuesday, Clear, 56-78 F, Humidity 45% - Tower Activities



- \* First day started for "Tower Activities" works.
- \* Per Mohammad & Sami, several work activities are in Tower Field:
  - NDT and repair of the tower base shear plate welding
  - Tower fender fabrication & tower footing temporary fender removal
  - Removal of erection tower / favco tower crane
  - Tower painting
  - Tower punch list., etc.
- \* Saw Sami at the CT connex near by area, he was watching removal of the erection tower operation (@ Ele. 112 area). Sami said that no access from elevator to El. 112 area for us, There were around 10 IRWs (Tony's group) working on tower frame removal. Another crew were removing last section of Catwalk at NMS near N60 area - this operation finished on 10:15 AM. Tower crew also removed a big flan frame from tower to deck as well (see pic.). Mohammad was here around 10:00 AM.
- \* After break, Sami took me to the tower base area to see the base shear plate welding & tower footing temporary tower / fender removal operation (from 10:35 AM to 12:25 PM).
- \* After lunch, went to field and saw Sami at deck near tower area. He left around 2:30 PM. I covered inspection from now on to end of work.
- \* Talked to Doug & Lariane about Tony's group personnel for diary purpose. Sami told me, he will take care of labor listing on his diary and if I see workers coming or leaving just can tell him next day.
- \* Forman Tony told us (Doug, Lariane & myself) that ABF will work 10 hours today due to strong wind affecting the swing of big piece cuted frame.
- \* At 5:00 PM, Tony's group stopped removal working & came down from the stair (total 11 workers). Also five piledrivers left job side (fender area) at 5:00 PM.
- \* Need to obtain crew name list from PMIV Sami's diary tomorrow.
- \* Went back office and left around 05:30 PM.
- \* OT 2 hrs today 04-23-13.

**Attachment**

## Daily Diary Report by Bid Item

Job Name: 04-0120F4

Inspector Name: Liu, Tai-Lin

Diary #: 209

Date: 23-Apr-2013


Tuesday




Big flat erection tower frame & last section cable catwalk came down



Erection Tower frame removal @ Ele. 112.

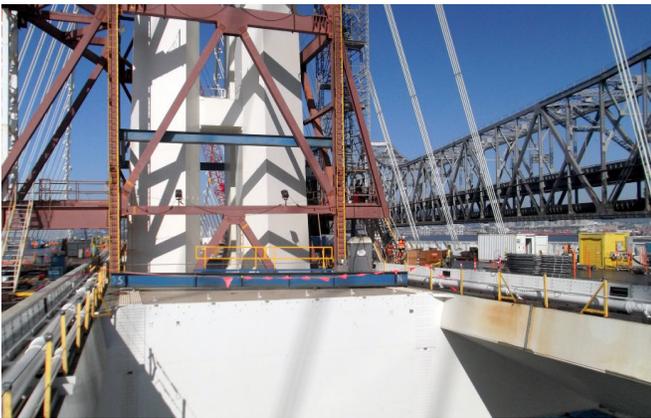

At 5 PM, crew of 11 came down from elevator.

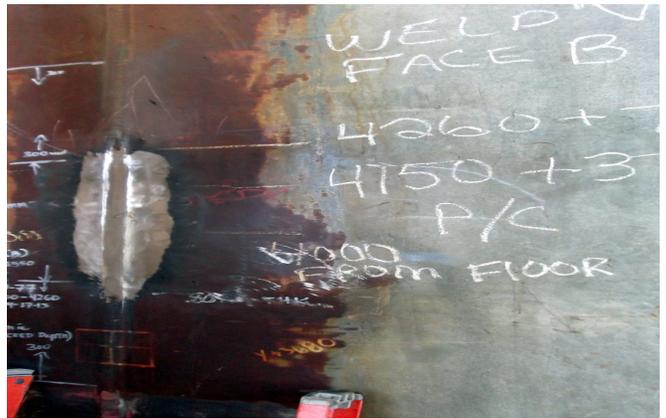

Marking on tower base shear plate repair welding



Tower base shear plate welding repair - QA/QC weld testing



Tower south fender temporary structure removal

---

## Daily Diary Report by Bid Item

Job Name: 04-0120F4


Inspector Name: Liu, Tai-Lin

Diary #: 209

Date: 23-Apr-2013

Tuesday

---

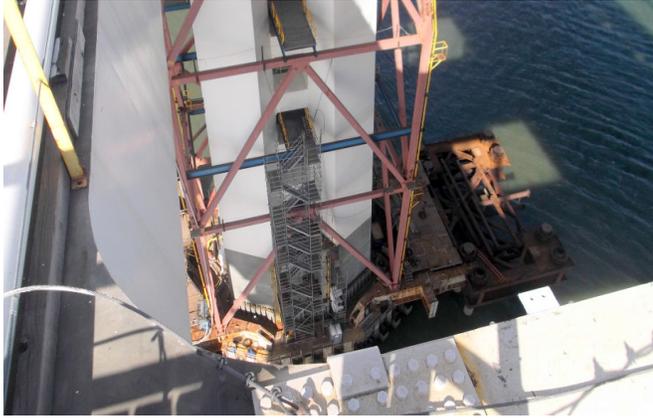

Five pipedriviers worked on temporary fender & structure removal
