



Daily Diary Report by Bid Item

Contract No.: 04-0120F4

Diary #: 130 Const Calendar Day: 508 Date: 25-Oct-2013 Friday
 Inspector Name: Gagnier, Pamela Title: Transportation Engineer
 Inspection Type: Continuous
 Shift Hours: 07:00 AM 05:30 PM Break: Over Time:
 Federal ID:
 Location:
 Reviewer: Jefferson, Paul Approved Date: 23-May-14 Status: Approved

04-0120F4
 04-SF-80-13.2/13.9
 Self-Anchored
 Suspension Bridge

Weather

Temperature 7 AM 12 PM 4PM
 Precipitation Condition

Working Day If no, explain:

Diary:

Dispute

E2 Shear Key Modifications

CCO 328 - HARRIS SALINAS
 E2W East -

Today HS is installing Tendons TL2, TL4, TL6, TL7 and TL8. An issue arised during the installation of TL6 - the lower saddle assembly is lower on the east face compared to the west face. Due to this the profile of TL6 must be adjusted because the tendon conflicts with layer B vertical ducts. After dicussion with Michele DJV it was agreed the TL6 tendon's profile would be lowered by approximately 4" in the middle of the wall to avoid conflict with Layer B ducts. See attached photos.

Today HS installed the #19 angled rebars, vertical #25 between the saddles and # 25 verticals in the saddle rungs.
 Installed the mid layer horizontals. Finished all spirals throughout.
 Installed DL1, DL3 ducts and layer B vertical ducts.

CCO 329 - CONCO

E2W West - Today Conco finished installing form panels and now are installing hardware and whalers.

I worked 2 hours overtime to cover field activities.

CCO-328 Bid Item: 001 0-BRS-ELS.328 Pier E2 Bar Reinforcing Steel

HARRIS SALINAS REBAR

Labor

Trade	Class	Name	RT Hrs	OT Hrs	DT Hrs	Total	Remarks	Dispute
Contractor: HARRIS SALINAS REBAR								
Ironworker	JNM	ALFREDO CORPUS	8.00	2.00	0.00	10.00		<input type="checkbox"/>
Ironworker	JNM	VILLASENOR GUELLERMO	8.00	2.00	0.00	10.00		<input type="checkbox"/>
Ironworker	JNM	ZAVALA ALONZO	8.00	2.00	0.00	10.00		<input type="checkbox"/>
Ironworker	JNM	WALTER GODOY	0.00	0.00	0.00	0.00		<input type="checkbox"/>
Ironworker	JNM	DOUG WALLACH	0.00	0.00	0.00	0.00		<input type="checkbox"/>
Ironworker	JNM	JUAN ROBLES	0.00	0.00	0.00	0.00		<input type="checkbox"/>
Ironworker	JNM	DANIAL MONTES	8.00	2.00	0.00	10.00		<input type="checkbox"/>
Ironworker	JNM	JAIME MONTES	0.00	0.00	0.00	0.00		<input type="checkbox"/>
Ironworker	JNM	DANIAL GUDINO	8.00	2.00	0.00	10.00		<input type="checkbox"/>
Ironworker	JNM	HECTOR LEON	8.00	2.00	0.00	10.00		<input type="checkbox"/>
Ironworker	FOR	SIMON MARTINEZ	8.00	2.00	1.00	11.00		<input type="checkbox"/>

Daily Diary Report by Bid Item

Job Name: 04-0120F4 Inspector Name: Gagnier, Pamela Diary #: 130 Date: 25-Oct-2013 Friday

CCO-329 Bid Item: 001 0-PCC-ELS.329 Pier E2 Place Concrete

CONCO PUMPING

Labor

Trade	Class	Name	RT Hrs	OT Hrs	DT Hrs	Total	Remarks	Dispute
Contractor: CONCO PUMPING								
Semi-Skilled Laborer	JNM	ARTURO SEGURA	8.00	0.00	0.00	8.00		<input type="checkbox"/>
Semi-Skilled Laborer	FOR	WENDELL STEPHENS	8.00	0.00	0.00	8.00		<input type="checkbox"/>
Carpenter	JNM	PEDRO BARRON	8.00	0.00	0.00	8.00		<input type="checkbox"/>
Carpenter	JNM	MIKE ABARRA	8.00	0.00	0.00	8.00		<input type="checkbox"/>
Carpenter	JNM	SALVADOR MARROQUIN	8.00	0.00	0.00	8.00		<input type="checkbox"/>
Carpenter	JNM	ABRAHAM RUELAS	8.00	0.00	0.00	8.00		<input type="checkbox"/>
Carpenter	FOR	JAMES CROTTY	8.00	0.00	0.00	8.00		<input type="checkbox"/>
Carpenter	GEN	MARK WOZNICKI	8.00	0.00	0.00	8.00		<input type="checkbox"/>
Carpenter	JNM	RALPH GOMEZ	8.00	0.00	0.00	8.00		<input type="checkbox"/>

Attachment



E2W East - Conflict B/W TL6 & Vertical Layer B after Adjustment



E2W East - Conflict B/W TL6 & Vertical Layer B after Adjustment - Elevation View



E2W East - Conflict B/W TL6 & Vertical Layer B after Adjustment - Elevation View



E2W East - Conflict B/W TL6 & Vertical Layer B after Adjustment - Elevation View

Daily Diary Report by Bid Item


Job Name: 04-0120F4

Inspector Name: Gagnier, Pamela

Diary #: 130

Date: 25-Oct-2013

Friday

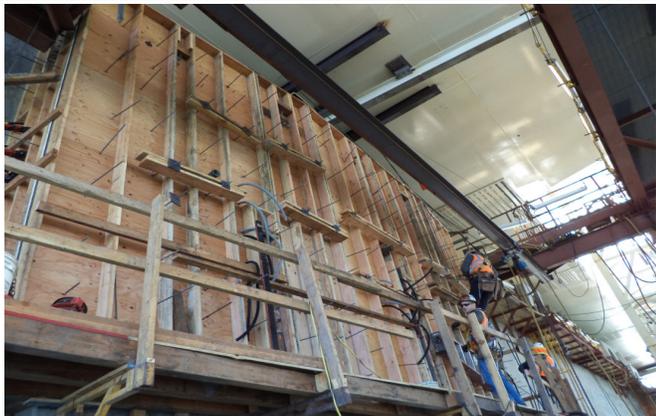

E2W West - Conco Finished Panels Working on Hardware & Whalers



E2W East - Conflict B/W TL6 & Vertical Layer B before Adjustment
