



**Daily Diary Report by Bid Item**

Contract No.: 04-0120F4

Diary #: 314 Const Calendar Day: 750 Date: 24-Jun-2014 Tuesday  
 Inspector Name: Liu, Tai-Lin Title: Transportation Engineer  
 Inspection Type: Continuous  
 Shift Hours: 07:00 AM 03:30 PM Break: 00:30 Over Time:  
 Federal ID:  
 Location:  
 Reviewer: Awal, Mohammad Approved Date: 17-Aug-14 Status: Approved

04-0120F4  
 04-SF-80-13.2/13.9  
 Self-Anchored  
 Suspension Bridge

**Weather**

Temperature 7 AM 60 - 70 12 PM 70 - 80 4PM 70 - 80  
 Precipitation Condition Clear

Working Day  If no, explain:

**Diary:**

Dispute

**Tower Activites**

\* Went to T1 - Tower Base Area by boat around 9:45 AM, saw Tony (CCC), Joe (METS), Jin (CCC) and ABF paint inspector Ray Shutley as well.

\* There was still no Tower (beyond 53 m) cleaning / painting work due to accident happended on the ladder.

Six ABF's labors: Rogelio Rodriguez, Aurelio Rodriguez (not in PMIV system), Guillermo Limon (Labor Forman), Javier Medina, Danny Schwartz, Luis jimenez and James Sturgeon (ABF's Forman) were in tower (below 53 m) performed cleaning, caulking (area missed from China) and installed safety features today. Tower base caulk sealing also started at the base per RFI-0366R0.

\* Talked to Joe (METS) about the tower base work status, he told me that:  
 - Paint (two coatings) on west side of tower skirt (exterior) has been done, containment & scaffolding ready to remove. Crew performed cleaning & tuch - up the area they missed.  
 - Two panters continued repairing damaged paint on the east side of opering (see pictures)

Paint Crew: Billy Gatewood, Joege Fiones, Mark Sterward, Recavdo Pasalla (paint forman), Marco Ornuo, Javier Alvag, Edilberto Leon, & Tony Katrones (Superintendent).

\* There was a small fire on Demo project next to Tower area (see Picture).

\* Back to office, performed paper work including RFI/Submittal PMIV works until 3:40 PM.

04-0120F4 Bid Item: 053 T-L01-DSE.053 Tower Lift 01 Diaphram Tower SE Erect structural steel (bridge tower)  
 AMERICAN BRIDGE/FLUOR, A JV

**Labor**

Trade	Class	Name	RT Hrs	OT Hrs	DT Hrs	Total	Remarks	Dispute
Contractor: AMERICAN BRIDGE/FLUOR, A JV								
Semi-Skilled Laborer	JNM	FERMIN MEDINA	0.00	0.00	0.00	0.00		<input type="checkbox"/>
Ironworker	GEN	AARON KENT	0.00	0.00	0.00	0.00		<input type="checkbox"/>
Semi-Skilled Laborer	JNM	LUIS Jimenez	8.00	0.00	0.00	8.00		<input type="checkbox"/>
Semi-Skilled Laborer	JNM	DANNY SCHWARTZ	8.00	0.00	0.00	8.00		<input type="checkbox"/>
Semi-Skilled Laborer	APP	JAVIER MEDINA	8.00	0.00	0.00	8.00		<input type="checkbox"/>
Semi-Skilled Laborer	FOR	GUILLERMO LIMON	8.00	0.00	0.00	8.00		<input type="checkbox"/>

## Daily Diary Report by Bid Item

**Job Name:** 04-0120F4    **Inspector Name:** Liu, Tai-Lin    **Diary #:** 314    **Date:** 24-Jun-2014    **Tuesday**

Semi-Skilled Laborer	APP	ROGELIO RODRIGUEZ	8.00	0.00	0.00	8.00	<input type="checkbox"/>
Semi-Skilled Laborer	JNM	CARLOS MONTEJANO	0.00	0.00	0.00	0.00	<input type="checkbox"/>
Semi-Skilled Laborer	APP	JOSE AVILA	0.00	0.00	0.00	0.00	<input type="checkbox"/>
Semi-Skilled Laborer	JNM	VICTOR HERNANDEZ	0.00	0.00	0.00	0.00	<input type="checkbox"/>
Ironworker	FOR	JAMES STURGEON	8.00	0.00	0.00	8.00	<input type="checkbox"/>
<b>Equipment</b>			<b>Rental Company</b>				
<b>Equipment ID</b>	<b>Description</b>		<b>RT Hrs</b>	<b>OT Hrs</b>	<b>ST Hrs</b>	<b>IT Hrs</b>	<b>Dispute</b>
<b>Contractor:</b> AMERICAN BRIDGE/FLUOR, A JV							
*E0020562	WELDING EQUIPMENT					No	<input type="checkbox"/>
			0.00	0.00	0.00	0.00	<input type="checkbox"/>
*E0030562	WELDING EQUIPMENT					No	<input type="checkbox"/>
			0.00	0.00	0.00	0.00	<input type="checkbox"/>
*E0010562	WELDING EQUIPMENT					No	<input type="checkbox"/>
			0.00	0.00	0.00	0.00	<input type="checkbox"/>
2292	WELDER, 600 AMP					No	<input type="checkbox"/>
			0.00	0.00	0.00	0.00	<input type="checkbox"/>
2293	WELDER, 600 AMP					No	<input type="checkbox"/>
			0.00	0.00	0.00	0.00	<input type="checkbox"/>
<b>04-0120F4</b>	<b>Bid Item: 078</b>	<b>T-L01-ENE.078</b>	<b>Tower Lift 01 External Paint Tower NE</b>				
CERTIFIED COATINGS COMPANY							
<b>04-0120F4</b>	<b>Bid Item: 078</b>	<b>T-L05-ENE.078</b>	<b>Tower Lift 05 External Paint Tower NE</b>				
CERTIFIED COATINGS COMPANY							
<b>04-0120F4</b>	<b>Bid Item: 078</b>	<b>T-HEA-ENE.078</b>	<b>Tower Head External Paint Tower NE</b>				
CERTIFIED COATINGS COMPANY							
<b>CCO-355</b>	<b>Bid Item: 001</b>	<b>0-CIC-EFA.355</b>	<b>CIC - Elevator Impacts - USA Hoist</b>				
AMERICAN BRIDGE/FLUOR, A JV							

**Attachment**



## Daily Diary Report by Bid Item

Job Name: 04-0120F4

Inspector Name: Liu, Tai-Lin

Diary #: 314

Date: 24-Jun-2014

Tuesday



CCC superentant Tony was measuring temperature at tower panel



CCC performed second coating spray on West side of tower base



CCC painter mixed the paint for West Side of Tower paint spray



CCC completed second paint coating spray on West side of tower



CCC painters were fixing paint damaged area at East Side of opening area



CCC performed second paint coating spray

## Daily Diary Report by Bid Item

Job Name: 04-0120F4

Inspector Name: Liu, Tai-Lin


Diary #: 314

Date: 24-Jun-2014

Tuesday



There was a small fire on the Demo project next to tower area

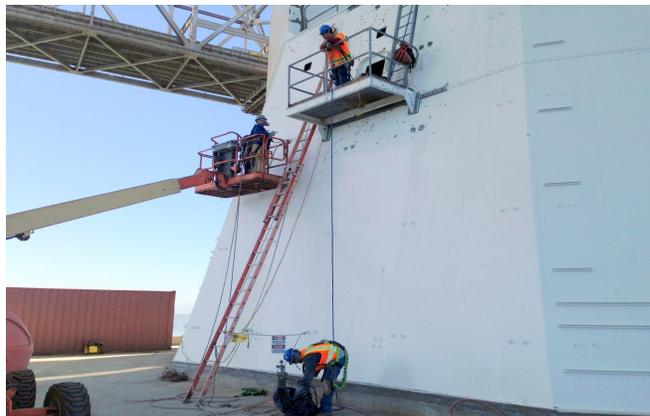

CCC personnel (2) performed paint repair by hand in east side of opening with ABF's labores working inside the tower
