



Daily Diary Report by Bid Item

Contract No.: 04-0120F4

Diary #: 317 Const Calendar Day: 757 Date: 01-Jul-2014 Tuesday
 Inspector Name: Liu, Tai-Lin Title: Transportation Engineer
 Inspection Type: Continuous
 Shift Hours: 07:00 AM 03:30 PM Break: 00:30 Over Time:

04-0120F4
 04-SF-80-13.2/13.9
 Self-Anchored
 Suspension Bridge

Federal ID:

Location:

Reviewer: Awal, Mohammad Approved Date: 17-Aug-14 Status: Approved

Weather

Temperature 7 AM 60 - 70 12 PM 70 - 80 4PM 70 - 80
 Precipitation Condition Clear

Working Day If no, explain:

Diary:

Dispute

Tower Activites

Tower Base Works:

* CCC painting works (See pictures #P1-P6):

- CCC completed exterior skirt paint works at west side, containment & scaffolding were removed and loaded to barge and left from T1.
- CCC performed primer application at bottom of skirt after ABF labores completed the grout chipping & patching.
- CCC started touch-up works inside the tower skirt by the METS inspector Joe's direction. Total 5 persons worked 8 hours today.

Paint Crew: Billy Gatewood, Recavdo Pasalla (paint forman), Javier Alvag, Edilberto Leon & Tony Katrones (Superintendent).

* ABF crew performed bottom skirt grout chipping & patching work & cleaning inside tower shaft between 13m to 53 m area. Saw Donald & Paul at field at elevator - tower north side (see pictures #M1-M3 & #CL1).

ABF's crew: Rogelio Rodriguez, Aurelio Rodriguez (not in PMIV system), Guillermo Limon (Labor Forman), Javier Medina, Danny Schwartz.

* Tower base plate caulking works (see pictures #C1 - C8)

- Went down to Tower base to check caulk sealing between base plates (Cell #5) with METS inspector Joe (see pictures for detail).

04-0120F4	Bid Item: 053	T-L01-DSE.053	Tower Lift 01 Diaphram Tower SE Erect structural steel (bridge tower)
AMERICAN BRIDGE/FLUOR, A JV			

Labor							Dispute	
Trade	Class	Name	RT Hrs	OT Hrs	DT Hrs	Total	Remarks	Dispute
Contractor: AMERICAN BRIDGE/FLUOR, A JV								
Ironworker	JNM	DONALD PLUMB	8.00	0.00	0.00	8.00		<input type="checkbox"/>
Ironworker	JNM	PAUL FAMBRINI	8.00	0.00	0.00	8.00		<input type="checkbox"/>
Semi-Skilled Laborer	JNM	FERMIN MEDINA	0.00	0.00	0.00	0.00		<input type="checkbox"/>
Ironworker	GEN	AARON KENT	0.00	0.00	0.00	0.00		<input type="checkbox"/>
Semi-Skilled Laborer	JNM	LUIS Jimenez	0.00	0.00	0.00	0.00		<input type="checkbox"/>

Daily Diary Report by Bid Item

Job Name: 04-0120F4 **Inspector Name:** Liu, Tai-Lin **Diary #:** 317 **Date:** 01-Jul-2014 **Tuesday**

Semi-Skilled Laborer	JNM	DANNY SCHWARTZ	8.00	0.00	0.00	8.00	<input type="checkbox"/>
Semi-Skilled Laborer	APP	JAVIER MEDINA	8.00	0.00	0.00	8.00	<input type="checkbox"/>
Semi-Skilled Laborer	FOR	GUILLERMO LIMON	8.00	0.00	0.00	8.00	<input type="checkbox"/>
Semi-Skilled Laborer	APP	ROGELIO RODRIGUEZ	8.00	0.00	0.00	8.00	<input type="checkbox"/>
Semi-Skilled Laborer	JNM	CARLOS MONTEJANO	0.00	0.00	0.00	0.00	<input type="checkbox"/>
Semi-Skilled Laborer	APP	JOSE AVILA	0.00	0.00	0.00	0.00	<input type="checkbox"/>
Semi-Skilled Laborer	JNM	VICTOR HERNANDEZ	0.00	0.00	0.00	0.00	<input type="checkbox"/>
Ironworker	FOR	JAMES STURGEON	0.00	0.00	0.00	0.00	<input type="checkbox"/>

Equipment		Rental Company				Dispute	
Equipment ID	Description	RT Hrs	OT Hrs	ST Hrs	IT Hrs	Remarks	Dispute
Contractor: AMERICAN BRIDGE/FLUOR, A JV							
*E0020562	WELDING EQUIPMENT					No	<input type="checkbox"/>
		0.00	0.00	0.00	0.00		
*E0030562	WELDING EQUIPMENT					No	<input type="checkbox"/>
		0.00	0.00	0.00	0.00		
*E0010562	WELDING EQUIPMENT					No	<input type="checkbox"/>
		0.00	0.00	0.00	0.00		
2292	WELDER, 600 AMP					No	<input type="checkbox"/>
		0.00	0.00	0.00	0.00		
2293	WELDER, 600 AMP					No	<input type="checkbox"/>
		0.00	0.00	0.00	0.00		

04-0120F4 Bid Item: 078 T-L01-ENE.078 Tower Lift 01 External Paint Tower NE
 CERTIFIED COATINGS COMPANY

04-0120F4 Bid Item: 078 T-L05-ENE.078 Tower Lift 05 External Paint Tower NE
 CERTIFIED COATINGS COMPANY

04-0120F4 Bid Item: 078 T-HEA-ENE.078 Tower Head External Paint Tower NE
 CERTIFIED COATINGS COMPANY

CCO-355 Bid Item: 001 0-CIC-EFA.355 CIC - Elevator Impacts - USA Hoist
 AMERICAN BRIDGE/FLUOR, A JV

Attachment

Daily Diary Report by Bid Item

Job Name: 04-0120F4

Inspector Name: Liu, Tai-Lin

Diary #: 317

Date: 01-Jul-2014

Tuesday



#C3: Culking between vertical plates at south of inside tower base



#C7: Tower base plate caulking at cell # 6



#P4: CCC performed paint touch-up inside the tower base directing by METS Joe



#C2: Tower base plate culking at cell #6 area



#M2: New barge moved in to T1, old barge with all equipment & loaded junk were left from T1



#P2: METS paint inspector Joe was checking the mouse hole paint along the culking line

Daily Diary Report by Bid Item

Job Name: 04-0120F4

Inspector Name: Liu, Tai-Lin


Diary #: 317

Date: 01-Jul-2014

Tuesday



#C5: Culking between tower base plates at north side of tower base

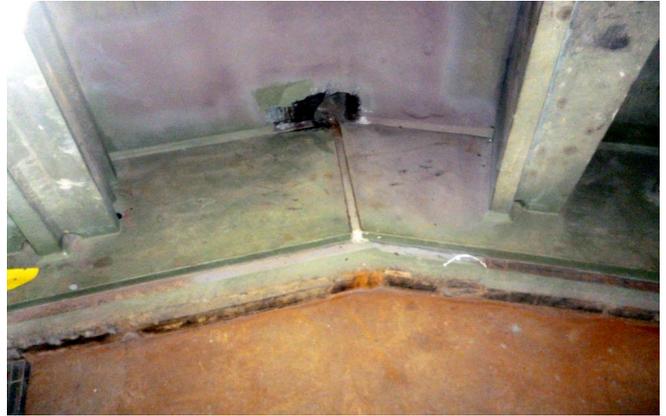

#C4: Culking between tower base plates at east side of tower base



#P3: METS Joe used reflected mirror to check the paint at mouse hole



#C1: Base plate caulking at cell # 6 area



#P5: METS Joe showed the CCC painter where need paint touch up



#C6: Tower base plate caulking

Daily Diary Report by Bid Item

Job Name: 04-0120F4

Inspector Name: Liu, Tai-Lin

Diary #: 317

Date: 01-Jul-2014

Tuesday



#CL1: ABF cleaning group at El; 13 area performing cleaning work



#C8: Tower base plate culking at cell 4 area inside of tower base



#P6: Completed paint at West side of tower & 5 ABF's labores complete grout chipping & patching at bottom of skirt



#M3: Two IRWs - Donald & Paul worked in elevator area at north side of tower



#M1: Installed water pipe connecting to inside bottom pump at north side of tower



#P1: CCC painter performed paint repair at bottom of tower base
