



Daily Diary Report by Bid Item

Contract No.: 04-0120F4

Diary #: 319 Const Calendar Day: 763 Date: 07-Jul-2014 Monday
 Inspector Name: Liu, Tai-Lin Title: Transportation Engineer
 Inspection Type: Continuous
 Shift Hours: 07:00 AM 03:30 PM Break: 00:30 Over Time:
 Federal ID:
 Location:
 Reviewer: Awal, Mohammad Approved Date: 17-Aug-14 Status: Approved

04-0120F4
 04-SF-80-13.2/13.9
 Self-Anchored
 Suspension Bridge

Weather

Temperature 7 AM 60 - 70 12 PM 70 - 80 4PM 70 - 80
 Precipitation Condition Clear

Working Day If no, explain:

Diary:

Dispute

Tower Activites

Tower Base Works:

* CCC painting works:

- Talked to METS Joe and CCC Tony to obtain the work status.
- Total 5 CCC painters worked today including Superintendent Tony.
- CCC crew worked in interior skirt and inside bottom tower base area performing touch-up works and checked by METS paint inspector Joe.
- Joe pointed out several locations need to be repaired: A few spot area at interior of skirt, tower anchor bolt down areas, inside mouse holes at tower base plate area, and exterior skirt underneath strip area.
- Joe also pointed out that the tower pipe outlet area - for black pipe connecting to water pump inside to outside tower (see picture - at north and south faces two locations) need caulking to seal the gaps.
- CCC Tony and Joege performed touch-up at opening area in east side of tower (see picture).

Paint Crew: Billy Gatewood, Joege Flones, Javier Alvag, Edilberto Leon & Tony Katrones (Superintendent).

* Did not see ABF cleaning crew at tower base area, might be working cleaning work inside the tower shafts between 13m to 53 m area. saw ABF's labores working on exterior cleaning work about 53 meter area at the time I were there (see pictures).

ABF's crew: Rogelio Rodriguez, Aurelio Rodriguez (not in PMIV system), Guillermo Limon (Labor Forman), Javier Medina, Danny Schwartz.

* Performed paper work including RFI/Submittal PMIV works at the office, I left office around 03:40 PM.

04-0120F4 Bid Item: 053 T-L01-DSE.053 Tower Lift 01 Diaphram Tower SE Erect structural steel (bridge tower)
 AMERICAN BRIDGE/FLUOR, A JV

Labor

| Trade | Class | Name | RT Hrs | OT Hrs | DT Hrs | Total | Remarks | Dispute |
|-----------------------------------------|-------|---------------|--------|--------|--------|-------|---------|--------------------------|
| Contractor: AMERICAN BRIDGE/FLUOR, A JV | | | | | | | | |
| Ironworker | JNM | DONALD PLUMB | 0.00 | 0.00 | 0.00 | 0.00 | | <input type="checkbox"/> |
| Ironworker | JNM | PAUL FAMBRINI | 0.00 | 0.00 | 0.00 | 0.00 | | <input type="checkbox"/> |
| Semi-Skilled Laborer | JNM | FERMIN MEDINA | 0.00 | 0.00 | 0.00 | 0.00 | | <input type="checkbox"/> |
| Ironworker | GEN | AARON KENT | 0.00 | 0.00 | 0.00 | 0.00 | | <input type="checkbox"/> |
| Semi-Skilled Laborer | JNM | LUIS Jimenez | 0.00 | 0.00 | 0.00 | 0.00 | | <input type="checkbox"/> |

Daily Diary Report by Bid Item

Job Name: 04-0120F4 **Inspector Name:** Liu, Tai-Lin **Diary #:** 319 **Date:** 07-Jul-2014 **Monday**

| | | | | | | | |
|----------------------|-----|-------------------|------|------|------|------|--------------------------|
| Semi-Skilled Laborer | JNM | DANNY SCHWARTZ | 8.00 | 0.00 | 0.00 | 8.00 | <input type="checkbox"/> |
| Semi-Skilled Laborer | APP | JAVIER MEDINA | 8.00 | 0.00 | 0.00 | 8.00 | <input type="checkbox"/> |
| Semi-Skilled Laborer | FOR | GUILLERMO LIMON | 8.00 | 0.00 | 0.00 | 8.00 | <input type="checkbox"/> |
| Semi-Skilled Laborer | APP | ROGELIO RODRIGUEZ | 8.00 | 0.00 | 0.00 | 8.00 | <input type="checkbox"/> |
| Semi-Skilled Laborer | JNM | CARLOS MONTEJANO | 0.00 | 0.00 | 0.00 | 0.00 | <input type="checkbox"/> |
| Semi-Skilled Laborer | APP | JOSE AVILA | 0.00 | 0.00 | 0.00 | 0.00 | <input type="checkbox"/> |
| Semi-Skilled Laborer | JNM | VICTOR HERNANDEZ | 0.00 | 0.00 | 0.00 | 0.00 | <input type="checkbox"/> |
| Ironworker | FOR | JAMES STURGEON | 0.00 | 0.00 | 0.00 | 0.00 | <input type="checkbox"/> |

| Equipment | | | | | | Rental Company | |
|------------------------------------------------|-------------------|--------|--------|--------|--------|----------------|--------------------------|
| Equipment ID | Description | RT Hrs | OT Hrs | ST Hrs | IT Hrs | Remarks | Dispute |
| Contractor: AMERICAN BRIDGE/FLUOR, A JV | | | | | | | |
| *E0020562 | WELDING EQUIPMENT | | | | | No | <input type="checkbox"/> |
| | | 0.00 | 0.00 | 0.00 | 0.00 | | |
| *E0030562 | WELDING EQUIPMENT | | | | | No | <input type="checkbox"/> |
| | | 0.00 | 0.00 | 0.00 | 0.00 | | |
| *E0010562 | WELDING EQUIPMENT | | | | | No | <input type="checkbox"/> |
| | | 0.00 | 0.00 | 0.00 | 0.00 | | |
| 2292 | WELDER, 600 AMP | | | | | No | <input type="checkbox"/> |
| | | 0.00 | 0.00 | 0.00 | 0.00 | | |
| 2293 | WELDER, 600 AMP | | | | | No | <input type="checkbox"/> |
| | | 0.00 | 0.00 | 0.00 | 0.00 | | |

04-0120F4 Bid Item: 078 T-L01-ENE.078 Tower Lift 01 External Paint Tower NE
 CERTIFIED COATINGS COMPANY

04-0120F4 Bid Item: 078 T-L05-ENE.078 Tower Lift 05 External Paint Tower NE
 CERTIFIED COATINGS COMPANY

04-0120F4 Bid Item: 078 T-HEA-ENE.078 Tower Head External Paint Tower NE
 CERTIFIED COATINGS COMPANY

CCO-355 Bid Item: 001 0-CIC-EFA.355 CIC - Elevator Impacts - USA Hoist
 AMERICAN BRIDGE/FLUOR, A JV

Attachment



Daily Diary Report by Bid Item

Job Name: 04-0120F4

Inspector Name: Liu, Tai-Lin

Diary #: 319

Date: 07-Jul-2014

Monday



Joe pointed out that CCC need repair the paint underneath the bottom strip



METS painter Joe get ready to get in the tower base area to check CCC's works



Saw crew worked on 53 meter exterior of tower shaft area



Need to be caulked at the outlet area that pipe run out from inside the tower



Tower base concrete crack need to be repaired later



ABF's crew worked on external tower shaft cleaning work

Daily Diary Report by Bid Item

Job Name: 04-0120F4

Inspector Name: Liu, Tai-Lin


Diary #: 319

Date: 07-Jul-2014

Monday



CCC Billy at south tower entrance to check personnel in and out the tower base area

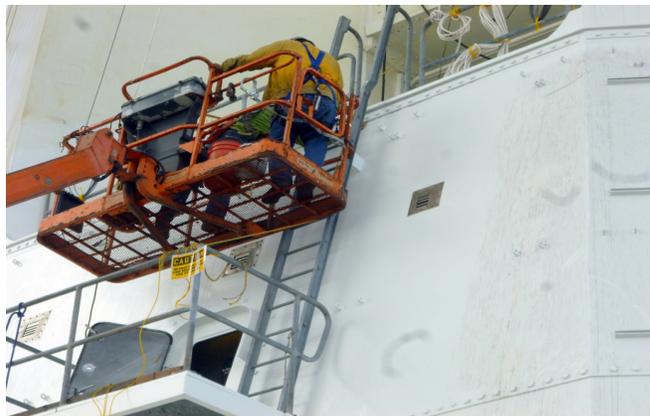

CCC Tony & Jorge performed touch-up repair paint at east opening area
