



Daily Diary Report by Bid Item

Contract No.: 04-0120F4

Diary #: 320 Const Calendar Day: 764 Date: 08-Jul-2014 Tuesday
 Inspector Name: Liu, Tai-Lin Title: Transportation Engineer
 Inspection Type: Continuous
 Shift Hours: 07:00 AM 03:30 PM Break: 00:30 Over Time:
 Federal ID:
 Location:
 Reviewer: Awal, Mohammad Approved Date: 17-Aug-14 Status: Approved

04-0120F4
 04-SF-80-13.2/13.9
 Self-Anchored
 Suspension Bridge

Weather

Temperature 7 AM 60 - 70 12 PM 70 - 80 4PM 70 - 80
 Precipitation Condition Clear

Working Day If no, explain:

Diary:

Dispute

Tower Activites

Tower Base Works:

* CCC painting works:

- Talked to METS Joe and CCC Tony to obtain the work status.
 - Total 5 CCC painters worked today including Superintendent Tony.
 - CCC crew stopped working in interoir skirt and inside bottom tower base area today.
- Four painter performing area preparation at tower elevation 18 m South-west & north-west inside the shafts area, and checked by METS paint inspector Joe.
- Joe told me that the tower base touch-up works almost finished, CCC started preparation works in the area between elevation 13 to 53 meters. Today CCC will work insidfe the north-west and south-west shaft area.

Paint Crew: Billy Gatewood, Joege Flones, Javier Alvag, Edilberto Leon & Tony Katrones (Superintendent).

* Did not see ABF cleaning crew at tower base area, might be working cleaning work inside the tower shafts between 13m to 53 m area.

ABF's crew: Rogelio Rodriguez, Aurelio Rodriguez (not in PMIV system), Guillermo Limon (Labor Forman), Javier Medina, Danny Schwartz.

* Performed paper work including RFI/Submittal PMIV works at the office, finnalized 5 letters today and sent to Shally for log in to the system. Left office around 03:40 PM.

04-0120F4 Bid Item: 053 T-L01-DSE.053 Tower Lift 01 Diaphram Tower SE Erect structural steel (bridge tower)
 AMERICAN BRIDGE/FLUOR, A JV

Labor

Trade	Class	Name	RT Hrs	OT Hrs	DT Hrs	Total	Remarks	Dispute
Contractor: AMERICAN BRIDGE/FLUOR, A JV								
Ironworker	JNM	DONALD PLUMB	0.00	0.00	0.00	0.00		<input type="checkbox"/>
Ironworker	JNM	PAUL FAMBRINI	0.00	0.00	0.00	0.00		<input type="checkbox"/>
Semi-Skilled Laborer	JNM	FERMIN MEDINA	0.00	0.00	0.00	0.00		<input type="checkbox"/>
Ironworker	GEN	AARON KENT	0.00	0.00	0.00	0.00		<input type="checkbox"/>
Semi-Skilled Laborer	JNM	LUIS Jimenez	0.00	0.00	0.00	0.00		<input type="checkbox"/>
Semi-Skilled Laborer	JNM	DANNY SCHWARTZ	8.00	0.00	0.00	8.00		<input type="checkbox"/>

Daily Diary Report by Bid Item

Job Name: 04-0120F4 **Inspector Name:** Liu, Tai-Lin **Diary #:** 320 **Date:** 08-Jul-2014 **Tuesday**

Semi-Skilled Laborer	APP	JAVIER MEDINA	8.00	0.00	0.00	8.00		<input type="checkbox"/>
Semi-Skilled Laborer	FOR	GUILLERMO LIMON	8.00	0.00	0.00	8.00		<input type="checkbox"/>
Semi-Skilled Laborer	APP	ROGELIO RODRIGUEZ	8.00	0.00	0.00	8.00		<input type="checkbox"/>
Semi-Skilled Laborer	JNM	CARLOS MONTEJANO	0.00	0.00	0.00	0.00		<input type="checkbox"/>
Semi-Skilled Laborer	APP	JOSE AVILA	0.00	0.00	0.00	0.00		<input type="checkbox"/>
Semi-Skilled Laborer	JNM	VICTOR HERNANDEZ	0.00	0.00	0.00	0.00		<input type="checkbox"/>
Ironworker	FOR	JAMES STURGEON	0.00	0.00	0.00	0.00		<input type="checkbox"/>
Equipment							Rental Company	
Equipment ID	Description		RT Hrs	OT Hrs	ST Hrs	IT Hrs	Remarks	Dispute
Contractor: AMERICAN BRIDGE/FLUOR, A JV								
*E0020562	WELDING EQUIPMENT						No	<input type="checkbox"/>
			0.00	0.00	0.00	0.00		<input type="checkbox"/>
*E0030562	WELDING EQUIPMENT						No	<input type="checkbox"/>
			0.00	0.00	0.00	0.00		<input type="checkbox"/>
*E0010562	WELDING EQUIPMENT						No	<input type="checkbox"/>
			0.00	0.00	0.00	0.00		<input type="checkbox"/>
2292	WELDER, 600 AMP						No	<input type="checkbox"/>
			0.00	0.00	0.00	0.00		<input type="checkbox"/>
2293	WELDER, 600 AMP						No	<input type="checkbox"/>
			0.00	0.00	0.00	0.00		<input type="checkbox"/>
04-0120F4	Bid Item: 078	T-L01-ENE.078	Tower Lift 01 External Paint Tower NE					
CERTIFIED COATINGS COMPANY								
04-0120F4	Bid Item: 078	T-L05-ENE.078	Tower Lift 05 External Paint Tower NE					
CERTIFIED COATINGS COMPANY								
04-0120F4	Bid Item: 078	T-HEA-ENE.078	Tower Head External Paint Tower NE					
CERTIFIED COATINGS COMPANY								
CCO-355	Bid Item: 001	0-CIC-EFA.355	CIC - Elevator Impacts - USA Hoist					
AMERICAN BRIDGE/FLUOR, A JV								

Attachment



Daily Diary Report by Bid Item

Job Name: 04-0120F4

Inspector Name: Liu, Tai-Lin

Diary #: 320

Date: 08-Jul-2014


Tuesday



METS paint inspector Joe checked painter's work inside the shaft



Javier performed area preparation inside the shaft at El.18m

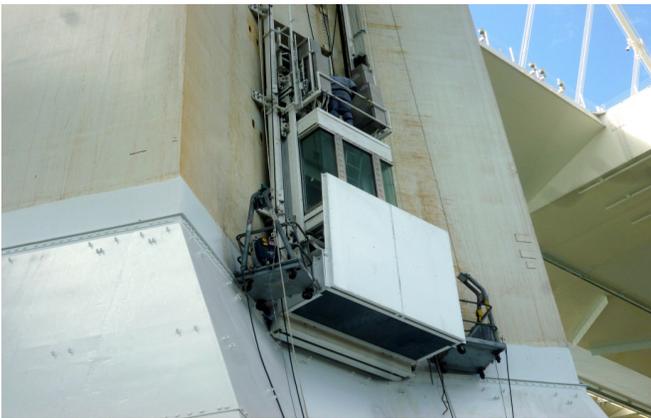

Elevator work at north side of tower



Saw 5 workers worked on elevator & Mound was inspecting the works



CCC painter Javier performed area preparation at south-west shaft elevation 18 meter



Joege performed cleaning area at the same elevation area
