



Daily Diary Report by Bid Item

Contract No.: 04-0120F4

Diary #: 326 Const Calendar Day: 772 Date: 16-Jul-2014 Wednesday

Inspector Name: Liu, Tai-Lin Title: Transportation Engineer

Inspection Type: Continuous

Shift Hours: 07:00 AM 03:30 PM Break: 00:30 Over Time:

Federal ID:

Location:

Reviewer: Awal, Mohammad Approved Date: 17-Aug-14 Status: Approved

04-0120F4
 04-SF-80-13.2/13.9
 Self-Anchored
 Suspension Bridge

Weather

Temperature 7 AM 60 - 70 12 PM 70 - 80 4PM 70 - 80

Precipitation Condition Clear

Working Day If no, explain:

Diary:

Dispute

Tower Activites

Tower Base Works (7/16/14, Wednesday - Clear):

* CCC painting works:

- CCC crew (7) continued performing prep & painting work on tower facad area between elevation 23 meter to 33 meter area.

- Met Forman Recado at pier, he told me that they finished façade painting on El. 23 will continue to higher elevation same as prep work, also mentioned that the painter Edllberto came back for work at field today.

Paint Crew: Billy Gatewood, Joege Flones, Javier Alvag, Recardo Pasalla, Manuel Ramirer, Marco Ornuo, Edllberto Leon & Eric Garza.

* Saw ABF cleaning crew at tower around 33 meter exterior of shaft (See pictures) - Refer to Laraine's diary for detail.

ABF's crew: Rogelio Rodriguez, Aurelio Rodriguez (not in PMIV system), Guillermo Limon (Labor Forman), Javier Medina, Danny Schwartz.

* Saw one ABF labor performed caulking on drainage outlet pipes on south/north of tower (see picture).

* Saw 3 electricians worked on elevator area.

* Crane operator Neil Caldwell & helper Justin at barge stand by for any lifting work needed.

* Performed paper work including RFI/Submittal PMIV works at the office. Left office around 03:40 PM.

04-0120F4 Bid Item: 053 T-L01-DSE.053 Tower Lift 01 Diaphram Tower SE Erect structural steel (bridge tower)
 AMERICAN BRIDGE/FLUOR, A JV

Labor								Dispute
Trade	Class	Name	RT Hrs	OT Hrs	DT Hrs	Total	Remarks	
Contractor: AMERICAN BRIDGE/FLUOR, A JV								
Ironworker	JNM	DONALD PLUMB	0.00	0.00	0.00	0.00		<input type="checkbox"/>
Ironworker	JNM	PAUL FAMBRINI	0.00	0.00	0.00	0.00		<input type="checkbox"/>
Semi-Skilled Laborer	JNM	FERMIN MEDINA	0.00	0.00	0.00	0.00		<input type="checkbox"/>
Ironworker	GEN	AARON KENT	0.00	0.00	0.00	0.00		<input type="checkbox"/>

Daily Diary Report by Bid Item

Job Name: 04-0120F4 **Inspector Name:** Liu, Tai-Lin **Diary #:** 326 **Date:** 16-Jul-2014 **Wednesday**

Semi-Skilled Laborer	JNM	LUIS Jimenez	0.00	0.00	0.00	0.00		<input type="checkbox"/>
Semi-Skilled Laborer	JNM	DANNY SCHWARTZ	8.00	0.00	0.00	8.00		<input type="checkbox"/>
Semi-Skilled Laborer	APP	JAVIER MEDINA	8.00	0.00	0.00	8.00		<input type="checkbox"/>
Semi-Skilled Laborer	FOR	GUILLERMO LIMON	8.00	0.00	0.00	8.00		<input type="checkbox"/>
Semi-Skilled Laborer	APP	ROGELIO RODRIGUEZ	8.00	0.00	0.00	8.00		<input type="checkbox"/>
Semi-Skilled Laborer	JNM	CARLOS MONTEJANO	0.00	0.00	0.00	0.00		<input type="checkbox"/>
Semi-Skilled Laborer	APP	JOSE AVILA	0.00	0.00	0.00	0.00		<input type="checkbox"/>
Semi-Skilled Laborer	JNM	VICTOR HERNANDEZ	0.00	0.00	0.00	0.00		<input type="checkbox"/>
Ironworker	FOR	JAMES STURGEON	0.00	0.00	0.00	0.00		<input type="checkbox"/>

Equipment		Rental Company				Dispute	
Equipment ID	Description	RT Hrs	OT Hrs	ST Hrs	IT Hrs	Remarks	Dispute
Contractor: AMERICAN BRIDGE/FLUOR, A JV							
*E0020562	WELDING EQUIPMENT					No	<input type="checkbox"/>
		0.00	0.00	0.00	0.00		
*E0030562	WELDING EQUIPMENT					No	<input type="checkbox"/>
		0.00	0.00	0.00	0.00		
*E0010562	WELDING EQUIPMENT					No	<input type="checkbox"/>
		0.00	0.00	0.00	0.00		
2292	WELDER, 600 AMP					No	<input type="checkbox"/>
		0.00	0.00	0.00	0.00		
2293	WELDER, 600 AMP					No	<input type="checkbox"/>
		0.00	0.00	0.00	0.00		

04-0120F4 Bid Item: 078 T-L01-ENE.078 Tower Lift 01 External Paint Tower NE
 CERTIFIED COATINGS COMPANY

04-0120F4 Bid Item: 078 T-L05-ENE.078 Tower Lift 05 External Paint Tower NE
 CERTIFIED COATINGS COMPANY

04-0120F4 Bid Item: 078 T-HEA-ENE.078 Tower Head External Paint Tower NE
 CERTIFIED COATINGS COMPANY

CCO-355 Bid Item: 001 0-CIC-EFA.355 CIC - Elevator Impacts - USA Hoist
 AMERICAN BRIDGE/FLUOR, A JV

Attachment

Daily Diary Report by Bid Item

Job Name: 04-0120F4

Inspector Name: Liu, Tai-Lin

Diary #: 326

Date: 16-Jul-2014

Wednesday




One ABF labor - Nujo worked on drain pipe caulking for two hours today



ABF's crew performed tower exterior cleaning work today



FWS electricians performed electric line installation for tower elevation

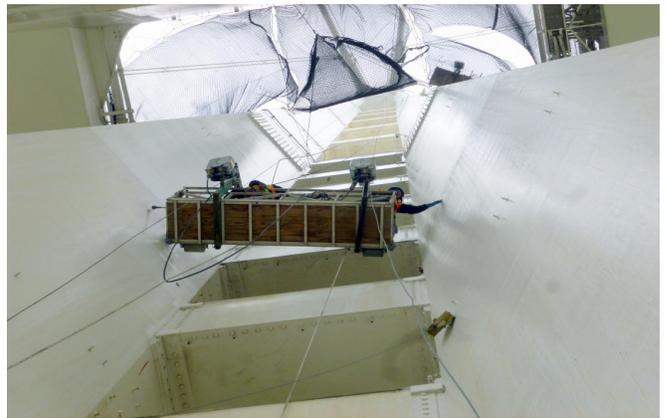

ABF's labores performed tower exterior cleaning works on west side around 33 meter area



ABF's labores performed tower east shaft exterior cleaning works



Workers performed works on elevator
