



Daily Diary Report by Bid Item

Contract No.: 04-0120F4

Diary #: 341 Const Calendar Day: 795 Date: 08-Aug-2014 Friday
 Inspector Name: Liu, Tai-Lin Title: Transportation Engineer
 Inspection Type: Continuous
 Shift Hours: 07:00 AM 03:30 PM Break: 00:30 Over Time:
 Federal ID:
 Location:
 Reviewer: Awal, Mohammad Approved Date: 17-Aug-14 Status: Approved

04-0120F4
 04-SF-80-13.2/13.9
 Self-Anchored
 Suspension Bridge

Weather

Temperature 7 AM 60 - 70 12 PM 70 - 80 4PM 70 - 80
 Precipitation Condition Clear

Working Day If no, explain:

Diary: Dispute

Tower Activites

CCO # 382 - Tower Painting and Cleaning works (Below 53 m area) (8/8/14, Friday - Clear):

- * Performed paper work, and RFI/Submittal PMIV process then went to field with Grady (safety office).
- * At job site, saw three labores (Jose Jr. Avile, Julio Hernandez and Dave Draper) at East side of tower base (see picture). They continued cleaning inside cell area and moved garbage out of tower base area to the barge and to boat as well. Dave told me that they still have lots of stuff to be removed from inside the cell. Crane operator Neil and helper Justine were helping them moving garbage container to the boat.
- * CCC paint repair work:
 - Total seven painters continued performing paint repair at the location from 33m to 23m area (external façade and shaft face A and E area).
 - At field, saw METS Mihal at tower base he told me he was checking punchlist items and paint inspector Stuart was checking paint repair work at higher elevation. I pointed out the south side of tower the façade areas only having half done the paint repair work. Mihal said CCC will complete that area later.
 - Paint Crew: Ron Shaver, Franciso Serano, Rafael Serano, Mike Woodnancy, Cory Robinson, Alfredo Gutierrez, Cory Reese (7).
- * Other works:
 - Saw crane operator Neil Caldwell & helper Justin performed moving garbage container from tower base to barge & on the boat.
 - Saw Mahmoud performed inspection on tower elevator installation with 2 workers (US Hoist).
 - Grady was in tower base with me today.

Performed paper work and RFI/Submittal PMIV process work at office.

04-0120F4 Bid Item: 053 T-L01-DSE.053 Tower Lift 01 Diaphragm Tower SE Erect structural steel (bridge tower)
 AMERICAN BRIDGE/FLUOR, A JV

Labor							Dispute	
Trade	Class	Name	RT Hrs	OT Hrs	DT Hrs	Total	Remarks	Dispute
Contractor:		AMERICAN BRIDGE/FLUOR, A JV						

Daily Diary Report by Bid Item

Job Name: 04-0120F4 **Inspector Name:** Liu, Tai-Lin **Diary #:** 341 **Date:** 08-Aug-2014 **Friday**

Ironworker	JNM	DONALD PLUMB	0.00	0.00	0.00	0.00	<input type="checkbox"/>
Ironworker	JNM	PAUL FAMBRINI	0.00	0.00	0.00	0.00	<input type="checkbox"/>
Semi-Skilled Laborer	JNM	FERMIN MEDINA	0.00	0.00	0.00	0.00	<input type="checkbox"/>
Ironworker	GEN	AARON KENT	0.00	0.00	0.00	0.00	<input type="checkbox"/>
Semi-Skilled Laborer	JNM	LUIS Jimenez	0.00	0.00	0.00	0.00	<input type="checkbox"/>
Semi-Skilled Laborer	JNM	DANNY SCHWARTZ	0.00	0.00	0.00	0.00	<input type="checkbox"/>
Semi-Skilled Laborer	APP	JAVIER MEDINA	0.00	0.00	0.00	0.00	<input type="checkbox"/>
Semi-Skilled Laborer	FOR	GUILLERMO LIMON	0.00	0.00	0.00	0.00	<input type="checkbox"/>
Semi-Skilled Laborer	APP	ROGELIO RODRIGUEZ	0.00	0.00	0.00	0.00	<input type="checkbox"/>
Semi-Skilled Laborer	JNM	CARLOS MONTEJANO	0.00	0.00	0.00	0.00	<input type="checkbox"/>
Semi-Skilled Laborer	APP	JOSE AVILA	0.00	0.00	0.00	0.00	<input type="checkbox"/>
Semi-Skilled Laborer	JNM	VICTOR HERNANDEZ	0.00	0.00	0.00	0.00	<input type="checkbox"/>
Ironworker	FOR	JAMES STURGEON	0.00	0.00	0.00	0.00	<input type="checkbox"/>

Equipment		Rental Company				Dispute
Equipment ID	Description	RT Hrs	OT Hrs	ST Hrs	IT Hrs	Remarks
Contractor: AMERICAN BRIDGE/FLUOR, A JV						
*E0020562	WELDING EQUIPMENT	0.00	0.00	0.00	0.00	No
*E0030562	WELDING EQUIPMENT	0.00	0.00	0.00	0.00	No
*E0010562	WELDING EQUIPMENT	0.00	0.00	0.00	0.00	No
2292	WELDER, 600 AMP	0.00	0.00	0.00	0.00	No
2293	WELDER, 600 AMP	0.00	0.00	0.00	0.00	No

04-0120F4 Bid Item: 078 T-L01-ENE.078 Tower Lift 01 External Paint Tower NE
 CERTIFIED COATINGS COMPANY

04-0120F4 Bid Item: 078 T-L05-ENE.078 Tower Lift 05 External Paint Tower NE
 CERTIFIED COATINGS COMPANY

04-0120F4 Bid Item: 078 T-HEA-ENE.078 Tower Head External Paint Tower NE
 CERTIFIED COATINGS COMPANY

CCO-355 Bid Item: 001 0-CIC-EFA.355 CIC - Elevator Impacts - USA Hoist
 AMERICAN BRIDGE/FLUOR, A JV

Attachment

Daily Diary Report by Bid Item

Job Name: 04-0120F4

Inspector Name: Liu, Tai-Lin

Diary #: 341

Date: 08-Aug-2014

Friday



Saw METS ASMR & ABF's labores on the opening area of east side of tower



METS ASMR Mihal was in field checking the paint repair work



Curtain on west side of tower from 33 meter to 13 meter



CCC's painter performed paint repair on 23 meter



ABF labores loaded the garbage container to the boat



Three ABF labores performed cleaning work and moved the garbage container from tower base to the boat

Daily Diary Report by Bid Item

Job Name: 04-0120F4

Inspector Name: Liu, Tai-Lin


Diary #: 341

Date: 08-Aug-2014

Friday



Curtain on East side of tower from 23m to 13 meter

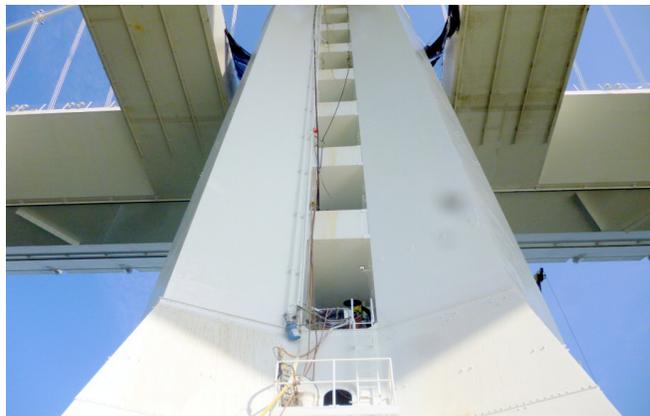

View from east side of tower base
