



Daily Diary Report by Bid Item

Contract No.: 04-0120F4

Diary #: 342 Const Calendar Day: 798 Date: 11-Aug-2014 Monday
 Inspector Name: Liu, Tai-Lin Title: Transportation Engineer
 Inspection Type: Continuous
 Shift Hours: 07:00 AM 05:00 PM Break: 00:30 Over Time: 02:00
 Federal ID:
 Location:
 Reviewer: Awal, Mohammad Approved Date: 17-Aug-14 Status: Approved

04-0120F4
 04-SF-80-13.2/13.9
 Self-Anchored
 Suspension Bridge

Weather

Temperature 7 AM 60 - 70 12 PM 70 - 80 4PM 70 - 80
 Precipitation Condition Clear

Working Day If no, explain:

Diary:

Dispute

Tower Activites

CCO # 382 - Tower Painting and Cleaning works (8/11/14, Monday - Clear):

- * Mohammad told me I need watch whole tower operation due to Laraine leaving the project.
- * Performed paper work, and attended staff meeting. Went to job site with Mohammad around 9:15AM to meet METS ASMR Mihal at W2 then took elevator to deck & walking to tower.
- * At tower road deck (53m), saw ABF's Engineer Levi and Forman James Sturgeon (Fish).
- * Climbed to higher elevation with Mohammad (El. 65m & 77m) to watch painters performing paint repair work. Mohammad continued climbing to higher elevation to check façade door latch with Mihal.
- * Tower External Cleaning Works (ABF's labores-worked 8 hours today):
 - Four labores (Victor Hernandez, Jose Jr. Avila Victor, Aurelio Rodriguez and Danny Schwartz) worked today.
 - They worked on N shaft Face E, E shaft Face E, S shaft Face E and W shaft Face E at area between El. 65m to 77m area. ABF also requested area inspection in the same elevation and Face A in different shafts.
 - Victor Hernandez & Jose Jr. Avila at tower base El. 13 meter area performed houskeeping work.
- * CCC paint repair work (crew worked 12 hours today - 6 Am to 6 PM):
 - CCC almost completed the paint repair works on the area below 53m to 3m, and requested METS inspection check on Face A / E on four shaft areas.
 - Saw 9 painters working in different area (above 53 meter, see pictures): E Shaft Face A, El. 77, N shaft Face A & E on El. 77m - 86m, swing stage on W shaft Face D / C, El. 139 m and N shaft Face C / D on El. 109 meter area.
 - Paint Crew: Ron Shaver, Franciso Serano, Rafael Ventura, Armado Dvitia, Manuel Ramirez, Mike Woodnancy, Cory Reese, Alberto Serrano, Johanny Fagundes.
- * Other works:
 - Saw crane operator Neil Caldwell & helper Justin on the barge moving garbage container from tower base to barge & on the boat.
 - Saw Mahmoud performed inspection on tower elevator installation with 4 workers (US Hoist).

Performed paper work and RFI/Submittal PMIV process work at office, left office around 5:00 PM.

04-0120F4	Bid Item: 053	T-L01-DSE.053	Tower Lift 01 Diaphram Tower SE Erect structural steel (bridge tower)
-----------	---------------	---------------	---

Daily Diary Report by Bid Item

Job Name: 04-0120F4

Inspector Name: Liu, Tai-Lin

Diary #: 342

Date: 11-Aug-2014 Monday

AMERICAN BRIDGE/FLUOR, A JV

Labor

Trade	Class	Name	RT Hrs	OT Hrs	DT Hrs	Total	Remarks	Dispute
Contractor: AMERICAN BRIDGE/FLUOR, A JV								
Ironworker	JNM	DONALD PLUMB	0.00	0.00	0.00	0.00		<input type="checkbox"/>
Ironworker	JNM	PAUL FAMBRINI	0.00	0.00	0.00	0.00		<input type="checkbox"/>
Semi-Skilled Laborer	JNM	FERMIN MEDINA	0.00	0.00	0.00	0.00		<input type="checkbox"/>
Ironworker	GEN	AARON KENT	0.00	0.00	0.00	0.00		<input type="checkbox"/>
Semi-Skilled Laborer	JNM	LUIS Jimenez	0.00	0.00	0.00	0.00		<input type="checkbox"/>
Semi-Skilled Laborer	JNM	DANNY SCHWARTZ	0.00	0.00	0.00	0.00		<input type="checkbox"/>
Semi-Skilled Laborer	APP	JAVIER MEDINA	0.00	0.00	0.00	0.00		<input type="checkbox"/>
Semi-Skilled Laborer	FOR	GUILLERMO LIMON	0.00	0.00	0.00	0.00		<input type="checkbox"/>
Semi-Skilled Laborer	APP	ROGELIO RODRIGUEZ	0.00	0.00	0.00	0.00		<input type="checkbox"/>
Semi-Skilled Laborer	JNM	CARLOS MONTEJANO	0.00	0.00	0.00	0.00		<input type="checkbox"/>
Semi-Skilled Laborer	APP	JOSE AVILA	0.00	0.00	0.00	0.00		<input type="checkbox"/>
Semi-Skilled Laborer	JNM	VICTOR HERNANDEZ	0.00	0.00	0.00	0.00		<input type="checkbox"/>
Ironworker	FOR	JAMES STURGEON	0.00	0.00	0.00	0.00		<input type="checkbox"/>

Equipment

Equipment ID	Description	RT Hrs	OT Hrs	ST Hrs	IT Hrs	Rental Company	Remarks	Dispute
Contractor: AMERICAN BRIDGE/FLUOR, A JV								
*E0020562	WELDING EQUIPMENT						No	<input type="checkbox"/>
		0.00	0.00	0.00	0.00			
*E0030562	WELDING EQUIPMENT						No	<input type="checkbox"/>
		0.00	0.00	0.00	0.00			
*E0010562	WELDING EQUIPMENT						No	<input type="checkbox"/>
		0.00	0.00	0.00	0.00			
2292	WELDER, 600 AMP						No	<input type="checkbox"/>
		0.00	0.00	0.00	0.00			
2293	WELDER, 600 AMP						No	<input type="checkbox"/>
		0.00	0.00	0.00	0.00			

04-0120F4 Bid Item: 078 T-L01-ENE.078 Tower Lift 01 External Paint Tower NE

CERTIFIED COATINGS COMPANY

04-0120F4 Bid Item: 078 T-L05-ENE.078 Tower Lift 05 External Paint Tower NE

CERTIFIED COATINGS COMPANY

04-0120F4 Bid Item: 078 T-HEA-ENE.078 Tower Head External Paint Tower NE

CERTIFIED COATINGS COMPANY

CCO-355 Bid Item: 001 0-CIC-EFA.355 CIC - Elevator Impacts - USA Hoist

AMERICAN BRIDGE/FLUOR, A JV

Daily Diary Report by Bid Item

Job Name: 04-0120F4

Inspector Name: Liu, Tai-Lin

Diary #: 342

Date: 11-Aug-2014

Monday

Attachment



Painter performed paint repair on El. 77 shaft E




Painters (Ron & Rafael) performed paint repair at El. 80m North shaft face A



Ron & Rafael performed paint repair at El. 77 North shaft face A



L shape scaffold at El. 139m on shaft W for paint repair

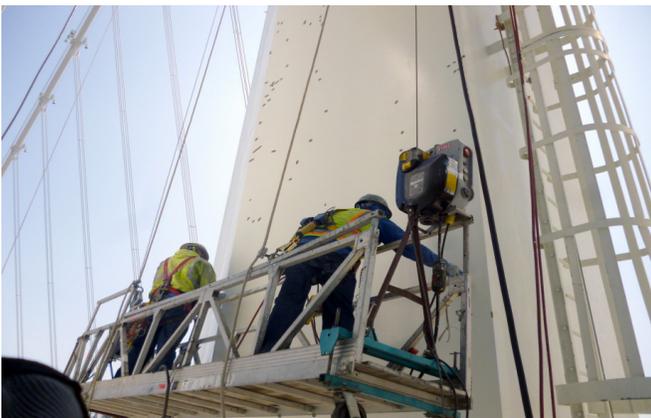

Ron & Rafael performed paint repair work at El. 86 meter



ABF's labor Victor performed housekeeping work at tower base El. 13m area

Daily Diary Report by Bid Item

Job Name: 04-0120F4

Inspector Name: Liu, Tai-Lin

Diary #: 342

Date: 11-Aug-2014

Monday



Saw Bill, Fish, Feather and on labor at El. 53 m East side of cross beam



Painters performed paint repair at El. 109m, 77m and 68m on North shaft
