



Daily Diary Report by Bid Item

Contract No.: 04-0120F4

Diary #: 343 Const Calendar Day: 799 Date: 12-Aug-2014 Tuesday
 Inspector Name: Liu, Tai-Lin Title: Transportation Engineer
 Inspection Type: Continuous
 Shift Hours: 06:30 AM 04:00 PM Break: 00:30 Over Time: 01:00

04-0120F4
 04-SF-80-13.2/13.9
 Self-Anchored
 Suspension Bridge

Federal ID:

Location:

Reviewer: Awal, Mohammad Approved Date: 17-Aug-14 Status: Approved

Weather

Temperature 7 AM 60 - 70 12 PM 70 - 80 4PM 70 - 80
 Precipitation Condition Clear

Working Day If no, explain:

Diary:

Dispute

Tower Activites

CCO # 382 - Tower Painting and Cleaning works (8/12/14, Tuesday - Clear):

- * Performed paper work, and checked e-mail. Went to job site (T1 base by boat) with Grady.
- * At tower base, saw two ABF's labores Victor Hernandez & Jose Jr. Avila at tower base El. 13 meter area performed houskeeping work. Talked to Forman Victor, he told me there are two more labores on the above 53m of tower (Aurelio Rodriuez & Danny Schwartz) total 4 labores worked in tower today (8 hours shift). ABF's labores mainly performed hosekeeping and moving swing stage for painters.
- * After lunch, drove to W2 and walked to Tower entance El.53. From deck area, saw 5 swing stages on the tower. Two L shape stages were in N & W shafts face C and D at El 89 & 109m, respectively. Two straight stages were in the area between shafts, shaft N / W Face E, El. 68m and 77 meter. There was one singer stage was in south side of tower at El. 53 by painter Edilberto for paint repair at that area.
- * At tower base area, there were 4 painter performed touch-up works (see pictures) at El. 13 to 47 meter area.
- * Paint Crew: Ron Shaver, Franciso Serano, Rafael Ventura, Armado Avitia, Manuel Ramirez, Mike Woodnancy, Cory Reese, Alberto Serrano, Johanny Fagundes, Juan Carlos, Luis Ventura, Oscar Salazar, Ramon Gutierrez, Edilberto Leno (worked 8 hours), Daniel Rosales, Abraham Ventura. Crew worked from 6AM to 6PM, 12 hours shift.
- * Saw METS Stuart at tower, he was leaving tower back to pier 7 for meeting and will back to tower later.
- * At 2:30 PM, saw James & Ray at tower entrance El. 53. James told me that there were four labors working in tower today, mainly for hourskeeping and moving swing stages for painter.
- * Four labores: Victor Hernandez, Jose Jr. Avila, Aurelio Rodriguez and Danny Schwartz worked 8 hours shift today (6 AM to 2:30PM).
- * Other works:
 - Saw crane operator Neil Caldwell & helper Justin on the barge moving garbage container from tower base to barge & on the boat.
 - Saw Mahmoud performed inspection on tower elevator installation with 4 workers (US Hoist).

Performed paper work and RFI/Submittal PMIV process work at office, office out off power around 3:00

Daily Diary Report by Bid Item

Job Name: 04-0120F4

Inspector Name: Liu, Tai-Lin

Diary #: 343

Date: 12-Aug-2014 Tuesday

PM. Left office around 4:00 PM.

04-0120F4 Bid Item: 053 T-L01-DSE.053 Tower Lift 01 Diaphragm Tower SE Erect structural steel (bridge tower)
 AMERICAN BRIDGE/FLUOR, A JV

Labor

Trade	Class	Name	RT Hrs	OT Hrs	DT Hrs	Total	Remarks	Dispute
Contractor: AMERICAN BRIDGE/FLUOR, A JV								
Ironworker	JNM	DONALD PLUMB	0.00	0.00	0.00	0.00		<input type="checkbox"/>
Ironworker	JNM	PAUL FAMBRINI	0.00	0.00	0.00	0.00		<input type="checkbox"/>
Semi-Skilled Laborer	JNM	FERMIN MEDINA	0.00	0.00	0.00	0.00		<input type="checkbox"/>
Ironworker	GEN	AARON KENT	0.00	0.00	0.00	0.00		<input type="checkbox"/>
Semi-Skilled Laborer	JNM	LUIS Jimenez	0.00	0.00	0.00	0.00		<input type="checkbox"/>
Semi-Skilled Laborer	JNM	DANNY SCHWARTZ	0.00	0.00	0.00	0.00		<input type="checkbox"/>
Semi-Skilled Laborer	APP	JAVIER MEDINA	0.00	0.00	0.00	0.00		<input type="checkbox"/>
Semi-Skilled Laborer	FOR	GUILLERMO LIMON	0.00	0.00	0.00	0.00		<input type="checkbox"/>
Semi-Skilled Laborer	APP	ROGELIO RODRIGUEZ	0.00	0.00	0.00	0.00		<input type="checkbox"/>
Semi-Skilled Laborer	JNM	CARLOS MONTEJANO	0.00	0.00	0.00	0.00		<input type="checkbox"/>
Semi-Skilled Laborer	APP	JOSE AVILA	0.00	0.00	0.00	0.00		<input type="checkbox"/>
Semi-Skilled Laborer	JNM	VICTOR HERNANDEZ	0.00	0.00	0.00	0.00		<input type="checkbox"/>
Ironworker	FOR	JAMES STURGEON	0.00	0.00	0.00	0.00		<input type="checkbox"/>

Equipment

Equipment ID	Description	RT Hrs	OT Hrs	ST Hrs	IT Hrs	Rental Company	Remarks	Dispute
Contractor: AMERICAN BRIDGE/FLUOR, A JV								
*E0020562	WELDING EQUIPMENT						No	<input type="checkbox"/>
		0.00	0.00	0.00	0.00			
*E0030562	WELDING EQUIPMENT						No	<input type="checkbox"/>
		0.00	0.00	0.00	0.00			
*E0010562	WELDING EQUIPMENT						No	<input type="checkbox"/>
		0.00	0.00	0.00	0.00			
2292	WELDER, 600 AMP						No	<input type="checkbox"/>
		0.00	0.00	0.00	0.00			
2293	WELDER, 600 AMP						No	<input type="checkbox"/>
		0.00	0.00	0.00	0.00			

04-0120F4 Bid Item: 078 T-L01-ENE.078 Tower Lift 01 External Paint Tower NE
 CERTIFIED COATINGS COMPANY

04-0120F4 Bid Item: 078 T-L05-ENE.078 Tower Lift 05 External Paint Tower NE
 CERTIFIED COATINGS COMPANY

04-0120F4 Bid Item: 078 T-HEA-ENE.078 Tower Head External Paint Tower NE
 CERTIFIED COATINGS COMPANY

CCO-355 Bid Item: 001 0-CIC-EFA.355 CIC - Elevator Impacts - USA Hoist
 AMERICAN BRIDGE/FLUOR, A JV

Daily Diary Report by Bid Item

Job Name: 04-0120F4

Inspector Name: Liu, Tai-Lin

Diary #: 343

Date: 12-Aug-2014

Tuesday

Attachment



Viewed from CB #6, painters were in swing stages at N shaft Face A/B/C performed paint repair (El. 89 m)



Painter Cory performed paint touch-up at El. 18 walkway area




Viewed from W2, swing stage was in W shaft Face C and D El.109 m (Paint Repair)



Painters performed paint repair at swing stages at North shaft



Painters Armando & Manuel at W shaft face E performed paint repair (El. 60 m)

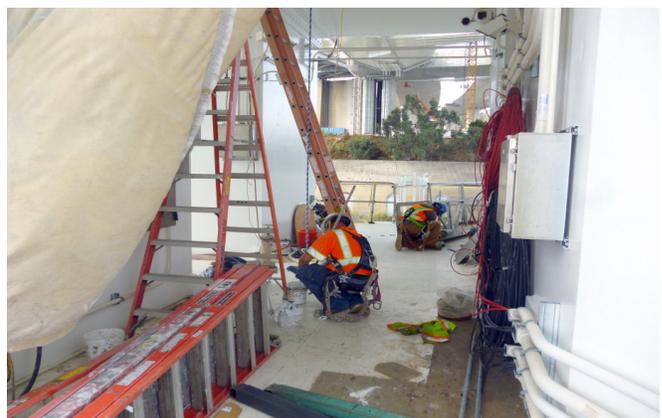

Painter Cory mixed the paint on the Tower base El. 13m, and labor Jose performed housekeeping at the same area

Daily Diary Report by Bid Item

Job Name: 04-0120F4

Inspector Name: Liu, Tai-Lin

Diary #: 343

Date: 12-Aug-2014 Tuesday



Edilberto performed paint repair on a sign swing stage on south of tower El.53m up



Two painters performed paint repair for piping at El. 53 entrance to the tower area
