



Daily Diary Report by Bid Item

Contract No.: 04-0120F4

Diary #: 346 Const Calendar Day: 802 Date: 15-Aug-2014 Friday
 Inspector Name: Liu, Tai-Lin Title: Transportation Engineer
 Inspection Type: Continuous
 Shift Hours: 06:45 AM 04:45 PM Break: 00:30 Over Time: 02:00
 Federal ID:
 Location:
 Reviewer: Awal, Mohammad Approved Date: 17-Aug-14 Status: Approved

04-0120F4
 04-SF-80-13.2/13.9
 Self-Anchored
 Suspension Bridge

Weather

Temperature 7 AM 60 - 70 12 PM 70 - 80 4PM 70 - 80
 Precipitation Condition Clear

Working Day If no, explain:

Diary:

Dispute

Tower Activites

CCO # 382 - Tower Painting and Cleaning works (8/15/14, Friday - Clear):

- * Performed paper work, and checked e-mail. Went to job site (T1 base by boat) with Grady.
- * At tower base, saw ABF's labor Jose Jr. Avila at tower El.13 and Victor on the footing area. Talked to Victor about operation. Saw painter Edilberto continued performing paint repair on south side of tower, El. 38m façade area (see picture). Went up to El.13m, saw Mahmoud with ABF's engineer and 4 personnel of US Hoist worked on tower elevator. Did not see CCC painter in the area between shafts. Took boat back to office around 11:15 AM.
- * After lunch, drove to W2 and walked to Tower entance El.53. Took presure reading on top of the air relief valve at PP44, WB bridge inboard side near tower area for Martin and Feather; (65 psi-second time measurement).
- * Saw two L-shape swing stages with 6 painters continued performed paint repair on N/W shafts, D/C faces at El. Between 53m and 71m. At tower El.53m, saw ABF paint inspector Ray, forman James and QC Sage at center of tower talking. Two painters (Armando & Manuel) performed paint repair on N shaft A face at El.55m area. Three painters (Eric, Robert & Victor) performed paint repair on piping at EB bridge near tower area (worked 8 hours shift).
- * Saw METS paint inspector Stuart inside the swing stage with two painters checking paint repair area at E shaft D face El. 56 m area. QC Sage & labor forman James also on the deck area helping painters to move swing stages, Talked to Stuart, he said that he checked cleaning and painting on N shaft D/C faces from El. 119m down to El. 56m, they were OK for him.
- * Talked to QC Sage, he told me that total 13 painters on the tower paint repair work and 3 on piping painting work today. Five more painters were in different elevation performed paint repair work, and Edilberto was in south of tower façade area performed paint preparation work.
- * Five (including James) ABF's labores performed housekeeping work in tower different area and left around 2:20 PM.
- * Paint Crew: Sage Ray, Armado Avitia, Manuel Ramirez, Cory Reese, Alberto Serrano, Juan Carlos, Luis Ventura, Oscar Salazar, Ramon Gutierrez, Edilberto Leno, Daniel Rosales, Abraham Ventura, Ron Shaver. Crew worked from 6AM to 6PM, 12 hours shift. Painters: Eric Garza, Robert Gonzalez and Victor Ruiz) worked 8 hours shift (6AM - 2:30 PM) today.

Daily Diary Report by Bid Item

Job Name: 04-0120F4

Inspector Name: Liu, Tai-Lin

Diary #: 346

Date: 15-Aug-2014 **Friday**

* Four labores: Victor Hernandez, Jose Jr. Avila, Rogelio Rodriguez and Danny Schwartz worked 8 hours shift today (6 AM to 2:30PM).

* Other works:

- Saw crane operator Neil Caldwell & helper Justin on the barge moving garbage container from tower base to barge & on the boat.
- Saw Mahmoud performed inspection on tower elevator installation with 5 workers (US Hoist), Martine was in site as well.

Performed paper work and RFI/Submittal PMIV process work at office, OT 2 hours today.

04-0120F4	Bid Item: 053	T-L01-DSE.053	Tower Lift 01 Diaphragm Tower SE Erect structural steel (bridge tower)
AMERICAN BRIDGE/FLUOR, A JV			

Labor								Dispute
Trade	Class	Name	RT Hrs	OT Hrs	DT Hrs	Total	Remarks	
Contractor: AMERICAN BRIDGE/FLUOR, A JV								
Ironworker	JNM	DONALD PLUMB	0.00	0.00	0.00	0.00		<input type="checkbox"/>
Ironworker	JNM	PAUL FAMBRINI	0.00	0.00	0.00	0.00		<input type="checkbox"/>
Semi-Skilled Laborer	JNM	FERMIN MEDINA	0.00	0.00	0.00	0.00		<input type="checkbox"/>
Ironworker	GEN	AARON KENT	0.00	0.00	0.00	0.00		<input type="checkbox"/>
Semi-Skilled Laborer	JNM	LUIS Jimenez	0.00	0.00	0.00	0.00		<input type="checkbox"/>
Semi-Skilled Laborer	JNM	DANNY SCHWARTZ	0.00	0.00	0.00	0.00		<input type="checkbox"/>
Semi-Skilled Laborer	APP	JAVIER MEDINA	0.00	0.00	0.00	0.00		<input type="checkbox"/>
Semi-Skilled Laborer	FOR	GUILLERMO LIMON	0.00	0.00	0.00	0.00		<input type="checkbox"/>
Semi-Skilled Laborer	APP	ROGELIO RODRIGUEZ	0.00	0.00	0.00	0.00		<input type="checkbox"/>
Semi-Skilled Laborer	JNM	CARLOS MONTEJANO	0.00	0.00	0.00	0.00		<input type="checkbox"/>
Semi-Skilled Laborer	APP	JOSE AVILA	0.00	0.00	0.00	0.00		<input type="checkbox"/>
Semi-Skilled Laborer	JNM	VICTOR HERNANDEZ	0.00	0.00	0.00	0.00		<input type="checkbox"/>
Ironworker	FOR	JAMES STURGEON	0.00	0.00	0.00	0.00		<input type="checkbox"/>

Equipment								Dispute
Equipment ID	Description	RT Hrs	OT Hrs	ST Hrs	IT Hrs	Remarks	Rental Company	
Contractor: AMERICAN BRIDGE/FLUOR, A JV								
*E0020562	WELDING EQUIPMENT					No		<input type="checkbox"/>
		0.00	0.00	0.00	0.00			<input type="checkbox"/>
*E0030562	WELDING EQUIPMENT					No		<input type="checkbox"/>
		0.00	0.00	0.00	0.00			<input type="checkbox"/>
*E0010562	WELDING EQUIPMENT					No		<input type="checkbox"/>
		0.00	0.00	0.00	0.00			<input type="checkbox"/>
2292	WELDER, 600 AMP					No		<input type="checkbox"/>
		0.00	0.00	0.00	0.00			<input type="checkbox"/>
2293	WELDER, 600 AMP					No		<input type="checkbox"/>
		0.00	0.00	0.00	0.00			<input type="checkbox"/>

04-0120F4	Bid Item: 078	T-L01-ENE.078	Tower Lift 01 External Paint Tower NE
CERTIFIED COATINGS COMPANY			

04-0120F4	Bid Item: 078	T-L05-ENE.078	Tower Lift 05 External Paint Tower NE
CERTIFIED COATINGS COMPANY			

Daily Diary Report by Bid Item

Job Name: 04-0120F4

Inspector Name: Liu, Tai-Lin

Diary #: 346

Date: 15-Aug-2014

Friday


04-0120F4	Bid Item: 078	T-HEA-ENE.078	Tower Head External Paint Tower NE
CERTIFIED COATINGS COMPANY			

CCO-355	Bid Item: 001	0-CIC-EFA.355	CIC - Elevator Impacts - USA Hoist
AMERICAN BRIDGE/FLUOR, A JV			

Attachment



Painters continued paint repair on N/W shaft D/C faces

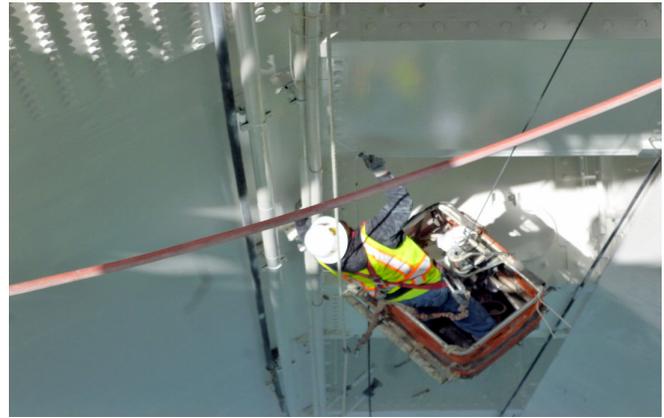

Ediberto continued paint repair on south side façade area



Two L-shape swing stages with six painters performed paint repair on N/W shaft D/C faces



Two painters performed paint repair on N shaft A face El. 56m area

Daily Diary Report by Bid Item

Job Name: 04-0120F4

Inspector Name: Liu, Tai-Lin

Diary #: 346

Date: 15-Aug-2014

Friday



Three painters continued paint repair on W shaft D/C faces El. 62m



ABF's laborer - Victor was in tower base area this morning performed housekeeping work




Edilberto - CCC painter continued performed paint repair on facade area on south side of tower



METS paint inspector checked paint repair on N shaft D/C faces El.56 m area with QC Sage & James



US Hoist personnel performed elevator installation at El.53m area

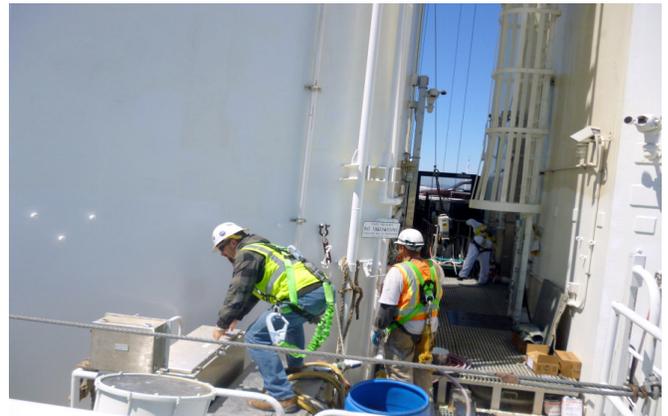

METS Stuart and QC Sage checked paint repair on S shaft D/C faces El. 53 m area

Daily Diary Report by Bid Item

Job Name: 04-0120F4

Inspector Name: Liu, Tai-Lin

Diary #: 346

Date: 15-Aug-2014 Friday



Two painters performed paint repair on E1.77m façade area
