



SAS Superstructure

Location: 04-SF-80-13.2 / 13.9

Client Name: CalTrans

Run date 22-Nov-14

Time 9:22 AM

Daily Diary Report by Bid Item

Contract No.: 04-0120F4

Diary #: 350 Const Calendar Day: 814 Date: 27-Aug-2014 Wednesday

Inspector Name: Liu, Tai-Lin Title: Transportation Engineer

Inspection Type: Continuous

Shift Hours: 07:00 AM 03:30 PM Break: 00:30 Over Time:

Federal ID:

Location:

Reviewer: Awal, Mohammad Approved Date: Status: Submit

04-0120F4
04-SF-80-13.2/13.9
Self-Anchored
Suspension Bridge

Weather

Temperature 7 AM 60 - 70 12 PM 70 - 80 4PM 70 - 80

Precipitation Condition Clear

Working Day [checked] If no, explain:

Diary:

Dispute

Tower Activites

CCO # 382 - Tower Painting and Cleaning works (8/27/14, Wednesday - Clear):

* Picked up Robert Wong from CT Milpitas Maintenance yard and rode back to office (around 8:20 AM).

* Performed paper work, and studied Tower cleaning & paint repair tracking sheets. Went to job site (T1 by driving to W2) around 10:00 AM. At tower deck El. 53 m area.

- Saw METS inspector Stuart talking to QC Sage, and labor forman Victor at El. 53 deck area.
- Talked to Stuart about work status, he told me that there were 5 CCC painters performed power tooling on Saddle housing & Parapet area at N/W shafts El. 150 m area (At internal area CCC applied prime paint at external the prime and two finishing coating were applied by painters).
- Five ABF's labores showed up in tower today (James Sturgeon, Victor Hernandez, Jose, Ragelio and Danny Schwartz), saw Victor and Danny moving swing stage's support beams from El. 90m to 53m area.
- They were few area needed to be touch-up and caulking below El. 53 m area (such as El. 13 m). Stuart checked these works this afternoon.
- Mohammad told me that tower painting works will be stopped soon and painters will back tower on 10 of September after tower elevator certified to finish the works near tower elevator.

* Paint Crew: Sage Ray, Juan Carlos, Luis Ventura, Oscar Salazar, Ramon Gutierrez, Daniel Rosales. Crew worked from 6AM to 2:30 PM, 8 hours shift.

* Labores: James Sturgeon, Jose Jr. Avila, Victor Hernandez, Rogelio Rodriguez and Danny Schwartz worked today (8 hours shift).

* Performed paper work at office, and left office around 4:30 PM.

04-0120F4 Bid Item: 053 T-L01-DSE.053 Tower Lift 01 Diaphram Tower SE Erect structural steel (bridge tower)

AMERICAN BRIDGE/FLUOR, A JV

Labor

Table with columns: Trade, Class, Name, RT Hrs, OT Hrs, DT Hrs, Total, Remarks, Dispute. Rows include Contractor: AMERICAN BRIDGE/FLUOR, A JV and various laborers like DONALD PLUMB, PAUL FAMBRINI, etc.



Daily Diary Report by Bid Item

Job Name: 04-0120F4 **Inspector Name** Liu, Tai-Lin **Diary #:** 350 **Date:** 27-Aug-2014 **Wednesday**

| | | | | | | | | |
|-----------------------------|-----------------------------|----------------------|--|---------------|---------------|---------------|-----------------------|--------------------------|
| Semi-Skilled Laborer | APP | JAVIER MEDINA | 0.00 | 0.00 | 0.00 | 0.00 | | <input type="checkbox"/> |
| Semi-Skilled Laborer | FOR | GUILLERMO LIMON | 0.00 | 0.00 | 0.00 | 0.00 | | <input type="checkbox"/> |
| Semi-Skilled Laborer | APP | ROGELIO RODRIGUEZ | 0.00 | 0.00 | 0.00 | 0.00 | | <input type="checkbox"/> |
| Semi-Skilled Laborer | JNM | CARLOS MONTEJANO | 0.00 | 0.00 | 0.00 | 0.00 | | <input type="checkbox"/> |
| Semi-Skilled Laborer | APP | JOSE AVILA | 0.00 | 0.00 | 0.00 | 0.00 | | <input type="checkbox"/> |
| Semi-Skilled Laborer | JNM | VICTOR HERNANDEZ | 0.00 | 0.00 | 0.00 | 0.00 | | <input type="checkbox"/> |
| Ironworker | FOR | JAMES STURGEON | 0.00 | 0.00 | 0.00 | 0.00 | | <input type="checkbox"/> |
| Equipment | | | | | | | | |
| Equipment ID | Description | | RT Hrs | OT Hrs | ST Hrs | IT Hrs | Rental Company | Dispute |
| Contractor: | AMERICAN BRIDGE/FLUOR, A JV | | | | | | | |
| *E0020562 | WELDING EQUIPMENT | | | | | | No | <input type="checkbox"/> |
| | | | 0.00 | 0.00 | 0.00 | 0.00 | | <input type="checkbox"/> |
| *E0030562 | WELDING EQUIPMENT | | | | | | No | <input type="checkbox"/> |
| | | | 0.00 | 0.00 | 0.00 | 0.00 | | <input type="checkbox"/> |
| *E0010562 | WELDING EQUIPMENT | | | | | | No | <input type="checkbox"/> |
| | | | 0.00 | 0.00 | 0.00 | 0.00 | | <input type="checkbox"/> |
| 2292 | WELDER, 600 AMP | | | | | | No | <input type="checkbox"/> |
| | | | 0.00 | 0.00 | 0.00 | 0.00 | | <input type="checkbox"/> |
| 2293 | WELDER, 600 AMP | | | | | | No | <input type="checkbox"/> |
| | | | 0.00 | 0.00 | 0.00 | 0.00 | | <input type="checkbox"/> |
| 04-0120F4 | Bid Item: 078 | T-L01-ENE.078 | Tower Lift 01 External Paint Tower NE | | | | | |
| CERTIFIED COATINGS COMPANY | | | | | | | | |
| | | | | | | | | |
| 04-0120F4 | Bid Item: 078 | T-L05-ENE.078 | Tower Lift 05 External Paint Tower NE | | | | | |
| CERTIFIED COATINGS COMPANY | | | | | | | | |
| | | | | | | | | |
| 04-0120F4 | Bid Item: 078 | T-HEA-ENE.078 | Tower Head External Paint Tower NE | | | | | |
| CERTIFIED COATINGS COMPANY | | | | | | | | |
| | | | | | | | | |
| CCO-355 | Bid Item: 001 | 0-CIC-EFA.355 | CIC - Elevator Impacts - USA Hoist | | | | | |
| AMERICAN BRIDGE/FLUOR, A JV | | | | | | | | |
| | | | | | | | | |

Attachment



Daily Diary Report by Bid Item

Job Name: 04-0120F4

Inspector Name Liu, Tai-Lin

Diary #: 350

Date: 27-Aug-2014

Wednesday



Tower picture shot from W2 area




Another labor Danny was on the tower El. 99 m moving support beam down to the El.53 m area



Labor Victor caught the swing stage support beam on the El. 53 m area



Martin took Beta personnel up to tower to check Dehumidifier

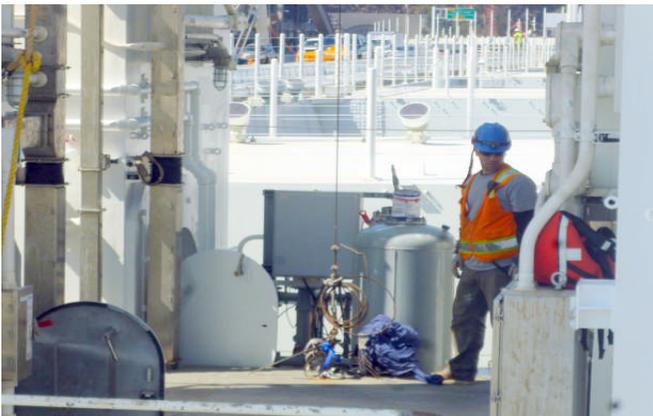

Labor formen Victor in tower El. 53m area



Saw METS Stuart left from Tower

Daily Diary Report by Bid Item


Job Name: 04-0120F4

Inspector Name Liu, Tai-Lin


Diary #: 350

Date: 27-Aug-2014

Wednesday

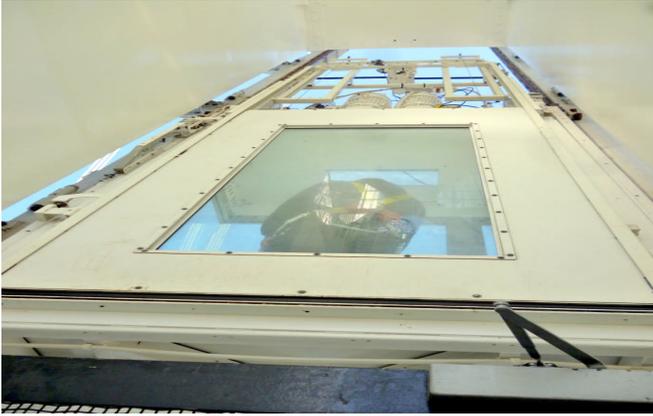

US Hoist personnel worked inside tower elevator at El. 56 m area

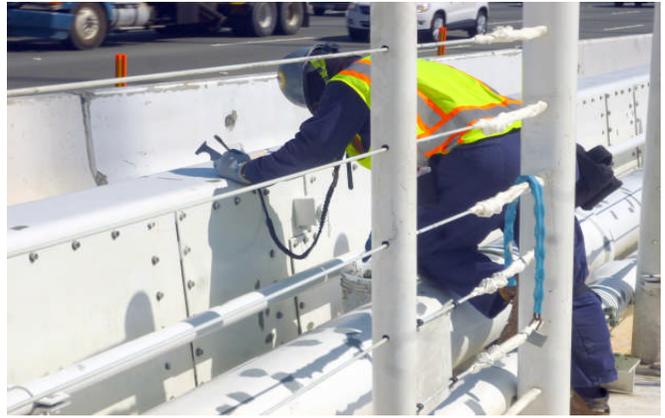

Painter performed power tooling the area on barrier next to Tower
