



SAS Superstructure

Location: 04-SF-80-13.2 / 13.9

Client Name: CalTrans

Run date 22-Nov-14

Time 9:19 AM

Daily Diary Report by Bid Item

Contract No.: 04-0120F4

Diary #: 354 Const Calendar Day: 822 Date: 04-Sep-2014 Thursday

Inspector Name: Liu, Tai-Lin Title: Transportation Engineer

Inspection Type: Continuous

Shift Hours: 07:00 AM 03:30 PM Break: 00:30 Over Time:

Federal ID:

Location:

Reviewer: Awal, Mohammad Approved Date: Status: Submit

04-0120F4
04-SF-80-13.2/13.9
Self-Anchored
Suspension Bridge

Weather

Temperature 7 AM 60 - 70 12 PM 70 - 80 4PM 70 - 80

Precipitation Condition Clear

Working Day If no, explain:

Diary:

Dispute

Tower Activites

CCO # 382 - Tower Painting and Cleaning works (9/4/14, Thursday - Clear):



* Took sick leave yesterday (9/3/14).

* Attended safety meeting this morning, and went to T1 tower base with Awal and two ABF's Engineers (Levi & Bret) to show then the unrepaired concrete crack area on tower base footing area. Levi said that he will inform Conco to come over footing area to complete concrete crack repair work next Monday. Total unrepaired crack length might be around 800 cm. I will be in footing area Monday to direct labor to finish the repair. At footing area also saw two painters performing paint repair on skirt area underneath the south shaft (see picture) area. Went back to office by boat around 10:30 AM.

* Performed paper work, and studied Tower cleaning & paint repair tracking sheets. Went to job site (T1 by driving to W2) around 1:00 PM.

- At parking lot near W2 elevator, saw METS paint inspector Stuart with painter checking cable shroud painting inside the mobile lifting car (see picture).

- Took elevator to the deck, and walked to tower El. 53 m area. Again, I saw dozen of CCC painters worked on barrier and piping paint repair works near tower area (see pictures).

- At El. 53 m deck area, saw ABF labor forman James unloaded the signle swin stage from truck to the deck near tower. Talked to him, there were 4 labores working in tower performing hours keeping work.

- There were 4 CCC's painters working in tower EL. 143 m floor area (El. 160, papapet paint repair work was completed).

* Paint Crew: Sage Ray, Juan Carlos, Luis Ventura, Oscar Salazar worked from 6AM to 2:30 PM, 8 hours shift.

* Labores: James Sturgeon, Jose Jr. Avila, Victor Hernandez, and Danny Schwartz worked today (8 hours shift).

- Left T1 around 1:45PM, saw Stuart still checking cable shroud painting also saw Grady at parking lot. Went back office around 2:25 PM.

* Performed paper work at office, and left office around 4:05 PM.



Daily Diary Report by Bid Item

Job Name: 04-0120F4 Inspector Name Liu, Tai-Lin Diary #: 354 Date: 04-Sep-2014 Thursday

04-0120F4	Bid Item: 053	T-L01-DSE.053	Tower Lift 01 Diaphragm Tower SE Erect structural steel (bridge tower)					
AMERICAN BRIDGE/FLUOR, A JV								
Labor								
Trade	Class	Name	RT Hrs	OT Hrs	DT Hrs	Total	Remarks	Dispute
Contractor: AMERICAN BRIDGE/FLUOR, A JV								
Ironworker	JNM	DONALD PLUMB	0.00	0.00	0.00	0.00		<input type="checkbox"/>
Ironworker	JNM	PAUL FAMBRINI	0.00	0.00	0.00	0.00		<input type="checkbox"/>
Semi-Skilled Laborer	JNM	FERMIN MEDINA	0.00	0.00	0.00	0.00		<input type="checkbox"/>
Ironworker	GEN	AARON KENT	0.00	0.00	0.00	0.00		<input type="checkbox"/>
Semi-Skilled Laborer	JNM	LUIS Jimenez	0.00	0.00	0.00	0.00		<input type="checkbox"/>
Semi-Skilled Laborer	JNM	DANNY SCHWARTZ	0.00	0.00	0.00	0.00		<input type="checkbox"/>
Semi-Skilled Laborer	APP	JAVIER MEDINA	0.00	0.00	0.00	0.00		<input type="checkbox"/>
Semi-Skilled Laborer	FOR	GUILLERMO LIMON	0.00	0.00	0.00	0.00		<input type="checkbox"/>
Semi-Skilled Laborer	APP	ROGELIO RODRIGUEZ	0.00	0.00	0.00	0.00		<input type="checkbox"/>
Semi-Skilled Laborer	JNM	CARLOS MONTEJANO	0.00	0.00	0.00	0.00		<input type="checkbox"/>
Semi-Skilled Laborer	APP	JOSE AVILA	0.00	0.00	0.00	0.00		<input type="checkbox"/>
Semi-Skilled Laborer	JNM	VICTOR HERNANDEZ	0.00	0.00	0.00	0.00		<input type="checkbox"/>
Ironworker	FOR	JAMES STURGEON	0.00	0.00	0.00	0.00		<input type="checkbox"/>
Equipment					Rental Company			
Equipment ID	Description		RT Hrs	OT Hrs	ST Hrs	IT Hrs	Remarks	Dispute
Contractor: AMERICAN BRIDGE/FLUOR, A JV								
*E0020562	WELDING EQUIPMENT						No	<input type="checkbox"/>
			0.00	0.00	0.00	0.00		<input type="checkbox"/>
*E0030562	WELDING EQUIPMENT						No	<input type="checkbox"/>
			0.00	0.00	0.00	0.00		<input type="checkbox"/>
*E0010562	WELDING EQUIPMENT						No	<input type="checkbox"/>
			0.00	0.00	0.00	0.00		<input type="checkbox"/>
2292	WELDER, 600 AMP						No	<input type="checkbox"/>
			0.00	0.00	0.00	0.00		<input type="checkbox"/>
2293	WELDER, 600 AMP						No	<input type="checkbox"/>
			0.00	0.00	0.00	0.00		<input type="checkbox"/>
04-0120F4	Bid Item: 078	T-L01-ENE.078	Tower Lift 01 External Paint Tower NE					
CERTIFIED COATINGS COMPANY								
04-0120F4	Bid Item: 078	T-L05-ENE.078	Tower Lift 05 External Paint Tower NE					
CERTIFIED COATINGS COMPANY								
04-0120F4	Bid Item: 078	T-HEA-ENE.078	Tower Head External Paint Tower NE					
CERTIFIED COATINGS COMPANY								
CCO-355	Bid Item: 001	0-CIC-EFA.355	CIC - Elevator Impacts - USA Hoist					
AMERICAN BRIDGE/FLUOR, A JV								

Daily Diary Report by Bid Item

Job Name: 04-0120F4

Inspector Name Liu, Tai-Lin

Diary #: 354

Date: 04-Sep-2014

Thursday


Attachment




Marked footing unrepair concrete crack with Levi



ABF engineer Levi with Awal at footing area for remarked unrepair concrete crack area

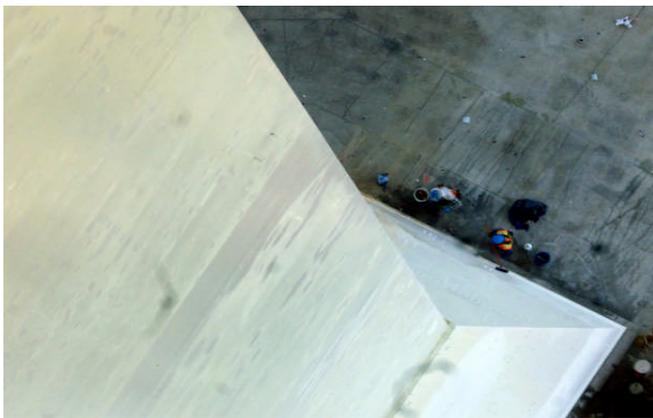

Viewed from EI. 53m for CCC's painters performing skirt paint repair - South shaft (paint on face B didn't look good)

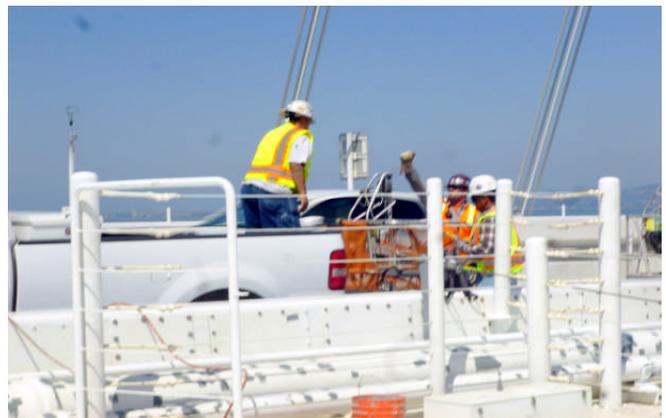

Labor forman James - removed single swin stage from truck to deck area near tower



Two CCC's painters performed paint repair on south skirt area



Mep group of people, Grady & ABF's engineer were in footing area today

Daily Diary Report by Bid Item

Job Name: 04-0120F4

Inspector Name Liu, Tai-Lin

Diary #: 354

Date: 04-Sep-2014

Thursday



Marked unrepair concrete crackarea with Levi at footing area



Saw paint inspector Stuart (METS) checking paint on W2 cable shroud area
