



Daily Diary Report by Bid Item

Contract No.: 04-0120F4

Diary #: 361 Const Calendar Day: 836 Date: 18-Sep-2014 Thursday
 Inspector Name: Liu, Tai-Lin Title: Transportation Engineer
 Inspection Type: Continuous
 Shift Hours: 07:00 AM 03:30 PM Break: 00:30 Over Time:
 Federal ID:
 Location:
 Reviewer: Awal, Mohammad Approved Date: Status: Submit

04-0120F4
 04-SF-80-13.2/13.9
 Self-Anchored
 Suspension Bridge

Weather

Temperature 7 AM 60 - 70 12 PM 70 - 80 4PM 70 - 80
 Precipitation Condition Clear

Working Day If no, explain:

Diary:

Dispute

Tower Activites

CCO # 382 - Tower Painting and Cleaning works (9/18/14, Thursday - overcast morning & fine day afternoon):

- * Attended safety meeting this morning, I was the presenter to talk about truck accident prevention.
- * Studied the paint repair tracking sheet. Went to job site (T1 by driving to W2) and walked to tower deck area El. 53m.
- Saw METS paint inspector Stuart and labor forman James on tower El. 53 m area. CCC (3) performed cleaning on elevator railing area between N and W shafts (El. 110m) using two spiders (see pictures). Two more painters worked on the area below El. 53 m for ladder paint repair. Stuart told me that there is no area to be checked today yet, he is going to see the caulking condition on El. 38 floor area with ABF labor forman James. Total 6 painters on the site and worked 10 hours today.
- Saw Awal & METS personnel on the tower base area (El. 13m area), they were going to inside the tower base to check caulking between anchor rods to anchor plate area. Also saw three Bleyco workers installing PVC pipes for lighting fixtures and camara equipment.
- * Paint Crew: Sage Ray, Juan Carlos, Luis Ventura, Oscar Salazar, Ramon Gutierrez, Abraham Ventura. Crew worked from 6AM to 4:30 PM, 10 hours shift.
- * Labores: James Sturgeon (10 hours), Aaron Kent (8 hours) and Donald Plumb (4 hours on tower) today.
- Left T1 around 2:30PM,
- * Performed paper work at office, and left office around 3:40 PM.

04-0120F4		Bid Item: 053		T-L01-DSE.053		Tower Lift 01 Diaphram Tower SE Erect structural steel (bridge tower)		
AMERICAN BRIDGE/FLUOR, A JV								
Labor								
Trade	Class	Name	RT Hrs	OT Hrs	DT Hrs	Total	Remarks	Dispute
Contractor: AMERICAN BRIDGE/FLUOR, A JV								
Ironworker	JNM	DONALD PLUMB	0.00	0.00	0.00	0.00		<input type="checkbox"/>
Ironworker	JNM	PAUL FAMBRINI	0.00	0.00	0.00	0.00		<input type="checkbox"/>
Semi-Skilled Laborer	JNM	FERMIN MEDINA	0.00	0.00	0.00	0.00		<input type="checkbox"/>
Ironworker	GEN	AARON KENT	0.00	0.00	0.00	0.00		<input type="checkbox"/>

Daily Diary Report by Bid Item

Job Name: 04-0120F4 **Inspector Name** Liu, Tai-Lin **Diary #:** 361 **Date:** 18-Sep-2014 **Thursday**

Semi-Skilled Laborer	JNM	LUIS Jimenez	0.00	0.00	0.00	0.00	<input type="checkbox"/>
Semi-Skilled Laborer	JNM	DANNY SCHWARTZ	0.00	0.00	0.00	0.00	<input type="checkbox"/>
Semi-Skilled Laborer	APP	JAVIER MEDINA	0.00	0.00	0.00	0.00	<input type="checkbox"/>
Semi-Skilled Laborer	FOR	GUILLERMO LIMON	0.00	0.00	0.00	0.00	<input type="checkbox"/>
Semi-Skilled Laborer	APP	ROGELIO RODRIGUEZ	0.00	0.00	0.00	0.00	<input type="checkbox"/>
Semi-Skilled Laborer	JNM	CARLOS MONTEJANO	0.00	0.00	0.00	0.00	<input type="checkbox"/>
Semi-Skilled Laborer	APP	JOSE AVILA	0.00	0.00	0.00	0.00	<input type="checkbox"/>
Semi-Skilled Laborer	JNM	VICTOR HERNANDEZ	0.00	0.00	0.00	0.00	<input type="checkbox"/>
Ironworker	FOR	JAMES STURGEON	0.00	0.00	0.00	0.00	<input type="checkbox"/>

Equipment		Rental Company				Dispute	
Equipment ID	Description	RT Hrs	OT Hrs	ST Hrs	IT Hrs	Remarks	Dispute
Contractor: AMERICAN BRIDGE/FLUOR, A JV							
*E0020562	WELDING EQUIPMENT					No	<input type="checkbox"/>
		0.00	0.00	0.00	0.00		
*E0030562	WELDING EQUIPMENT					No	<input type="checkbox"/>
		0.00	0.00	0.00	0.00		
*E0010562	WELDING EQUIPMENT					No	<input type="checkbox"/>
		0.00	0.00	0.00	0.00		
2292	WELDER, 600 AMP					No	<input type="checkbox"/>
		0.00	0.00	0.00	0.00		
2293	WELDER, 600 AMP					No	<input type="checkbox"/>
		0.00	0.00	0.00	0.00		

04-0120F4 Bid Item: 078 T-L01-ENE.078 Tower Lift 01 External Paint Tower NE
 CERTIFIED COATINGS COMPANY

04-0120F4 Bid Item: 078 T-L05-ENE.078 Tower Lift 05 External Paint Tower NE
 CERTIFIED COATINGS COMPANY

04-0120F4 Bid Item: 078 T-HEA-ENE.078 Tower Head External Paint Tower NE
 CERTIFIED COATINGS COMPANY

CCO-355 Bid Item: 001 0-CIC-EFA.355 CIC - Elevator Impacts - USA Hoist
 AMERICAN BRIDGE/FLUOR, A JV

Attachment



Daily Diary Report by Bid Item


Job Name: 04-0120F4

Inspector Name Liu, Tai-Lin

Diary #: 361

Date: 18-Sep-2014


Thursday

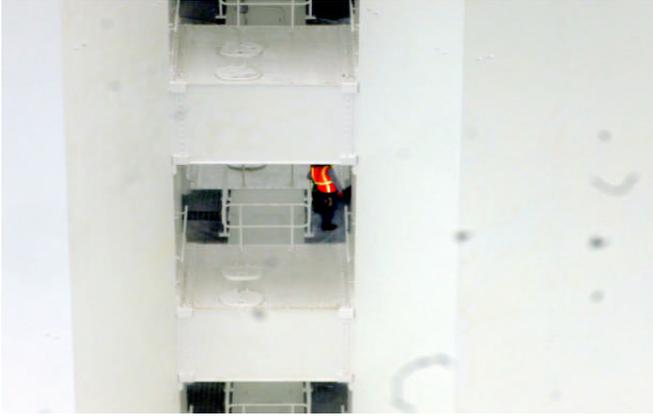

ABF's labor forman James checked paint repair on el. 47m floor area




CCC performed cleaning on elevator railing area (El. 110M)

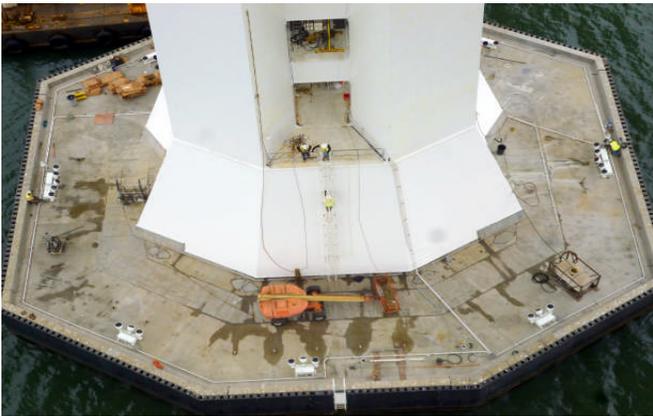

Pictures for tower base view, Awal & METS personnel on the El. 13 area ready to go into tower base area to check anchor rod caulking



Two spiders with three painters worked in elevator rail area between N & W shafts (El. 110m)

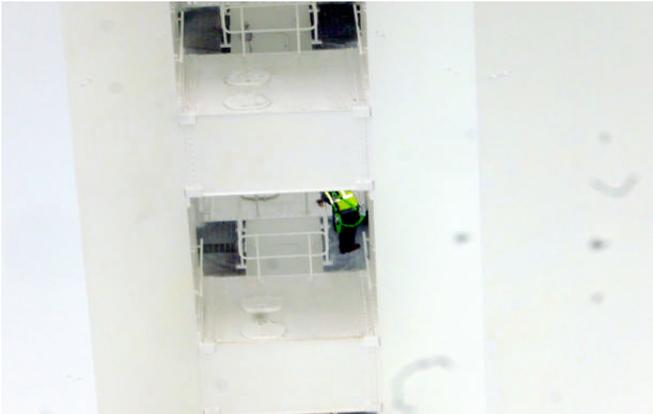

METS paint inspector Stuart at El. 47 m area checking paint repair



Tower El. 53 - 65 m view from east cross beam to west
