



SAS Superstructure

Location: 04-SF-80-13.2 / 13.9

Client Name: CalTrans

Run date 22-Nov-14

Time 9:15 AM

Daily Diary Report by Bid Item

Contract No.: 04-0120F4

Diary #: 362 Const Calendar Day: 837

Date: 19-Sep-2014 Friday

Inspector Name: Liu, Tai-Lin

Title: Transportation Engineer

Inspection Type: Continuous

Shift Hours: 07:00 AM 03:30 PM Break:

Over Time:

Federal ID:

Location:

Reviewer: Awal, Mohammad

Approved Date:

Status: Submit

04-0120F4  
04-SF-80-13.2/13.9  
Self-Anchored  
Suspension Bridge

Weather

Temperature 7 AM 60 - 70 12 PM 70 - 80 4PM 70 - 80

Precipitation Condition Clear

Working Day  If no, explain:

Diary:

Dispute

Tower Activites

CCO # 382 - Tower Painting and Cleaning works (9/19/14, Friday - fine day):

\* Awal talked to me about tower base anchor rod caulking issue this morning, also talked about the same thing with Stanley later on.

\* Studied the paint repair tracking sheet. Went to job site (T1 by driving to W2) and walked to tower deck area El. 53m around 11 AM.

- Saw cross beam entrance door has been fixed by Doanald Plumb yesterday (see picture).

- Saw CCC QC Sage and forman Francisco on the tower El. 53 area. Sage told me three painters continued performing cleaning on the elevator railing area, and two painters in the area between El. 53 to El. 28 performing ladder paint repair. Sage worked 8 hours today and Francico will work two more hours for Sage for tower painting works. Other panters (5) worked 10 hours shift today. BleyCo workers continued working on lighting fixtures on the tower footing area.

\* Paint Crew: Sage Ray(8), Juan Carlos, Luis Ventura, Oscar Salazar, Ramon Gutierrez, Abraham Ventura. Crew worked from 6AM to 4:30 PM, 10 hours shift, Francisco Serrano worked 2 hours on tower today.

\* Labore: James Sturgeon (10 hours) today.

- Left T1 around 12:45PM.

\* Performed paper work at office, and left office around 1:40 PM to Oakland downtown for car accident issue.

04-0120F4		Bid Item: 053		T-L01-DSE.053		Tower Lift 01 Diaphram Tower SE Erect structural steel (bridge tower)		
AMERICAN BRIDGE/FLUOR, A JV								
<b>Labor</b>								
Trade	Class	Name	RT Hrs	OT Hrs	DT Hrs	Total	Remarks	Dispute
<b>Contractor:</b> AMERICAN BRIDGE/FLUOR, A JV								
Ironworker	JNM	DONALD PLUMB	0.00	0.00	0.00	0.00		<input type="checkbox"/>
Ironworker	JNM	PAUL FAMBRINI	0.00	0.00	0.00	0.00		<input type="checkbox"/>
Semi-Skilled Laborer	JNM	FERMIN MEDINA	0.00	0.00	0.00	0.00		<input type="checkbox"/>
Ironworker	GEN	AARON KENT	0.00	0.00	0.00	0.00		<input type="checkbox"/>



## Daily Diary Report by Bid Item

**Job Name:** 04-0120F4    **Inspector Name** Liu, Tai-Lin    **Diary #:** 362    **Date:** 19-Sep-2014    **Friday**

Semi-Skilled Laborer	JNM	LUIS Jimenez	0.00	0.00	0.00	0.00	<input type="checkbox"/>
Semi-Skilled Laborer	JNM	DANNY SCHWARTZ	0.00	0.00	0.00	0.00	<input type="checkbox"/>
Semi-Skilled Laborer	APP	JAVIER MEDINA	0.00	0.00	0.00	0.00	<input type="checkbox"/>
Semi-Skilled Laborer	FOR	GUILLERMO LIMON	0.00	0.00	0.00	0.00	<input type="checkbox"/>
Semi-Skilled Laborer	APP	ROGELIO RODRIGUEZ	0.00	0.00	0.00	0.00	<input type="checkbox"/>
Semi-Skilled Laborer	JNM	CARLOS MONTEJANO	0.00	0.00	0.00	0.00	<input type="checkbox"/>
Semi-Skilled Laborer	APP	JOSE AVILA	0.00	0.00	0.00	0.00	<input type="checkbox"/>
Semi-Skilled Laborer	JNM	VICTOR HERNANDEZ	0.00	0.00	0.00	0.00	<input type="checkbox"/>
Ironworker	FOR	JAMES STURGEON	0.00	0.00	0.00	0.00	<input type="checkbox"/>

Equipment		Rental Company				Dispute	
Equipment ID	Description	RT Hrs	OT Hrs	ST Hrs	IT Hrs	Remarks	Dispute
<b>Contractor:</b> AMERICAN BRIDGE/FLUOR, A JV							
*E0020562	WELDING EQUIPMENT					No	<input type="checkbox"/>
		0.00	0.00	0.00	0.00		
*E0030562	WELDING EQUIPMENT					No	<input type="checkbox"/>
		0.00	0.00	0.00	0.00		
*E0010562	WELDING EQUIPMENT					No	<input type="checkbox"/>
		0.00	0.00	0.00	0.00		
2292	WELDER, 600 AMP					No	<input type="checkbox"/>
		0.00	0.00	0.00	0.00		
2293	WELDER, 600 AMP					No	<input type="checkbox"/>
		0.00	0.00	0.00	0.00		

**04-0120F4    Bid Item: 078    T-L01-ENE.078    Tower Lift 01 External Paint Tower NE**  
 CERTIFIED COATINGS COMPANY

**04-0120F4    Bid Item: 078    T-L05-ENE.078    Tower Lift 05 External Paint Tower NE**  
 CERTIFIED COATINGS COMPANY

**04-0120F4    Bid Item: 078    T-HEA-ENE.078    Tower Head External Paint Tower NE**  
 CERTIFIED COATINGS COMPANY

**CCO-355    Bid Item: 001    0-CIC-EFA.355    CIC - Elevator Impacts - USA Hoist**  
 AMERICAN BRIDGE/FLUOR, A JV

**Attachment**



## Daily Diary Report by Bid Item

Job Name: 04-0120F4

Inspector Name Liu, Tai-Lin

Diary #: 362

Date: 19-Sep-2014


Friday



ABF IRW Donald Plumb fixed door on the cross beam yesterday




Traveler view from El. 53m looking south

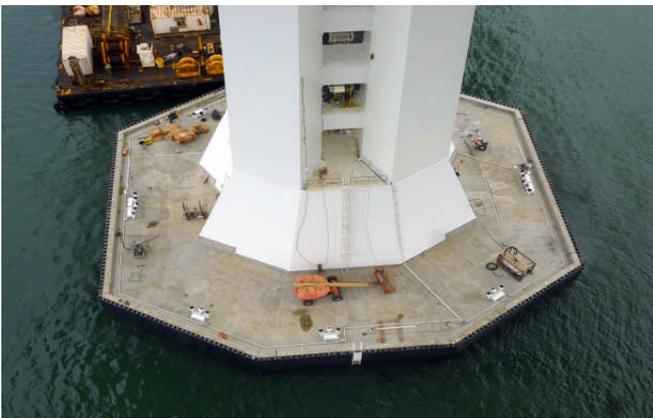

Tower base view from tower El. 53 m cross beam area



Two spiders view from El.53 area looking up

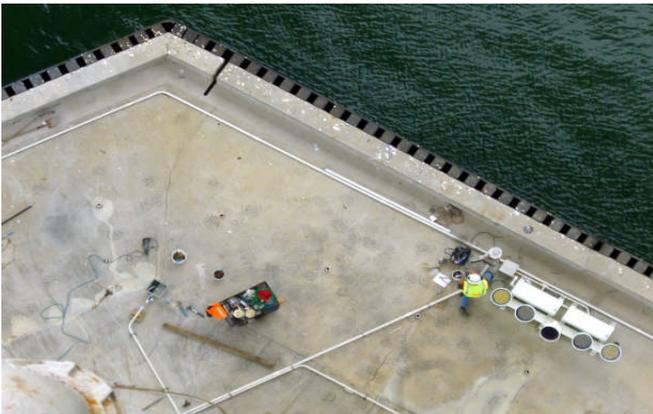

Bleyco workers installed lighting fixtures on tower base area



CCC three painters performed tower elevator railing cleaning (El. 106 m)
