

RESIDENT ENGINEER'S DAILY REPORT
ASST. RESIDENT ENGINEER'S DAILY REPORT

RESIDENT ENGINEER'S SUMMARY REPORT
RESIDENT ENGINEER'S DAILY REPORT
ASST. RESIDENT ENGINEER'S DAILY REPORT

 Contract #: 04-0120F4
 SAS Superstructure
 04-SF-80-13.2 / 13.9


| | | |
|---|------------------------------------|--------------------------|
| Report No: DR-000041 | Working Day Calendar: 223 | Date: 24-Jul-2007 |
| Fabricator: Zhenhua Port Machinery Company, Ltd (ZPMC), Changxing Island | Fabricator Shift Hour: to | |
| Location: Shanghai, China | RE Shift Hour: 0830 to 1700 | |
| Weather: | Temperature: F/ F | |
| Material Description: | | |

Summary:

? I worked on Changxing Island.

? Robert Cuellar and I visited workshop for steel cutting at about 10:15 a.m. Eric told Robert that the flame cutting machine had been down since yesterday and there would be no steel plate cutting at that workshop. Robert and I walked to the area for machine milling to check the condition of surfaces that were milled yesterday. The condition of the surfaces looked good (see photo).

? Robert was told that steel plates for mock up at 89m and 77m would be cut at other workshop. After we arrived at the workshop with Eric of ZPMC, Robert checked steel plate identification. When we were ready to see some cutting, we were told by a technician that the steel transporter was being repair. Again, no cutting.

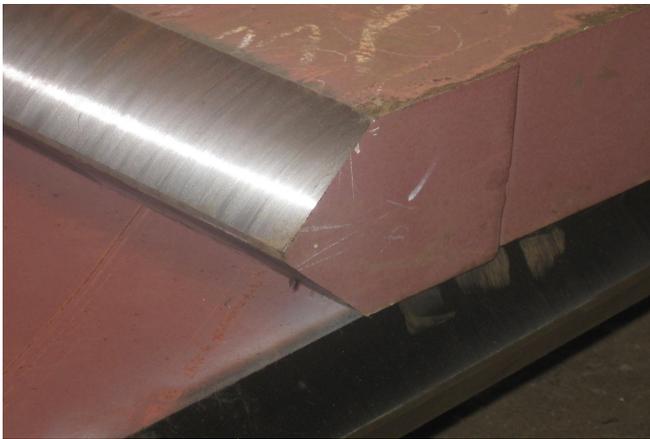

| | | |
|---------------------------------|------------------------------|-------------|
| Prepared By: Ku, Stanley | Sr. Bridge Engineer | 24-Jul-2007 |
| Reviewed By: Tom, Jason | Sup. Transportation Engineer | 01-Aug-2007 |
