

**DEPARTMENT OF TRANSPORTATION****DIVISION OF ENGINEERING SERVICES**

Office of Structural Materials

Quality Assurance and Source Inspection



Bay Area Branch  
690 Walnut Ave. St. 150  
Vallejo, CA 94592-1133  
(707) 649-5453  
(707) 649-5493

Contract #: 04-0120F4Cty: SF/ALA Rte: 80 PM: 13.2/13.9File #: 1.28**WELDING INSPECTION REPORT****Resident Engineer:** Pursell, Gary**Address:** 333 Burma Road**City:** Oakland, CA 94607**Report No:** WIR-014485**Date Inspected:** 26-May-2010**Project Name:** SAS Superstructure**OSM Arrival Time:** 1000**Prime Contractor:** American Bridge/Fluor Enterprises, a JV**OSM Departure Time:** 1830**Contractor:** American Bridge/Fluor Enterprises, a JV**Location:** Job Site

<b>CWI Name:</b>	Jim Cunningham and William She			<b>CWI Present:</b>	<b>Yes</b>	<b>No</b>
<b>Inspected CWI report:</b>	<b>Yes</b>	<b>No</b>	<b>N/A</b>	<b>Rod Oven in Use:</b>	<b>Yes</b>	<b>No</b> <b>N/A</b>
<b>Electrode to specification:</b>	<b>Yes</b>	<b>No</b>	<b>N/A</b>	<b>Weld Procedures Followed:</b>	<b>Yes</b>	<b>No</b> <b>N/A</b>
<b>Qualified Welders:</b>	<b>Yes</b>	<b>No</b>	<b>N/A</b>	<b>Verified Joint Fit-up:</b>	<b>Yes</b>	<b>No</b> <b>N/A</b>
<b>Approved Drawings:</b>	<b>Yes</b>	<b>No</b>	<b>N/A</b>	<b>Approved WPS:</b>	<b>Yes</b>	<b>No</b> <b>N/A</b>
				<b>Delayed / Cancelled:</b>	<b>Yes</b>	<b>No</b> <b>N/A</b>
<b>Bridge No:</b>	34-0006			<b>Component:</b>	Orthotropic Box Girder	

**Summary of Items Observed:**

Caltrans Office of Structural Material (OSM) Quality Assurance Inspector (QAI) Joselito Lizardo was present at the Self Anchored Suspension (SAS) job site as requested to perform observations on the welding of components for the San Francisco Oakland Bay Bridge (SFOBB) Project.

QA randomly observed ABF/JV qualified welders Rory Hogan (ID #3186) perform CJP groove (splice ) back welding fill pass on Orthotropic Box Girder (OBG) L2W/L3W side plate 'E1' outside. The welder was observed back welding in the 4G (overhead) position utilizing a dual shield Flux Cored Arc Welding (FCAW-G) with E71T-1M, 1/16" diameter wire electrode and implementing Caltrans approved Welding Procedure Specification (WPS) ABF-WPS-D15-3110-4. The welder was using a track mounted welder holder assembly that is remotely controlled. The joint being welded has the backing bar gouged using the Esab Plasma Arc machine and was ground smooth. The gouged and ground splice butt joint was also Non Destructive Testing (NDT) tested using the Magnetic Particle Testing (MT). The splice joint was preheated and maintained to greater than 150 degree Fahrenheit using Miller Proheat 35 Induction Heating System located at the other side of the plate prior/during welding. The vicinity was also properly protected from wind and other climatic conditions. During welding, ABF Quality Control (QC) Jim Cunningham was noted monitoring the welding parameters of the welder.


At OBG L1W/L2W edge plate 'B' outside, QA randomly observed new ABF/JV qualified welder Javier Arvizu ID# 2603 perform root pass welding on the splice butt joint. The welder was observed manually welding in the 3G (vertical) position utilizing a dual shield Flux Cored Arc Welding (FCAW-G) with E71T-1M, 1/16" diameter wire electrode and implementing Caltrans approved Welding Procedure Specification (WPS) ABF-WPS-D15-3040B-3. The joint being welded has a single V-groove butt joint with backing bar. The splice

# WELDING INSPECTION REPORT

( Continued Page 2 of 3 )

joint was preheated to greater than 150 degree Fahrenheit using propane gas torch prior welding. During welding, ABF Quality Control (QC) William Sherwood was noted monitoring the welding parameters of the welder. QA randomly monitored the welding parameters with readings 210 amperes, 21.0 voltages. The welder left the job site for some reason and was replaced by another new ABF welder Xiao Jian Wan ID# 9677. Welder Xiao Jian Wan put few fill passes but stopped the welding operation later due to rain.

At OBG L1W/L2W side plate 'E' outside, QA randomly observed ABF/JV qualified welder Jordan Hazelaar perform CJP groove welding repair. The welder was observed welding in the 4G (overhead) position utilizing Shielded metal Arc Welding (SMAW) with 1/8" diameter E7018H4R electrode implementing welding procedure ABF-WPS-D15-1000-Repairs. The repair excavations were preheated to more than 140 degree Fahrenheit using propane gas torch prior welding. During the shift, ABF QC Steven Mc Connell was noted monitoring the welder. Prior welding, ABF QC Steven Mc Connell was also observed performing Magnetic Particle Testing (MT) using Parker Contour Probe with red magnetic powder as detecting media on the repair excavation prior welding. During the shift, the welder has completed six welding repairs that should complete all the repairs outside the plate.

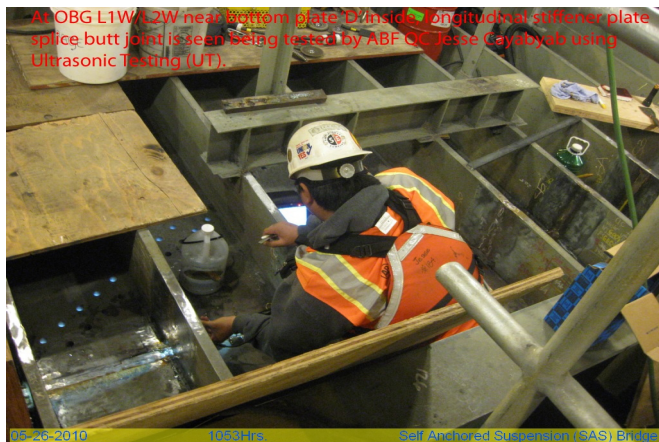

## Summary of Conversations:

As stated above.

## Comments

This report is for the purpose of determining conformance with the contract documents and is not for the purpose of making repair or fit for purpose recommendations. Should you require recommendations concerning repairs or remedial efforts please contact SMR Mohammad Fatemi (916) 227-5298, who represents the Office of Structural

---

## WELDING INSPECTION REPORT

( Continued Page 3 of 3 )

---

Materials for your project.

---

**Inspected By:** Lizardo, Joselito

Quality Assurance Inspector

---

**Reviewed By:** Levell, Bill

QA Reviewer
