

## **Daily Update** July 7

## **Repair Work**

Devil's Slide (post mile 39.14)

- Level 'A' (upper level ocean side) cables that had been stressed once were checked for tension and re-stressed where necessary.
- Level 'B' (lower level ocean side) Drilling for tie backs continued using two rigs. 43 of 58 tie backs now installed. Tie back stressing also continued.



Drilling at level B with reach over rig




Stressing tie backs - level B

• Level 'C' (lower level cliff side) – Tie back stressing continued.



Stressing tie backs - level C

Level 'D' (upper level cliff side) – Drilling for tie backs continued today. 11 of 33 now installed.

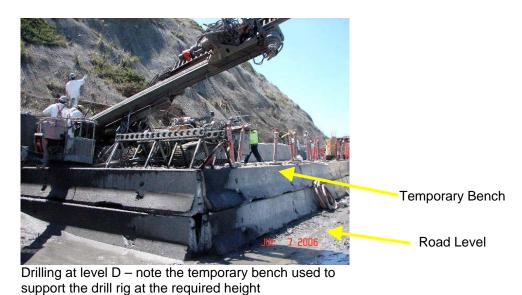

Retaining (micropile) Wall

 Drilling and driving steel piles continued today. The 4 inch diameter steel piles are filled with cement slurry after being driven into the ground. 23 of 99 now installed.
