


**STATE OF CALIFORNIA
DEPARTMENT OF TRANSPORTATION
Contract 0120F – SFOBB – Superstructure
Week ending 2009-01-16**

Tuesday January 13, 2009: Observation via Engineer's Boat between 0930 and 1130 – Clear, Warm (Spring in January?), Light Breeze.

- E2 – West Elevation – Note that approximately 40% of vertical forms have been stripped

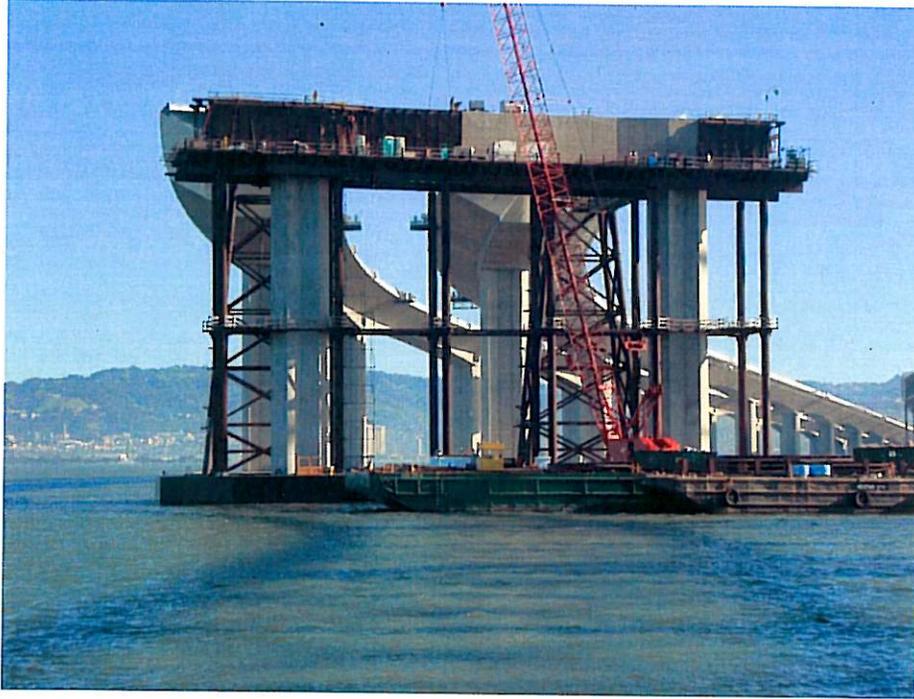


E2 – Eastern Elevation – Approximately 80% of vertical forms have been stripped – note concrete repair (rock pocket) in progress



REC'D '09 JAN 22 H008378


E2 – Clearing PT Conduit @ South End

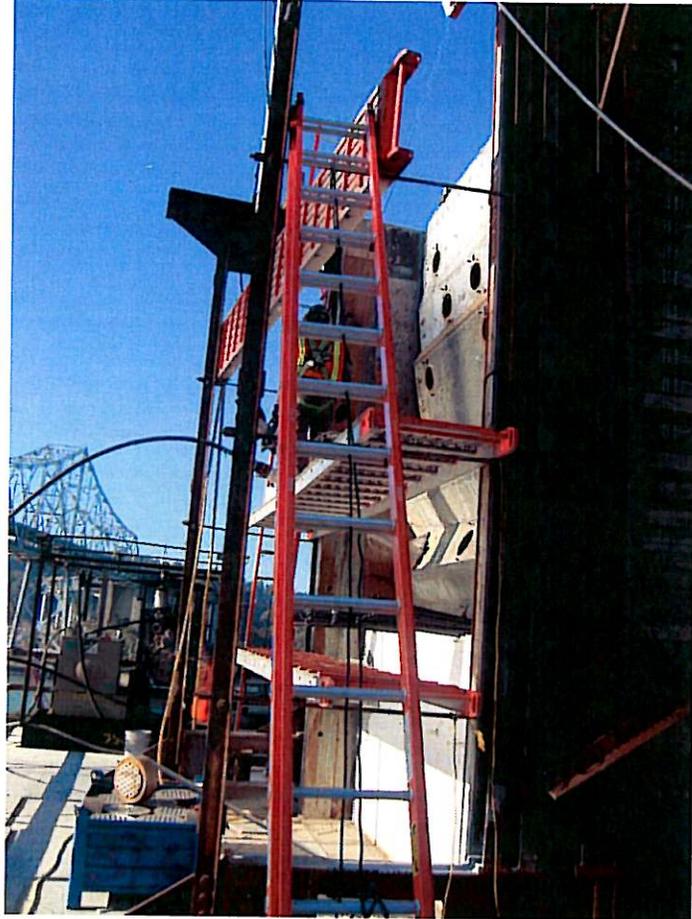


E2 – Inserting PT rods @ North end



E2 – Northerly portion top view from Skyway

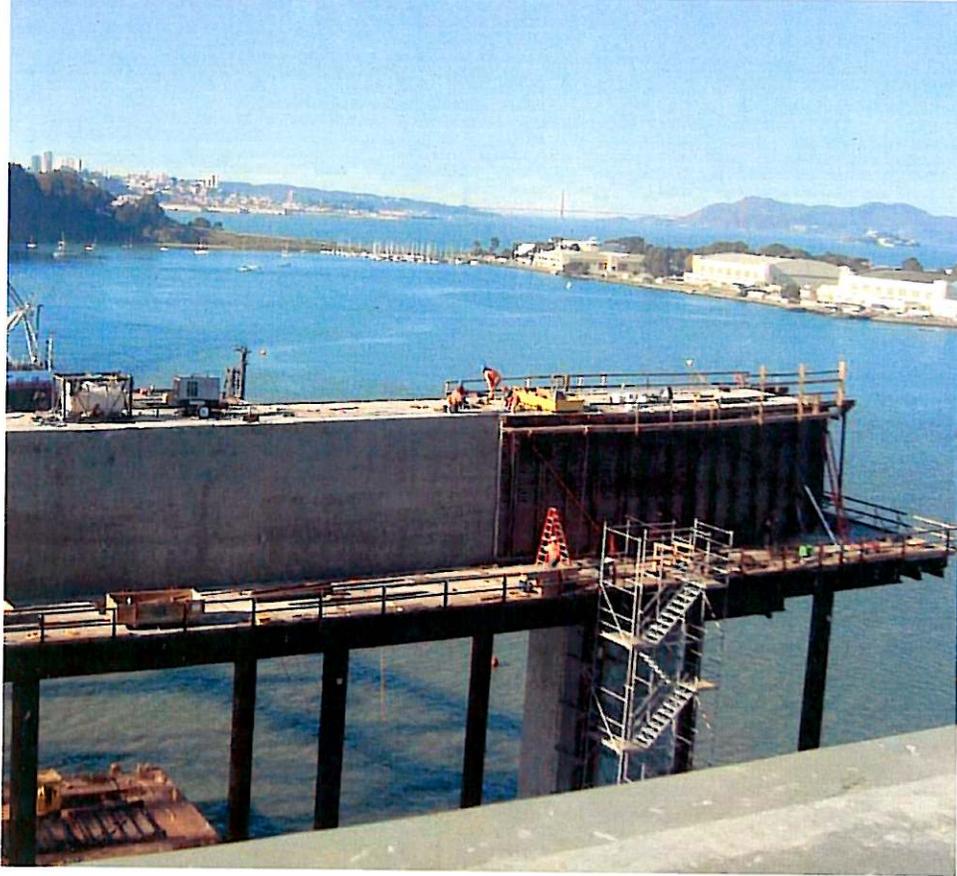

E2 – Southerly portion top view from Skyway

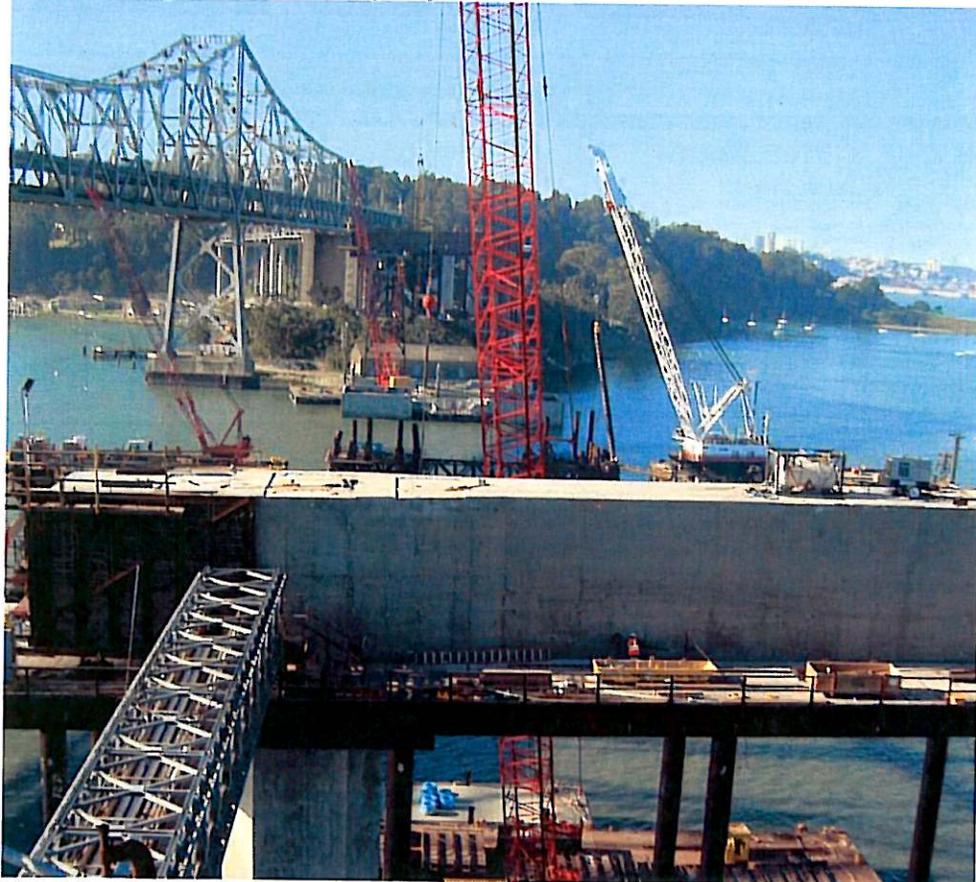

- TT “FW” Foundation – Welding top lift of battered pile



Close-up of welding



Pile prep barge area



View from the West




- **T1 Foundation – Surveying observed**




- **Temporary Truss E-Line in area of TT “CE” – Erection in progress**




Another view of erection of E-Line Temporary Truss near TT "CE"

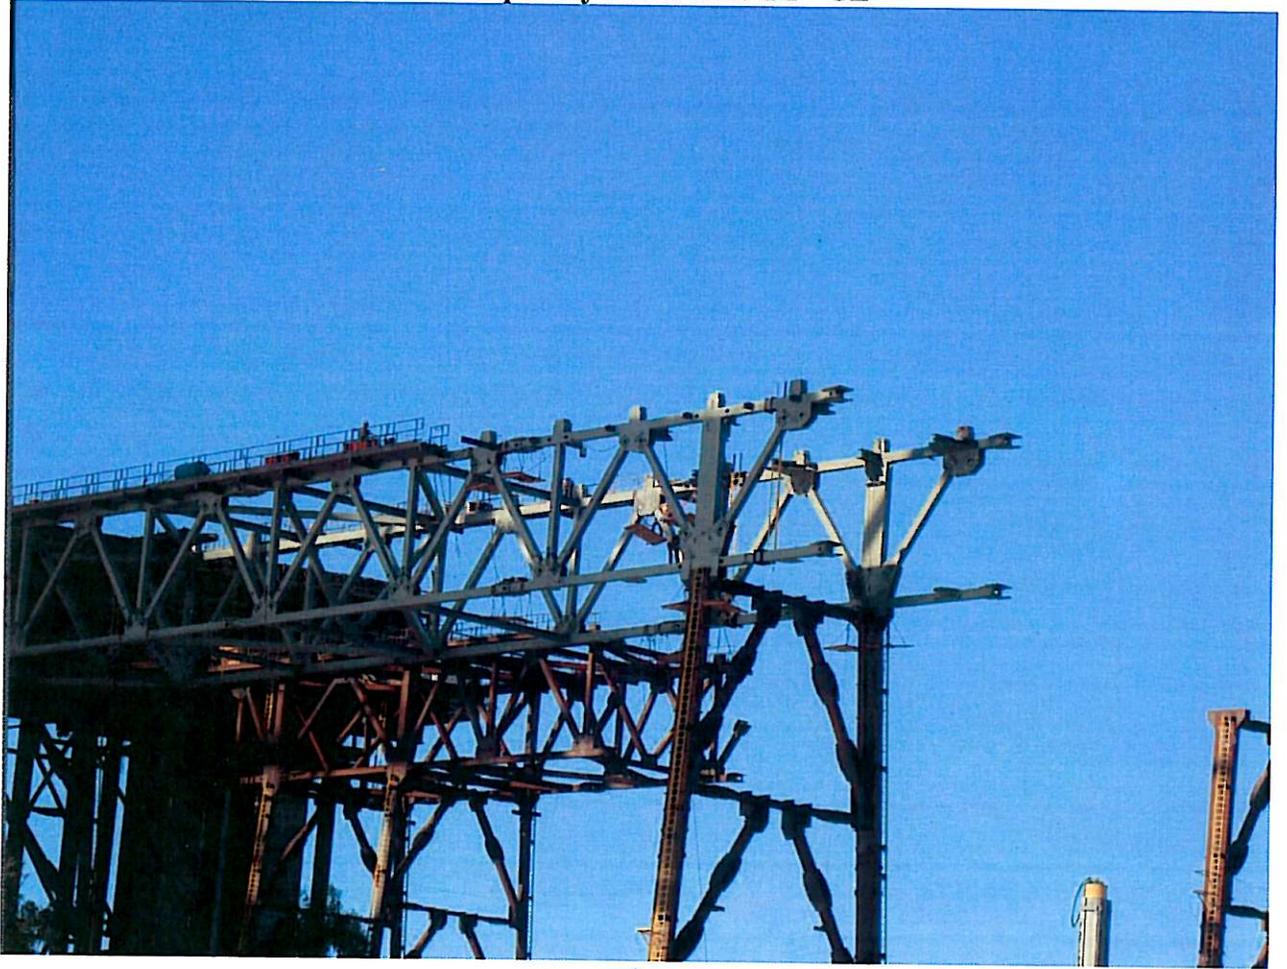


- **Temporary Trusses on barges delivered by ZPMC ship**

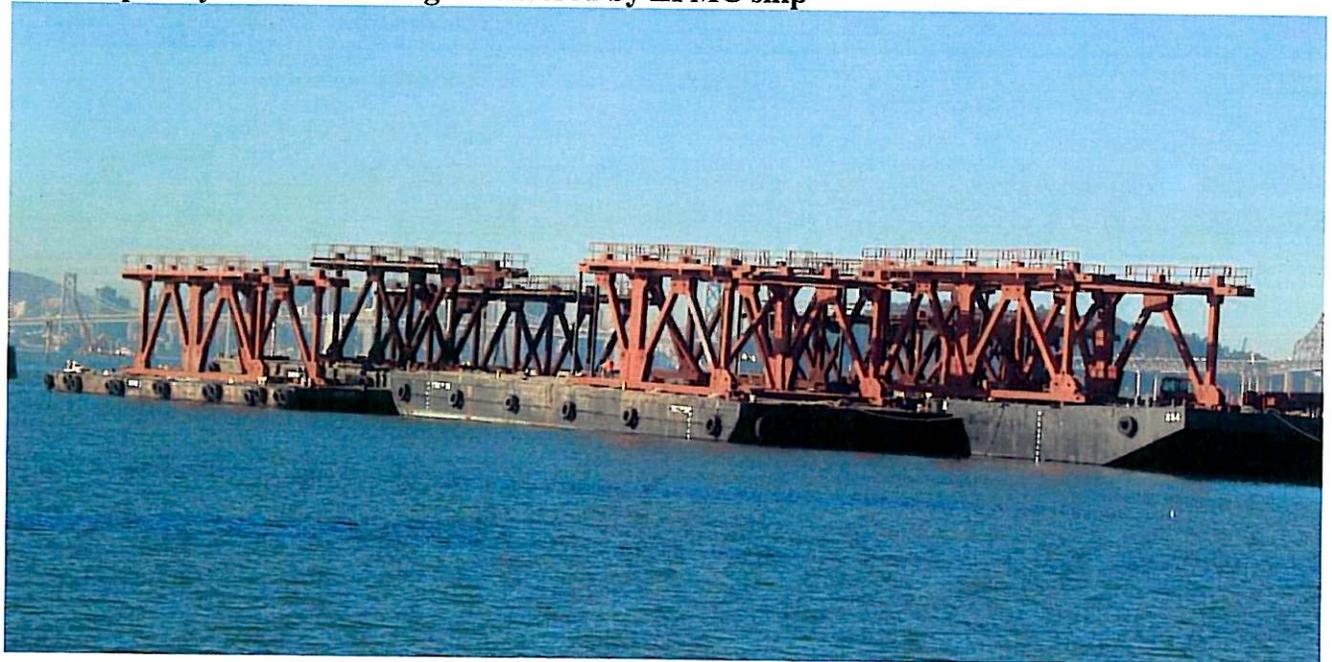

More Temporary Trusses on barges

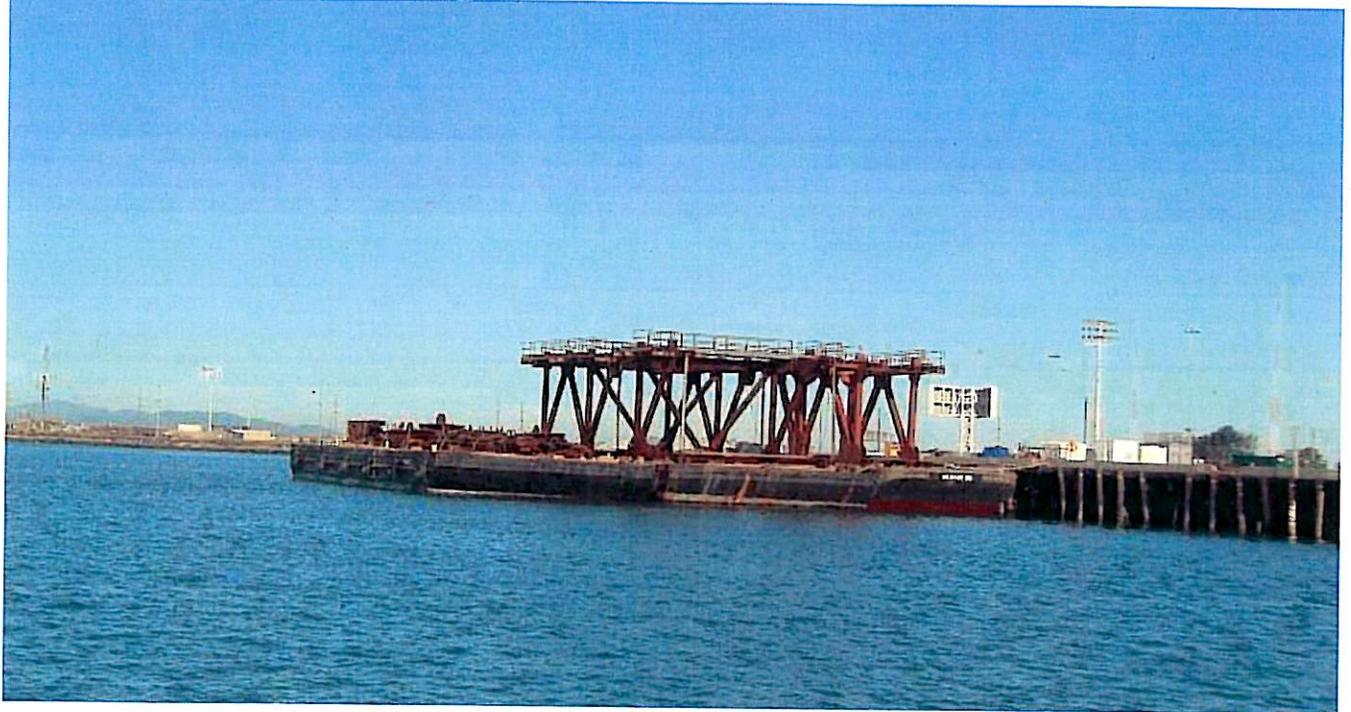

Temporary Towers on Barges

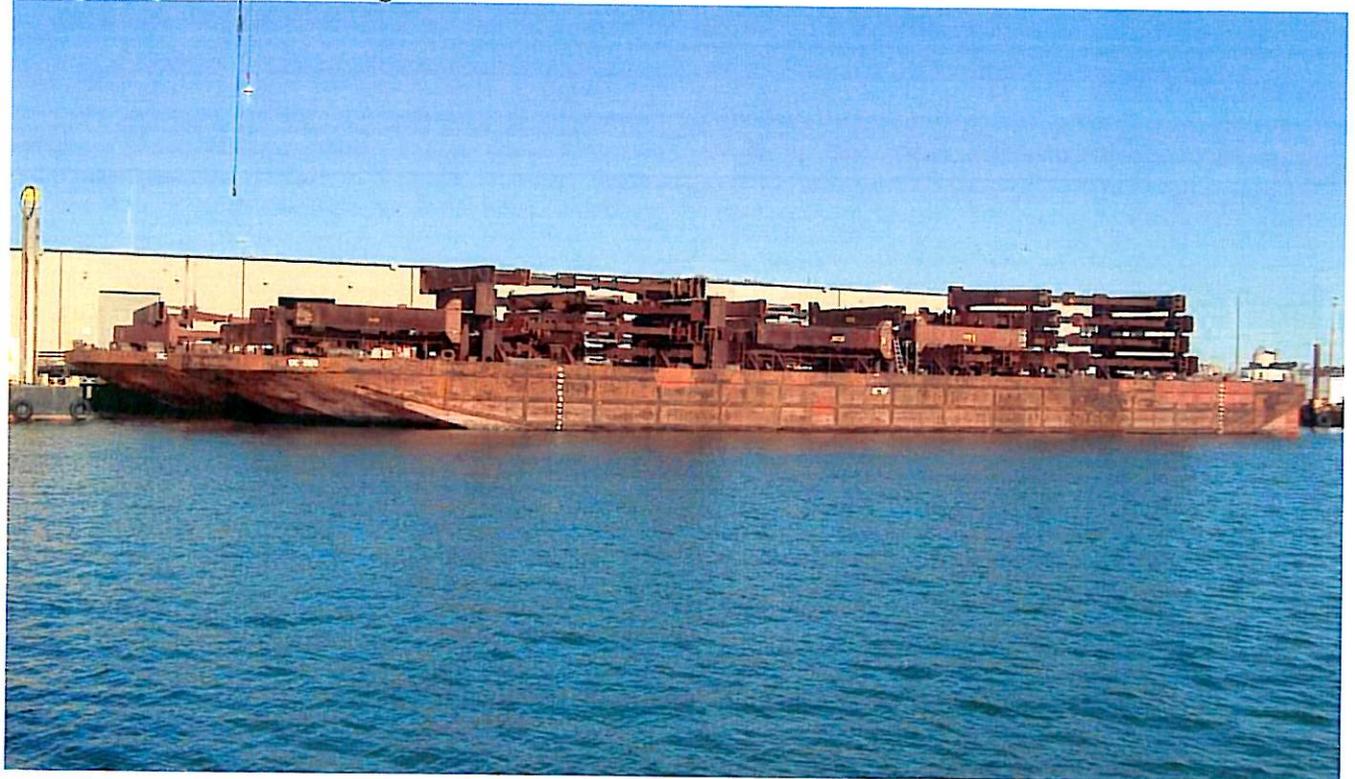

Thursday January 15, 2009 – Observation from Yerba Buena Island between 1300 and 1400; Clear, Warm (warm, dry weather continues), and Calm

- **E2 – West Elevation - Stripping of vertical forms continue**



- **Temporary Tower “F” W-Line: Driving top lift battered piles**



Closer view of pile driving at Temporary Tower “F” W-Line




- **Temporary Truss E-Line @ TT “C” erection**




Another view of Temporary Truss E-Line @ Temp Tower "C"



Temporary Truss W-Line approaching Temp Tower "C" – no activity observed

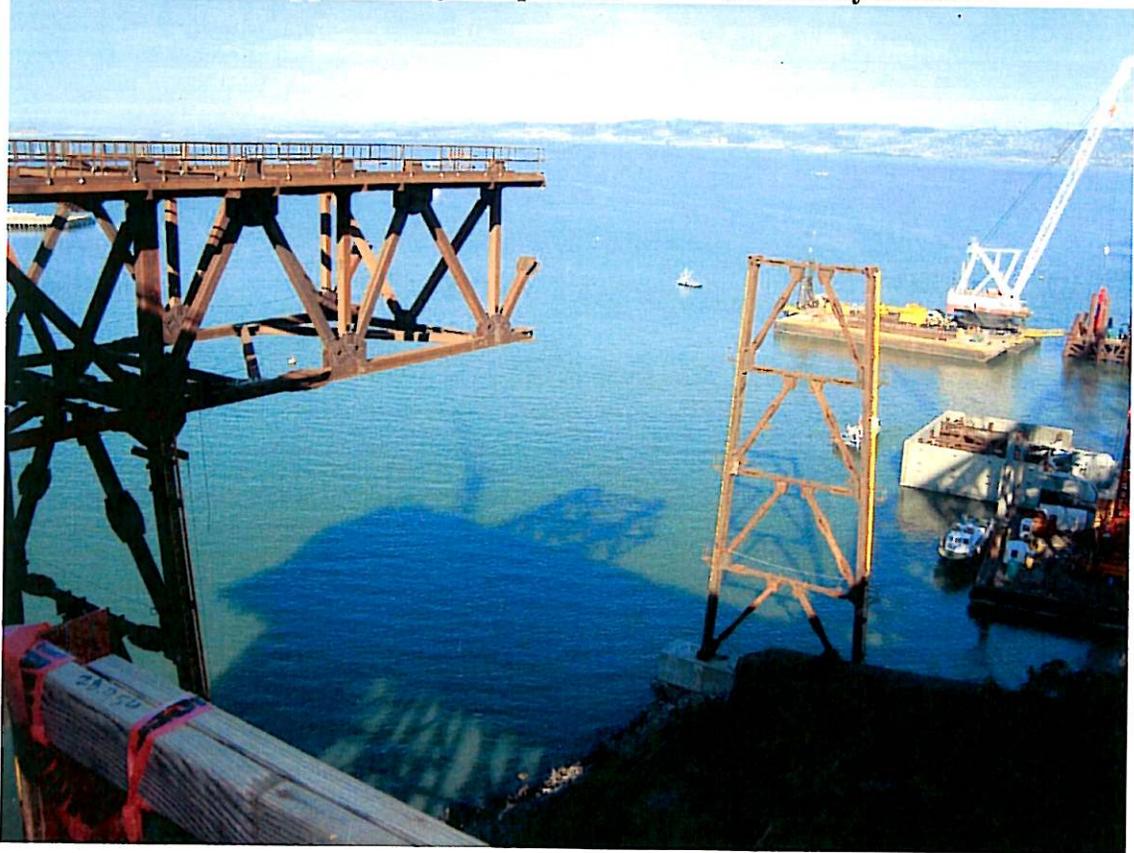

- **W2 – Re-bar installation @ South Pour #6 Area – (East Bound) Pour scheduled for Friday January 30th**

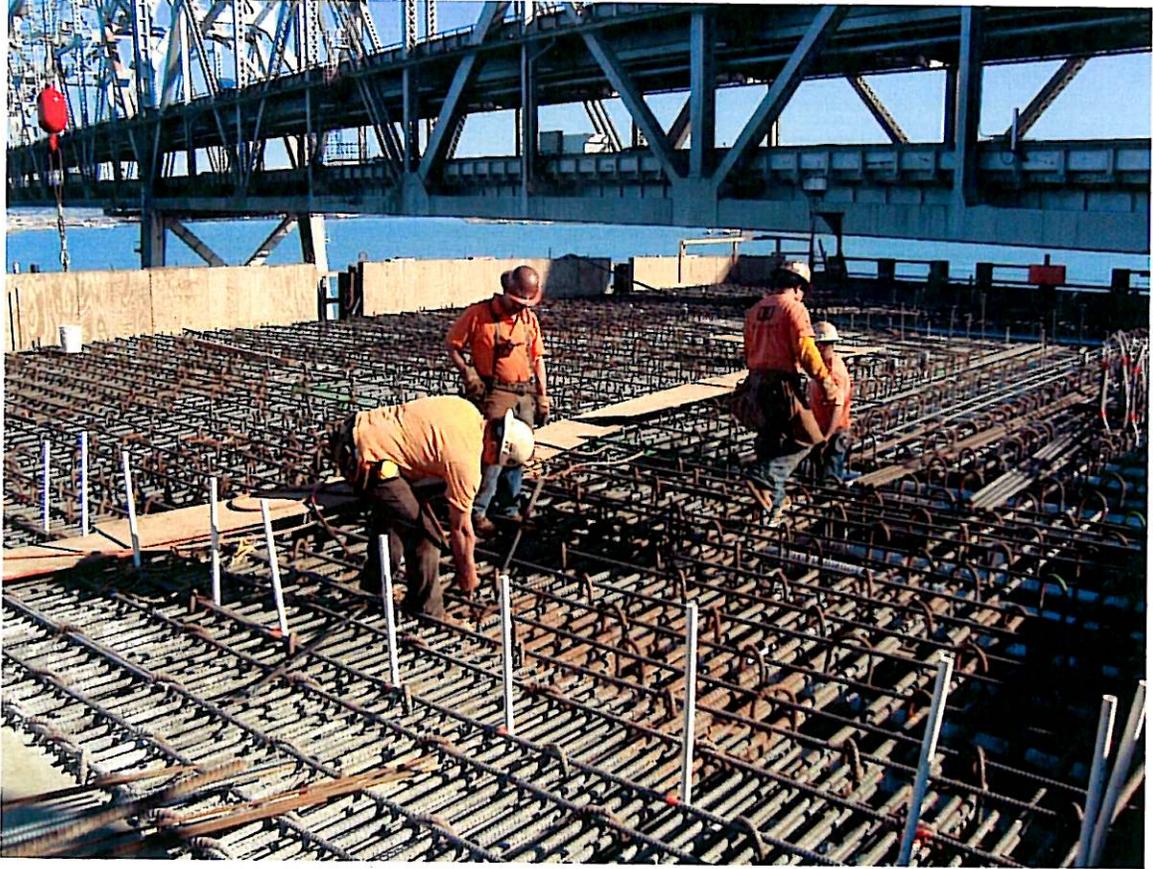

Another view of Pour #6 South Area



Pour # 6 North (West bound) – North / West portion



North East portion of Pour #6 North

