




**STATUS OF PROJECTS
CENTRAL REGION
DISTRICT 06
JANUARY 2006**

DOWNLOAD DATES XPM -01/05/06 PMCS - 01/13/06

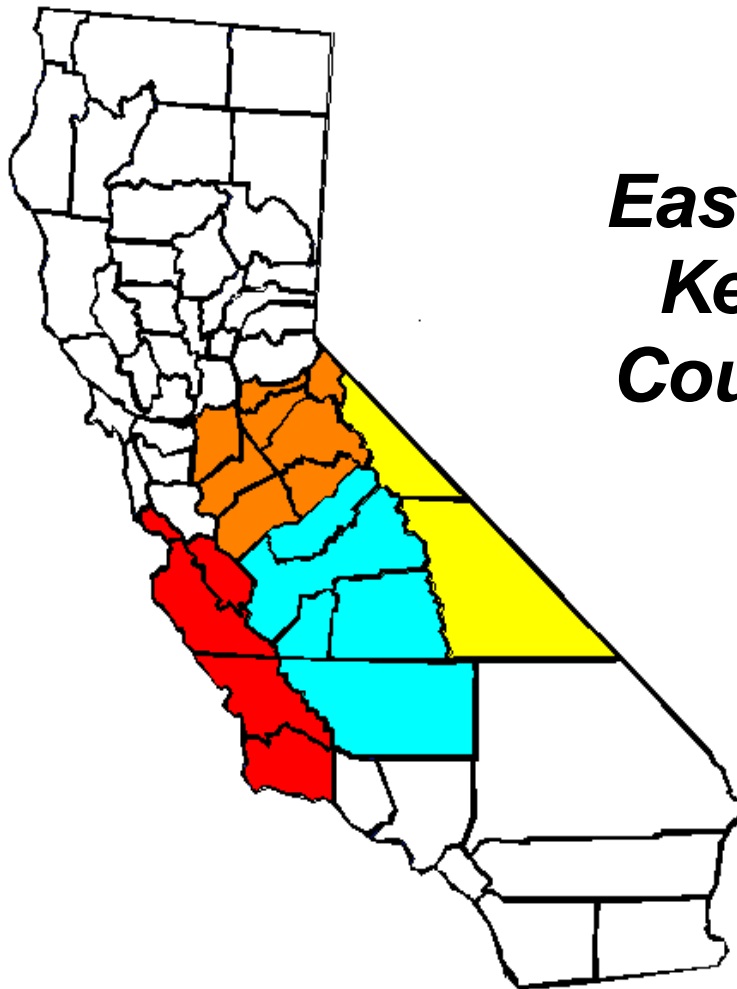

***Eastern
Kern
County***

STATUS INFORMATION AND UPDATE

PUBLIC (559) 243-3434

Internet Address <http://www.dot.ca.gov/dist9/projmgmt/projects.html>

Intra-net Address <http://sv06web/ppm/pmsu/>

2006 STATUS OF PROJECT REVIEW MEETINGS

(All meetings will be held in the respective District at the time & location listed below.)

Version I 01/12/06

FEB 2006	TIME	DISTRICT	Noted Changes
Tues Feb 14th	10:00 am - 12:00 noon	Dist 05 - Atoll Building "Manzanita" Room 1150 Laurel Lane	
Thurs Feb 16th	9:00 am - 12:00 noon	Dist 06 - Fresno Room #145 - "Yosemite" Room 2015 E. Shields Ave., Suite 100	
Wed Feb 22nd	9:00 am - 12:00 noon	Dist 10 - Stockton Room #56 / 71 - "Stanislaus" Room (in the basement) 1976 E. Charter Way	
Thurs Feb 23rd	8:00 am - 10:30 am	Dist 09 - Bishop Room #109 - "Mt. Whitney" Room 500 Main Street	
APR 2006	TIME	DISTRICT	Noted Changes
Tues Apr 11th	10:00 am - 12:00 noon	Dist 05 - Atoll Building "Manzanita" Room 1150 Laurel Lane	
Thurs Apr 13th	9:00 am - 12:00 noon	Dist 06 - Fresno Room #145 - "Yosemite" Room 2015 E. Shields Ave., Suite 100	
Mon Apr 17th	1:00 pm - 4:00 pm	Dist 10 - Stockton Room #56 / 71 - "Stanislaus" Room (in the basement) 1976 E. Charter Way	
Thurs Apr 20th	8:00 am - 10:30 am	Dist 09 - Bishop Room #109 - "Mt. Whitney" Room 500 Main Street	
JUN 2006	TIME	DISTRICT	Noted Changes
Tues Jun 6th	10:00 am - 12:00 noon	Dist 05 - Atoll Building "Manzanita" Room 1150 Laurel Lane	
Thurs Jun 8th	9:00 am - 12:00 noon	Dist 06 - Fresno Room #145 - "Yosemite" Room 2015 E. Shields Ave., Suite 100	
Mon Jun 12th	1:00 pm - 4:00 pm	Dist 10 - Stockton Room #56 / 71 - "Stanislaus" Room (in the basement) 1976 E. Charter Way	
Thurs Jun 15th	8:00 am - 10:30 am	Dist 09 - Bishop Room #109 - "Mt. Whitney" Room 500 Main Street	

Note: Any changes from the previous schedule are shown bold and on the right of the meeting date listed.

2006 STATUS OF PROJECT REVIEW MEETINGS

(All meetings will be held in the respective District at the location listed below.)

Version I 01/12/06

AUG 2006	TIME	DISTRICT	Noted Changes
Tues Aug 1st	10:00 am - 12:00 noon	Dist 05 - Atoll Building "Manzanita" Room 1150 Laurel Lane	
Thurs Aug 3rd	9:00 am - 12:00 noon	Dist 06 - Fresno Room #145 - "Yosemite" Room 2015 E. Shields Ave., Suite 100	
Tues Aug 8th	1:00 pm - 4:00 pm	Dist 10 - Stockton Room #56 / 71 - "Stanislaus" Room (in the basement) 1976 E. Charter Way	
Thurs Aug 10th	8:00 am - 10:30 am	Dist 09 - Bishop Room #109 - "Mt. Whitney" Room 500 Main Street	
OCT 2006	TIME	DISTRICT	Noted Changes
Tues Oct 10th	10:00 am - 12:00 noon	Dist 05 - Atoll Building "Manzanita" Room 1150 Laurel Lane	
Thurs Oct 12th	9:00 am - 12:00 noon	Dist 06 - Fresno Room #145 - "Yosemite" Room 2015 E. Shields Ave., Suite 100	
Mon Oct 16th	1:00 pm - 4:00 pm	Dist 10 - Stockton Room #56 / 71 - "Stanislaus" Room (in the basement) 1976 E. Charter Way	
Thurs Oct 19th	8:00 am - 10:30 am	Dist 09 - Bishop Room #109 - "Mt. Whitney" Room 500 Main Street	
DEC 2006	TIME	DISTRICT	Noted Changes
Tues Dec 5th	1:00 pm - 4:00 pm	Dist 10 - Stockton Room #56 / 71 - "Stanislaus" Room (in the basement) 1976 E. Charter Way	
Thurs Dec 7th	8:00 am - 10:30 am	Dist 09 - Bishop Room #109 - "Mt. Whitney" Room 500 Main Street	
Mon Dec 11th	10:00 am - 12:00 noon	Dist 05 - Atoll Building "Manzanita" Room 1150 Laurel Lane	
Thurs Dec 14th	9:00 am - 12:00 noon	Dist 06 - Fresno Room #145 - "Yosemite" Room 2015 E. Shields Ave., Suite 100	

Note: Any changes from the previous schedule are shown bold and on the right of the meeting date listed.

LEGEND

INFORMATION FIELDS

Updates to Schedules
 Up-to-date Cost Estimates
 PM (Project Manager) Assignments
 DM (PJD-Design Manager) Assignments
 DM (MTC D5 -Design Mgr) Assignments
 DM (MTC D6 -Design Mgr) Assignments
 DM (MTC D9 -Design Mgr) Assignments
 DM (MTC D10 -Design Mgr) Assignments
 EM (Environmental Mgr) Assignments
 CM (Construction Mgr) Assignments
 Project Name
 Program Box (Right-hand upper box)
 Co-Rte-PM, description
 Phase Completion
 Comments Box

PERSON RESPONSIBLE FOR DATA ENTRY

Project Manager (directly into FMPro)
 Project Manager updates to PMCS contact
 Single Focal Point (SFP) for District (updates to Lisa Jackson)
 Samer Shaath, Calnet 8-425-3802
 Kelly McClain, Calnet 8-629-3278
 Bill Moses, Calnet 8-421-6514
 John Fox, Calnet 8-627-5207
 Alvin Mangindin, Calnet 8-423-7300
 Catherine Yim, Calnet 8-425-8258
 Eddie Wirawan, 559-445-6467, Calnet 8-421-6467
 Project Manager
 Teresa Rix, Calnet 8-425-3433
 PMCS group
 Project Managers (update in FMP)
 Project Managers

CONTACTS

D5 SFP	Tim Gubbins	Calnet 8-629-3113
D5 Program Manager	Val Houdyshell	" 8-629-3069
D6 SFP	Mike Rastegar	" 8-425-3421
D6 Program Manager	Teresa Rix	" 8-425-3433
D9 SFP	Craig Holste	" 8-627-5211
D9 Program Mgr (SHOPP/Minor)	Brian McElwain	" 8-627-4361
D10 SFP	Dennis T. Agar	" 8-423-6192
D10 Program Manager	Robert Nguyen	" 8-423-7988
CR SFP	Malcolm Dougherty	" 8-425-3420
CR Resource Manager	Nabeelah Hanif	" 8-425-3463
CR Program Manager	Teresa Rix	" 8-425-3433
CR PMSU Manager	Said Ismail	Calnet 8-425-3461
XPM Contact	Sami Shwiyhat (CR & D10)	" 8-425-3440
	Danny Dibyantoro (D5, D6 & D9)	" 8-425-3439
PMCS/Doc Coord Contact	Andrea Senan (D6)	" 8-425-3434
	Linda Araujo (D5 & D9)	" 8-425-3431
	Lydia Gomez (D10)	" 8-425-3435
Website/GIS Coord	Sarah Lesnikowski	" 8-425-3453
FMP/APL Coordinator	Lisa Jackson	" 8-425-3425
Website Development	Tony Hunt	" 8-425-8059
	Ilham Khachadourian	8-423-3436

ACRONYMS

APL	Approved Project List
CR	Central Region
FMP	File Maker Pro
LCO	Local Capital Outlay
NBSSR	Noise Barrier Scope Summary Report
PDS	Project Development Support
PID	Project Initiation Document
PMCS	Project Management Control System
PMSU	Project Management Support Unit
TEA	Transportation Enhancement Activities

PROGRAM BOX DEFINITIONS

TRAMS	Transportation Accounting Management System
TCRP	Transportation Congestion Relief Program
BR#	Bill Reference Number
XPM	Expert Project Management
Phase "PID"	Candidate with approved PID
Phase "Candidate"	Candidate without "PID"
PDS	Project Development Support
G13	Resourced for Support Costs (SHOPP projects only)

Programmed Projects

Delivery Plan:

Milestones that are tracked by HQ in the Delivery Plan for the current FY. In July of each year, HQ PM sets a new baseline that reflects XPM on 7/9/xxxx.

Approved Line:

Schedule at the time of programming and any approved changes, aka PCR/PCD. CR Document Coordinators update the schedule when either the district or HQ approves a PCR/PCD. PDS projects should have an approved line that matches the SB45 components that are programmed. When a project completes the PID phase and is still pending programming, we copy the current schedule into the approved line until the project is programmed.

Current Line:

Schedule at the time of preparing the Status of Projects. PM has the ability to change the schedule at any given time.

XPM Milestone Information	PA & ED M200	Bridge Site to Struc M221	Maps to Survey M224	Reg R/W M225	Struc PS&E to Dist M378	District PS&E to HQ M380	R/W Cert M410	RTL M460	HQ Advertise M480	Appr Const Cont M500	Contract Accept M600
Delivery Plan	10/1/2005										
Approved	4/1/2006		6/22/2005	4/1/2006		11/15/2007	3/1/2008	3/15/2008	4/15/2008	7/15/2008	7/15/2009
Current	4/1/2006	T	6/22/2005	A 4/1/2006	T	11/15/2007	T 3/1/2008	T 3/15/2008	T 4/15/2008	T 7/15/2008	T 7/15/2009

PROGRAM CODE SUMMARY

Program Code	Description
025.500	Grandfathered Interregional Improvement Program – IIP
025.700	New Programming Interregional Improvement Program – IIP
075.400	Grandfathered Regional Improvement Program - RIP
075.600	New Programming Regional Improvement Program - RIP
201.010	Safety Improvements (HB1)
201.015	Collision Severity Reduction (HB1-C.U.R.E.)
201.020	Upgrade Median Barrier (HB1)
201.110	Bridge Rehabilitation (HA21)
201.111	Bridge Scour Mitigation (HA21)
201.112	Bridge Rail Replacement/Upgrade (HA21)
201.114	Bridge Widening (HA21)
201.115	Bridge Preservation (HA21)
201.120	Roadway Rehabilitation (HA22)
201.121	Pavement Rehabilitation (HA22 – CAPM)
201.122	Pavement Preservation (HA22 – CAPM)
201.125	Long-Life Pavement Corridors (HA22)
201.130	Major Damage Restoration (HA23)
201.150	Roadway Protective Betterment (HA42)
201.151	Drainage System Restoration
201.170	Signs and Lighting Rehabilitation (HA22)
201.210	Highway Planting Restoration (HA25)
201.220	New Highway Planting (HB32)
201.230	Freeway Maintenance Access (HA28)
201.240	Roadside Enhancement (HB34)
201.245	Beautification and Modernization (HB34)
201.250	Safety Roadside Rest Area Restoration (HA26)
201.260	New Safety Roadside Rest Areas (HB33)
201.310	Operational Improvements (HB4N)
201.315	Transportation Management Systems (HB4N)
201.321	Weigh Stations and WIM Facilities
201.325	Railroad/Highway At-Grade Crossing
201.351	Equipment Facilities (HA11)
201.352	Maintenance Facilities (HA12)
201.353	Office Facilities
201.354	Materials Labs
201.361	ADA New Curb Ramps (HB71)
204.735	TEA – Caltrans Share from TEA 21 (SHOPP TEA)
204.736	TEA – Caltrans Share from TEA 21 by Others (Regional TEA)
400.000	Locally Funded State Highway Project
600.620	Local Roads
600.624	State Highway Improvements by Local Agencies
600.645	Intermodal Facilities
600.675	RSTP/CMAQ Matching Funds
710.870	Traffic Congestion Relief Program TCRP

**STATUS OF PROJECTS
INDEX BY E/A
District 06**

January 17, 2006

E/A	PAGE	E/A	PAGE	E/A	PAGE	E/A	PAGE	E/A	PAGE	E/A	PAGE
0A630_	9										
0A760_	10										
0C350_	13										
0C430_	14										
0E690_	1										
24340_	8										
24342_	7										
32880_	10										
33160_	9										
33190_	11										
33230_	12										
39320_	2										
39680_	2										
40840_	6										
41470_	11										
42550_	5										
43020_	3										
44310_	4										
45710_	3										
46300_	5										
48080_	13										
48790_	6										
49360_	14										

STATUS OF PROJECTS COUNTY, ROUTE AND POST MILE INDEX District 06

January 17, 2006

CO	ROUTE	POST MILE	E/A	PAGE	PHASE	DESCRIPTION	TYPE OF WORK
KER	0	L5719	39680_	2	PID	NEAR TEHACHAPI CONSTRUCT NEW MAINTENANCE STATION.	CONSTRUCT NEW MAINTENANCE STATION
CACHE CREEK							
KER	14	11.5/ 12.8	33160_	9	MINOR	IN KERN CO ON RTE 14 FROM 1.04 KM SOUTH TO 1.12KM NORTH OF SILVER QUEEN ROAD (KP 18.51/20.60)	EMERGENCY PCC SLAB REPAIR
EMERGENCY SLAB							
KER	14	16.2/ 26.6	40840_	6	Construction	IN KERN COUNTY IN AND NEAR MOJAVE AT VARIOUS LOCATIONS	WIDEN HIGHWAY
NORTH MOJAVE 4-LANE							
KER	14	35.5/ 37.1	43020_	3	PA&ED	NEAR CANTIL FROM ROGERS ROAD TO 0.3 KILOMETER SOUTH OF CANTIL WASH BRIDGE #50-424 (KPX057.1-X059.7)	"RAISE GR., AC OVERLAY, WIDENING"
SOUTH REDROCK REHAB							
KER	14	35.8/ 40.2	0C350_	13	MAINT.	IN KERN COUNTY AT VARIOUS LOCATIONS	SEAL COAT
PME CHIPS ON RTES KER							
KER	14	45.9/ 62.3	45710_	3	PA&ED	NEAR RIDGECREST FROM REDROCK INYOKERN RD TO RTE 178 (KP 73.9/100.3)	CONSTRUCT 4 LN EXPRESSWAY W/CONTROL ACCESS
Freeman Gulch 4-Lane							
KER	14	46.2/ 50.8	39320_	2	PID	NEAR CANTIL FROM 1.8 KM N TO 9.2 KM N OF RED ROCK-INYOKERN RD (KP 74.3/81.8)	AC OVERLAY & WIDEN SHOULDERS
LITTLE DIXIE WASH							
KER	58	77/ 82.6	48080_	13	MAINT.	IN KERN COUNTY NEAR KEENE FROM 0.1 KM WEST OF CALIENTE AND BEALVILLE ROAD TO TEHACHAPI CREEK BRIDGE OVERHEAD	CHIP SEAL
KER	58	82.7/ 90.7	48790_	6	Construction	IN KERN COUNTY NEAR TEHACHAPI FROM TEHACHAPI BRIDGE OVERHEAD TO 2.5 KM WEST OF TEHACHAPI CREEK BRIDGE AND FROM 1.6 KM WEST OF ROUTE 58 AND 202 SEPARATION TO ROUTE 58 AND 202	CONCRETE BARRIER & ASPHALT CONCRETE
GOLDEN HILLS MEDIAN							
KER	58	R92.1/R93.2	42550_	5	PS&E/RW	IN TEHACHAPI AT DENNISON RD BR #50-0339 (KP R148.3/R150.0)	REPLACE OC W/4-LANE OC & CONSTRUCT PARTIAL CLOVERLEAF INTERCHANGE
DENNISON ROAD							
KER	58	105.5/	0A630_	9	MINOR	IN KERN COUNTY AT THE CACHE CREEK WEIGHT STATION AT HIGHWAY 58. (KP 169.750)	IMPROVING WEIGHT STATION.
CACHE CREEK WEIGHT							
KER	58	R107.7/R118	24340_	8	CLOSEOUT	IN KERN COUNTY AT MOJAVE FROM 0.2 KM EAST OF CACHE CREEK BRIDGE TO 6.7 KM EAST OF AIRPORT ROAD	CONSTRUCT 4 LANE FREEWAY
MOJAVE BYPASS							
KER	58	M108.9/M108.9	33190_	11	MINOR	IN KERN COUNTY NEAR MOJAVE AT BUSINESS ROUTE 58 WEST OVERCROSSING (KP 175.27)	INSTALL WINDSCREENS
WINDSCREEN							
KER	58	109.1/ 117.1	24342_	7	Construction	IN KERN COUNTY AT MOJAVE FROM 0.2 KM EAST OF CHCHE CREEK BRIDGE TO 5.4 KM EAST OF AIRPORT ROAD	PAVEMENT REHABILITATION
Old 58 Relinquishment							
KER	58	138.7/	0A760_	10	MINOR	ON RTE 58 NEAR BORON AT THE BORON SRRA EB AND WB (KP 223.8)	SEWER CONSTRUCTION
CONSTRUCT SEWER LINE							
KER	58	R139/	46300_	5	PS&E/RW	IN KERN CO AT THE BORON SAFETY ROAD SIDE REST AREA (E/B AND W/B) (KP R223.7)	REHAB EB AND WB SAFETY ROADSIDE REST AREAS
Boron SRRA Rehab							
KER	58	R139/R143.8	0C430_	14	MAINT.	IN KERN COUNTY NEAR BORON AT VARIOUS LOCATIONS	RUBBERIZED ASPHALT CONCRETE OVERLAY
AR GGAC ON KER 58 NEAR							
KER	58	139/	33230_	12	MINOR	PM RTE 58 NEAR BORAON AT THE BORON SRAA EB/WB (KP 223.7)	EMERGENCY WELL REHAB
WATER WELL REHAB AT							
KER	65	6.1/ 25.2	49360_	14	MAINT.	IN KERN COUNTY NEAR BAKERSFIELD AT VARIOUS LOCATIONS	CHIP SEAL AND DIGOUTS
KER	178	72.8/ 73.1	41470_	11	MINOR	NEAR WALKER PASS FROM 3.4 KM W TO 3.9 KM W OF CHIMNEY CREEK RD (KP 117.2/117.6)	RAISE GRADE AND CONSTRUCT A WATER CUTOFF WALL
WALKER PASS DRAINAGE							
KER	178	90.4/ 92.3	32880_	10	MINOR	IN KERN COUNTY FROM 0.5 MI EAST OF SIERRA VISTA ROAD TO BROADWAY STREET (KP 145.48/148.53)	SHOULDER WIDENING
SHOULDER WIDENING IN							
KER	395	0/ 14.7	0E690_	1	Candidate	SR 395 FROM THE SAN BERNADINO/KERN COUNTY LINE TO SOUTH CHINA LAKE BLVD IN KERN COUNTY	WIDEN SHOULDERS TO 8 FT AND INSTALL SHOULDER'S RUMBLE STRIP
Searles Valley Shoulder							

**STATUS OF PROJECTS
COUNTY, ROUTE AND POST MILE INDEX
District 06**

January 17, 2006

CO	ROUTE	POST MILE	E/A	PAGE	PHASE	DESCRIPTION	TYPE OF WORK
KER	395	14.8/ 23	44310_	4	PA&ED	ON SR 395 FROM 0.4 KM S OF CHINA LAKE RD TO 0.3 KM S OF RTE 178 (KP 23.8/37.0)	2C TO 4E
INYOKERN 4-LANE							

SHOPP CANDIDATES

(State Highway Operation and Protection Program)

Projects listed in this section are in the Planning Phase (“K” phase) to develop Project Initiation Documents (Project Study Report or Project Scope Summary Report, aka PSR or PSSR)



Caltrans Central Region Project Initiation Document (PID) Status Report

XPM Download 1/5/2006

PMCS Download 1/13/2006

1	Dist-EA	Phase	County-Route-Post Mile	PPNO	Project Name	Project Phase	Program Information				
	06-0E690_	K	KER - 395 - 0/ 14.7		SEARLES VALLEY SHOULDER WIDENING	Candidate	XPM	Yes	Delivery	APL	Yes
							Plan		List		
Location Description SR 395 FROM THE SAN BERNADINO/KERN COUNTY LINE TO SOUTH CHINA LAKE BLVD IN KERN COUNTY							Work Description WIDEN SHOULDERS TO 8 FT AND INSTALL SHOULDER'S RUMBLE STRIP				
Project Documents							Right of Way Info				
Env State _____ Act _____							Parcels _____ Utilities _____ 0				
Env Federal _____ Act _____							Structure Est _____ \$0				
							District Est _____ \$8,800				
							Total Con Est _____ \$8,800				
							R/W Est _____ \$0				
PM Frank Momen PH# (559) 243-3444							Agreements				
DM Martin Nishikawa PH# (559) 230-3122							Type Agency Name Date				
EM Gail Miller PH# (559) 243-8222											
CM Roger Henderson PH# (661) 395-2569											
Milestone Information							PID & Workplan Approved				
PID Initiated							Percent Complete				
Purpose & Need Defined											
Scope, Limits & Alternatives Defined											
Drafts PID & Cost Estimate											
Target _____							_____				
Completed _____							_____				
Project Comments											

SHOPP PID

*(State Highway Operation and Protection Program
Project Initiation Document)*

Projects listed in this section have an approved Project Initiation Document and are awaiting programming or updating for future cycles



Caltrans Central Region Project Status Report

XPM Download 1/5/2006

PMCS Download 1/13/2006

Dist-EA	Phase	County-Route-Post Mile	PPNO	Project Name	Project Phase
2 06-39680	0	KER -0 -L5719	3095	CACHE CREEK MAINTENANCE STATION	PID

Location Description

NEAR TEHACHAPI CONSTRUCT NEW MAINTENANCE STATION.

Work Description

CONSTRUCT NEW MAINTENANCE STATION

ROW Info
 Parcels 5
 Utilities 4
Program Information
 XPM ☒ Yes Delivery ☒ Plan ☒ APL ☒ No
 Program SHOPP Status Active Doc Yr 2006

Prog Code 201.352 Prog FY Const \$\$ RW \$\$

Funds Req Date CTC Vote Date

Component Funding

	RIP	IIP	LOCAL	OTHER
CAPT				
SUPT				

Phase Completion

PA&ED 100% RW 3% PS&E 40% CON %

Project Documents
 Env State ND Act 11/08/2001
 Env Federal FI Act
 PID Appr 9/27/2000
 Project Rpt 5/4/2004
***Escalated Cost Estimate**
 Structure Est \$7,758
 District Est \$1,649
 Total Con Est \$9,407
Current Cost Estimate
 Structure Est \$7,100
 District Est \$1,509
 Total Con Est \$8,609
 R/W Est \$1,345
Agreements

PM	PH#	Type	Agency Name	Date
Frank Momen	(559) 243-3444			
Gurbhay Brar	(559) 230-3106			
Gail Miller	(559) 243-8222			
Roger Henderson	(661) 395-2569			

XPM Milestone Information	PA & ED M200	Bridge Site to Struc M221	Maps to Survey M224	Reg R/W M225	Struc PS&E to Dist M378	District PS&E to HQ M380	R/W Cert M410	RTL M460	HQ Advise M480	Appr Const Cont M500	Contract Accept M600
Delivery Plan											
Approved	12/21/2001	12/1/2006	1/1/2007		8/1/2008	10/1/2008	10/1/2008	1/1/2009	3/1/2009	6/1/2009	12/1/2010
Current	12/21/2001A	12/1/2006 T	1/1/2007 T		8/1/2008 T	10/1/2008 T	10/1/2008 T	1/1/2009 T	3/1/2009 T	6/1/2009 T	12/1/2010 T

Project Comments

G13 PROJECT

Dist-EA	Phase	County-Route-Post Mile	PPNO	Project Name	Project Phase
3 06-39320	K	KER -14 - 46.2/ 50.8	8045	LITTLE DIXIE WASH REHAB	PID

Location Description

NEAR CANTIL FROM 1.8 KM N TO 9.2 KM N OF RED AC OVERLAY & WIDEN ROCK-INYOKERN RD (KP 74.3/81.8)

Work Description

SHOULDERS

ROW Info
 Parcels 12
 Utilities 0
Program Information
 XPM ☒ Yes Delivery ☒ Plan ☒ APL ☒ No
 Program SHOPP Status Active Doc Yr 2006

Prog Code 201.120 Prog FY Const \$\$ RW \$\$

Funds Req Date CTC Vote Date

Component Funding

	RIP	IIP	LOCAL	OTHER
CAPT				
SUPT				

Phase Completion

PA&ED 100% RW 100% PS&E 95% CON %

Project Documents
 Env State ND Act 01/24/2000
 Env Federal EX Act 01/24/2000
 PID Appr 9/3/1997
 Project Rpt 1/24/2000
***Escalated Cost Estimate**
 Structure Est \$0
 District Est \$7,276
 Total Con Est \$7,276
Current Cost Estimate
 Structure Est \$0
 District Est \$6,659
 Total Con Est \$6,659
 R/W Est \$272
Agreements

PM	PH#	Type	Agency Name	Date
Frank Momen	(559) 243-3444			
Scott Shaver	(559) 230-3118			
Juergen Vespermann	(559) 243-8157			
Roger Henderson	(661) 395-2569			

XPM Milestone Information	PA & ED M200	Bridge Site to Struc M221	Maps to Survey M224	Reg R/W M225	Struc PS&E to Dist M378	District PS&E to HQ M380	R/W Cert M410	RTL M460	HQ Advise M480	Appr Const Cont M500	Contract Accept M600
Delivery Plan											
Approved	1/24/2000					10/1/2008	1/1/2009	1/1/2009	3/1/2009	6/1/2009	7/1/2010
Current	1/24/2000 A					10/1/2008 T	1/1/2009 T	1/1/2009 T	3/1/2009 T	6/1/2009 T	7/1/2010 T

Project Comments

This project is PS&E complete. The project has not been delivered to District Office Engineer. This project is a shelf project without capital funding.

PA&ED PHASE

Project Approval
(PA&ED Milestone)



Caltrans Central Region PA&ED Status Report

XPM Download 1/5/2006

PMCS Download 1/13/2006

4	Dist-EA	Phase	County-Route-Post Mile	PPNO	Project Name	Project Phase
	06-43020_	0	KER -14 - 35.5/ 37.1	0357	SOUTH REDROCK REHAB	PA&ED
Location Description			Work Description			ROW Info
NEAR CANTIL FROM ROGERS ROAD TO 0.3 KILOMETER SOUTH OF CANTIL WASH BRIDGE #50-424 (KPX057.1-X059.7)			"RAISE GR., AC OVERLAY, WIDENING"			Parcels 35 Utilities 1
Project Documents			*Escalated Cost Estimate		Current Cost Estimate	
Env State ND Act			Structure Est \$0		Structure Est \$0	
Env Federal EX Act			District Est \$14,570		District Est \$12,945	
PID Appr 11/3/1994			Total Con Est \$14,570		Total Con Est \$12,945	
Project Rpt			R/W Est \$1,039			
Agreements						
PM Frank Momen		PH# (559) 243-3444	Type	Agency Name	Date	
DM Scott Shaver		PH# (559) 230-3118				
EM Juergen Vespermann		PH# (559) 243-8157				
CM Roger Henderson		PH# (661) 395-2569				
Program Information						
XPM	In XPM	Delivery Plan	APL	No		
Doc Yr	Program	Status				
2006	SHOPP	Active				
Component	Funding					
Funds Req Date	CTC Vote Date					
Prog Code	Prog FY	Const \$\$	RW \$\$			
201.120						
RIP	IIP	LOCAL	OTHER			
CAPT						
SUPT						
Phase Completion						
PA&ED	30 %	RW	%	PS&E	%	CON

XPM Milestones	Begin Env M020	NOP M030	Circulate DED M120	Approve FED M160	PA & ED M200	Bridge Site to Struc M221	Maps to Survey M224	Reg R/W M225	R/W Cert M410	RTL M460	Contract Accept M600
Delivery Plan											
Approved	7/1/2000		5/1/2002		1/1/2005		1/1/2005	6/1/2005	1/1/2007	1/1/2007	7/1/2008
Current					7/1/2006 T		6/1/2007 T	10/1/2007 T	7/1/2009 T	7/1/2009 T	7/1/2011 T

Project Comments

Pending Issues/Risks.
B.O. by F&W Service in Ventura.
On 6/24/02 - FHWA submitted BA to FWS.

5	Dist-EA	Phase	County-Route-Post Mile	PPNO	Project Name	Project Phase
	06-45710_	0	KER -14 - 45.9/ 62.3	8042	FREEMAN GULCH 4-LANE	PA&ED
Location Description			Work Description			ROW Info
NEAR RIDGECREST FROM REDROCK INYOKERN RD TO RTE 178 (KP 73.9/100.3)			CONSTRUCT 4 LN EXPRESSWAY W/CONTROL ACCESS			Parcels 388 Utilities 2
Project Documents			*Escalated Cost Estimate		Current Cost Estimate	
Env State ND Act			Structure Est		Structure Est \$2,216	
Env Federal FI Act			District Est		District Est \$78,249	
PID Appr 9/14/2001			Total Con Est		Total Con Est \$80,465	
Project Rpt			R/W Est \$13,818			
Agreements						
PM Frank Momen		PH# (559) 243-3444	Type	Agency Name	Date	
DM Scott Shaver		PH# (559) 230-3118				
EM Juergen Vespermann		PH# (559) 243-8157				
CM Roger Henderson		PH# (661) 395-2569				
Program Information						
XPM	In XPM	Delivery Plan	APL	Yes		
Doc Yr	Program	Status				
2002	STIP	Programmed				
Component	Funding					
PDS	IIP, RIP					
Funds Req Date	CTC Vote Date					
Prog Code	Prog FY	Const \$\$	RW \$\$			
075.600		\$0	\$0			
RIP	IIP	LOCAL	OTHER			
CAPT	\$0	\$0				
SUPT	\$2,286	\$1,520				
Phase Completion						
PA&ED	60 %	RW	%	PS&E	%	CON

XPM Milestones	Begin Env M020	NOP M030	Circulate DED M120	Approve FED M160	PA & ED M200	Bridge Site to Struc M221	Maps to Survey M224	Reg R/W M225	R/W Cert M410	RTL M460	Contract Accept M600
Delivery Plan											
Approved					10/1/2007			1/1/2008			
Current	7/20/2002 A		10/1/2006 T		10/1/2007 T						

Project Comments

The project is programmed for PA&ED only. This project is a MOU project between the counties of Mono, Inyo, and Kern. Funding source is a combination of IIP and RIP monies. The State's IIP contribution is 40% or \$1,524,000, and the combined counties RIP contribution is 60% or 2,286,000 for a total cost of \$3,810,000 to achieve PA&ED phase. The schedule for the remaining phases will be determined after the Alternative is selected and the funding has been identified.



Caltrans Central Region PA&ED Status Report

XPM Download 1/5/2006

PMCS Download 1/13/2006

6	Dist-EA	Phase	County-Route-Post Mile	PPNO	Project Name	Project Phase	Program Information				
	06-44310_	0	KER -395 - 14.8/ 23	8539	INYOKERN 4-LANE	PA&ED	XPM	In XPM	Delivery Plan	Yes	APL List
Location Description		Work Description		ROW Info							
ON SR 395 FROM 0.4 KM S OF CHINA LAKE RD TO 0.3 KM S OF RTE 178 (KP 23.8/37.0)		2C TO 4E		Parcels 74 Utilities 0							
Project Documents		*Escalated Cost Estimate		Current Cost Estimate							
Env State ND Act		Structure Est		Structure Est \$8,000							
Env Federal FI Act		District Est		District Est \$38,800							
PID Appr 9/4/2001		Total Con Est		Total Con Est \$46,800							
Project Rpt				R/W Est \$4,200							
PM Frank Momen		PH# (559) 243-3444		Agreements							
DM Scott Shaver		PH# (559) 230-3118		Type							
EM Juergen Vespermann		PH# (559) 243-8157		Agency Name							
CM Roger Henderson		PH# (661) 395-2569		Date							
							Phase Completion				
							PA&ED 65 % RW % PS&E % CON %				

XPM Milestones		Begin Env	NOP	Circulate	Approve	PA & ED	Bridge Site	Maps to	Reg R/W	R/W Cert	RTL	Contract
		M020	M030	DED	FED	M200	to Struc	Survey	M225	M410	M460	Accept
				M120	M160		M221	M224				M600
Delivery Plan												
Approved		10/1/2002		2/1/2005	8/1/2005	7/1/2008			5/1/2009			
Current		10/1/2002 A		7/1/2007 T	7/1/2008 T	7/1/2008 T						

Project Comments

This project is programmed or PA&ED only. This project is a MOU project between the counties of Mono, Inyo, and Kern. Funding source is a combination of IIP and RIP monies. The State's IIP contribution is 40% or \$800,000, and the combined country RIP contribution is 60% or 1,200,000 for a total cost of \$2,000,000 to achieve PA&ED. The schedule for the remaining phases will be determined after the Alternative is selected and the funding has been identified.

PS&E AND R/W PHASE

Develop Project

(RTL Milestone)



Caltrans Central Region Project Status Report

XPM Download 1/5/2006

PMCS Download 1/13/2006

7	Dist-EA	Phase	County-Route-Post Mile	PPNO	Project Name	Project Phase
	06-42550_	1	KER -58 -R92.1/R93.2	3482	DENNISON ROAD IMPROVEMENTS	PS&E/RW
Location Description			Work Description			ROW Info
IN TEHACHAPI AT DENNISON RD BR #50-0339 (KP R148.3/R150.0)			REPLACE OC W/4-LANE OC & CONSTRUCT PARTIAL CLOVERLEAF INTERCHANGE			Parcels 8 Utilities 5
Project Documents			*Escalated Cost Estimate			Current Cost Estimate
Env State	CE	Act 07/28/2003	Structure Est			Structure Est \$4,521
Env Federal	EX	Act 07/28/2003	District Est			District Est \$6,350
PID Appr	5/19/2000		Total Con Est			Total Con Est \$10,871
Project Rpt	6/30/2003		R/W Est			\$632
PM Frank Momen			PH# (559) 243-3444			Type
DM Khaled Daher			PH# (559) 230-3130			Agency Name
EM Juergen Vespermann			PH# (559) 243-8157			Date
CM Roger Henderson			PH# (661) 395-2569			
Agreements						
Phase Completion						
PA&ED 100% RW % PS&E 70% CON %						

XPM Milestone Information	PA & ED M200	Bridge Site to Struc M221	Maps to Survey M224	Reg R/W M225	Struc PS&E to Dist M378	District PS&E to HQ M380	R/W Cert M410	RTL M460	HQ Advrtise M480	Appr Const Cont M500	Contract Accept M600
Delivery Plan											
Approved	10/1/2003			3/1/2004							
Current	7/28/2003	A 1/20/2004	A 4/9/2004	A	4/1/2006	T 6/1/2006	T				

Project Comments

The project is programmed for PA&ED and PS&E only. The schedule for the remaining phases will be determined after the Alternative is selected and the funding has been identified.

8	Dist-EA	Phase	County-Route-Post Mile	PPNO	Project Name	Project Phase
	06-46300_	1	KER -58 -R139/	3495	BORON SRRA REHAB	PS&E/RW
Location Description			Work Description			ROW Info
IN KERN CO AT THE BORON SAFETY ROAD SIDE REST AREA (E/B AND W/B) (KP R223.7)			REHAB EB AND WB SAFETY ROADSIDE REST AREAS			Parcels Utilities 0
Project Documents			*Escalated Cost Estimate			Current Cost Estimate
Env State	CE	Act 03/24/2004	Structure Est \$6,283			Structure Est \$6,100
Env Federal	EX	Act 03/24/2004	District Est \$4,980			District Est \$4,835
PID Appr	10/15/2001		Total Con Est \$11,263			Total Con Est \$10,935
Project Rpt	8/3/2004		R/W Est			\$0
PM Frank Momen			PH# (559) 243-3444			Type
DM Lori Butler			PH# (559) 230-3134			Agency Name
EM Gail Miller			PH# (559) 243-8222			Date
CM Roger Henderson			PH# (661) 395-2569			
Agreements						
Phase Completion						
PA&ED 100% RW % PS&E 0% CON %						

XPM Milestone Information	PA & ED M200	Bridge Site to Struc M221	Maps to Survey M224	Reg R/W M225	Struc PS&E to Dist M378	District PS&E to HQ M380	R/W Cert M410	RTL M460	HQ Advrtise M480	Appr Const Cont M500	Contract Accept M600
Delivery Plan											
Approved	8/1/2004	4/1/2005	8/31/2004	7/1/2005	9/1/2005	11/1/2005	1/1/2006	1/1/2006	3/1/2006	7/1/2006	11/1/2007
Current	7/29/2004	A 8/31/2004	A		6/1/2006	T 9/1/2006	T 11/1/2006	T 1/1/2007	T 3/1/2007	T 7/1/2007	T 7/1/2009

Project Comments

8/26/02-No work will be done on this project during FY 03 for resource recovery.-JCH
7/15/02-Schedule moved out 1 yr to coincide with Prog FY.
4/4/02-Programmed in 2002 SHOPP, FY 5/6
12/11/01-Project listed on 2nd draft of 2002 SHOPP.

CONSTRUCTION PHASE

Procure Construction

(CCA Milestone)



Caltrans Central Region Project Status Report

XPM Download 1/5/2006

PMCS Download 1/13/2006

Dist-EA	Phase	County-Route-Post Mile	PPNO	Project Name	Project Phase
9	06-48790_	1 KER -58 - 82.7/ 90.7	3496	GOLDEN HILLS MEDIAN BARRIER	Construction

Location Description				Work Description		ROW Info	
IN KERN COUNTY NEAR TEHACHAPI FROM TEHACHAPI BRIDGE OVERHEAD TO 2.5 KM WEST OF TEHACHAPI CREEK BRIDGE AND FROM 1.6 KM WEST OF ROUTE 58 AND 202 SEPARATION TO				CONCRETE BARRIER & ASPHALT CONCRETE		Parcels	
						Utilities	0

Project Documents			*Escalated Cost Estimate		Current Cost Estimate	
Env State	CE	Act 11/13/2003	Structure Est		Structure Est	\$0
Env Federal	EX	Act 11/13/2003	District Est		District Est	\$4,775
PID Appr	7/23/2003		Total Con Est		Total Con Est	\$4,775
Project Rpt	1/6/2004				R/W Est	\$0

Agreements		
Type	Agency Name	Date
RR	BNSF	090304

PM	PH#	PH#
Frank Momen	(559) 243-3444	
Martin Nishikawa	(559) 230-3122	
Gail Miller	(559) 243-8222	
Roger Henderson	(661) 395-2569	

Program Information												
XPM	Yes	Delivery Plan	Yes	APL	Yes							
Program	SHOPP	Status	Programmed	Doc Yr	2002A							
Prog Code	201.010	Prog FY	2005	Const \$\$	\$4,022	RW \$\$	\$0					
Funds Req Date	9/30/2004	CTC Vote Date	11/8/2004									
Component	Funding											
CAPT	RIP	IIP	LOCAL	OTHER								
SUPT												
Phase Completion												
PA&ED	100 %	RW		PS&E		CON						

XPM Milestone Information	PA & ED M200	Bridge Site to Struc M221	Maps to Survey M224	Reg R/W M225	Struc PS&E to Dist M378	District PS&E to HQ M380	R/W Cert M410	RTL M460	HQ Advise M480	Appr Const Cont M500	Contract Accept M600
Delivery Plan											
Approved	1/1/2004		10/1/2004	11/1/2004		10/1/2004	12/1/2004	1/1/2005	4/1/2005	6/1/2005	7/1/2006
Current	1/6/2004 A					9/30/2004 A	8/5/2004 A	11/5/2004 A	12/20/2004 A	3/10/2005 A	7/1/2006 T

Project Comments

PID developed by Scott Shaver. PR developed by Nick Chan. PS&E developed by Martin Nishikawa. The project is in two segments.
 Segment 1-PM 82.71/R87.07
 Segment 2-PM R89.75/R90.72.
 The project is due to cross median accident and also due to gap closure.

Dist-EA	Phase	County-Route-Post Mile	PPNO	Project Name	Project Phase
10	06-40840_	1 KER -14 - 16.2/ 26.6	8010	NORTH MOJAVE 4-LANE	Construction

Location Description				Work Description		ROW Info	
IN KERN COUNTY IN AND NEAR MOJAVE AT VARIOUS LOCATIONS				WIDEN HIGHWAY		Parcels	184
						Utilities	3

Project Documents			*Escalated Cost Estimate		Current Cost Estimate	
Env State	ND	Act 01/03/2003	Structure Est		Structure Est	\$4,535
Env Federal	FI	Act 01/03/2003	District Est		District Est	\$45,670
PID Appr	2/2/1999		Total Con Est		Total Con Est	\$50,205
Project Rpt	12/13/2002				R/W Est	\$7,719

Agreements		
Type	Agency Name	Date
CAH	COUNTY OF KERN	050105
COP	COUNTY OF KERN	

PM	PH#	PH#
Frank Momen	(559) 243-3444	
Scott Shaver	(559) 230-3118	
Juergen Vespermann	(559) 243-8157	
Roger Henderson	(661) 395-2569	

Program Information												
XPM	Yes	Delivery Plan	Yes	APL	Yes							
Program	STIP	Status	Programmed	Doc Yr	2000							
Prog Code	075.600	Prog FY	2006	Const \$\$	\$50,205	RW \$\$	\$7,638					
Funds Req Date	8/12/2005	CTC Vote Date	9/29/2005									
Component	Funding											
CAPT	RIP	IIP	LOCAL	OTHER								
SUPT	\$34,706	\$23,137										
	\$6,398	\$4,265										
Phase Completion												
PA&ED	100 %	RW	100 %	PS&E	100 %	CON						

XPM Milestone Information	PA & ED M200	Bridge Site to Struc M221	Maps to Survey M224	Reg R/W M225	Struc PS&E to Dist M378	District PS&E to HQ M380	R/W Cert M410	RTL M460	HQ Advise M480	Appr Const Cont M500	Contract Accept M600
Delivery Plan							7/5/2005	7/1/2005			
Approved	1/1/2004	4/1/2004	11/1/2002	10/1/2004	6/1/2006	8/1/2006	10/1/2006	10/1/2006	12/1/2006	3/1/2007	3/1/2010
Current	1/3/2003 A	1/29/2002 A	11/4/2001 A	4/1/2002 A	12/1/2003 A	5/16/2005 A	7/5/2005 A	8/22/2005 A	10/17/2005 A	3/1/2006 T	7/1/2008 T

Project Comments

Project is fully funded for Const, RW & support. JOINTLY FUNDED (Kern, Inyo, Mono) RTIP/ITIP PROJECT. The Scope of EA 09-25430(Cal City Interchange) is included in this project. Project is fast tracked, Risk schedule (RW prior to ED). Environmental has started studies and is on schedule to meet PA&ED of 10/02. 10/7/05 dac/JN: Controlled Access Highway Agreement (CAHA) was executed in May 2005. 10/7/05 dac/FM: Revised Relinquishment Agreement (DAN 06-1217) has been resubmitted to County of Kern (Pat Ebel) to process for approval and signature.



Caltrans Central Region Project Status Report

XPM Download 1/5/2006

PMCS Download 1/13/2006

11	Dist-EA	Phase	County-Route-Post Mile	PPNO	Project Name	Project Phase
	06-24342	1	KER -58 - 109.1/	0258B	OLD 58 RELINQUISHMENT	Construction
<u>Location Description</u>			<u>Work Description</u>		<u>ROW Info</u>	
IN KERN COUNTY AT MOJAVE FROM 0.2 KM EAST OF CHCHE CREEK BRIDGE TO 5.4 KM EAST OF AIRPORT ROAD			PAVEMENT REHABILITATION		Parcels _____ Utilities 0	
<u>Project Documents</u>			<u>*Escalated Cost Estimate</u>		<u>Current Cost Estimate</u>	
Env State ND Act 10/12/1999			Structure Est _____		Structure Est \$0	
Env Federal FI Act 09/26/1999			District Est _____		District Est \$4,897	
PID Appr 1/15/2002			Total Con Est _____		Total Con Est \$4,897	
Project Rpt 1/15/2002					R/W Est \$0	
<u>Agreements</u>						
PM Frank Momen PH# (559) 243-3444			Type _____ Agency Name _____ Date _____			
DM Gurbhay Brar PH# (559) 230-3106			COP KERN CO			
EM Juergen Vespermann PH# (559) 243-8157						
CM Roger Henderson PH# (661) 395-2569						
<u>Phase Completion</u>						
PA&ED 100% RW 100% PS&E 90% CON _____%						
<u>Program Information</u>						
XPM Yes Delivery Yes APL Yes						
Plan List						
Program Status Doc Yr						
STIP Programmed 1998A						
Prog Code Prog FY Const \$\$ RW \$\$						
025.500 2006 \$4,897 \$0						
Funds Req Date CTC Vote Date						
7/12/2005 8/18/2005						
Component Funding						
IIP						
RIP IIP LOCAL OTHER						
CAPT \$4,897						
SUPT \$935						
<u>XPM Milestone Information</u>						
PA & ED M200						
Bridge Site to Struc M221						
Maps to Survey M224						
Reg R/W M225						
Struc PS&E to Dist M378						
District PS&E to HQ M380						
R/W Cert M410						
RTL M460						
HQ Advrtise M480						
Appr Const Cont M500						
Contract Accept M600						
Delivery Plan _____						
Approved 1/1/2002 1/1/2002 5/1/2003 7/1/2003 9/1/2003 12/1/2003 12/1/2004						
Current 1/15/2002 A 1/15/2002 A 5/5/2003 A 3/4/2003 A 7/11/2005 A 9/12/2005 A 12/1/2005 A 12/1/2006 T						

Project Comments

Project will bring the existing Mojave 58 to a state of good repair for relinquishment.

CLOSE-OUT PHASE

Project Close Out

(End Project Milestone)



Caltrans Central Region Project Status Report

XPM Download 1/5/2006

PMCS Download 1/13/2006

Dist-EA	Phase	County-Route-Post Mile	PPNO	Project Name	Project Phase
12 06-24340	1	KER -58 -R107.7/R1180258		MOJAVE BYPASS	CLOSEOUT
Location Description		Work Description		ROW Info	
IN KERN COUNTY AT MOJAVE FROM 0.2 KM EAST OF CACHE CREEK BRIDGE TO 6.7 KM EAST OF AIRPORT ROAD		CONSTRUCT 4 LANE FREEWAY		Parcels	422
				Utilities	6
Project Documents		*Escalated Cost Estimate		Current Cost Estimate	
Env State	ER	Act	11/17/1998	Structure Est	\$11,061
Env Federal	ES	Act	08/26/1998	District Est	\$60,833
PID Appr	4/7/1992			Total Con Est	\$71,894
Project Rpt	5/22/1994			R/W Est	\$12,801
PM Frank Momen		PH# (559) 243-3444		Agreements	
DM Gurbhay Brar		PH# (559) 230-3106		Agency Name	
EM Juergen Vespermann		PH# (559) 243-8157		Date	
CM Roger Henderson		PH# (661) 395-2569			
				FWY KERN COUNTY TB	
				RR UPRR C12/29/99 122999	
Phase Completion					
PA&ED 100 % RW 100 % PS&E 100 % CON 100 %					
XPM Milestone Information					
PA & ED M200		Bridge Site to Struc M221	Maps to Survey M224	Reg R/W M225	Struc PS&E to Dist M378
District PS&E to HQ M380		R/W Cert M410	RTL M460	HQ Advise M480	Appr Const Cont M500
Contract Accept M600					
Delivery Plan					
Approved		8/26/1998	9/15/1997	9/1/1997	4/23/1999
Current		8/26/1998	A 8/26/1998	A 7/29/1998	A 4/23/1999
		12/16/1999	A 12/16/1999	A 6/15/2000	A 6/15/2000
		A 7/17/2000	A 12/1/2000	A 4/26/2004	A

Project Comments

06-243404 awarded 11/17/2000 for \$60,399,786.40 to E L YEAGER CONSTRUCTION.

MINOR A PROJECTS



Caltrans Central Region Minor Status Report

PMCS Download 1/13/2006

13 Dist-EA PhaseCounty-Route-Post Mile PPNO Project Name
09-33160_ 1 KER -14 - 11.5/ 12.8 EMERGENCY SLAB REPAIR ON RTE 14
NEAR SILVER QUEEN ROAD

Location Description

IN KERN CO ON RTE 14 FROM 1.04 KM SOUTH TO
1.12KM NORTH OF SILVER QUEEN ROAD (KP
18.51/20.60)

Work Description

EMERGENCY PCC SLAB REPAIR

Project Documents

Env State ☐ Act ☐
Env Federal ☐ Act ☐
PID Appr ☐
Project Rpt ☐

Right of Way Info

Parcels ☐ Utilities ☐ 0

Current Cost Estimate

Structure Est \$0
District Est \$200
Total Con Est \$200
R/W Est \$0

Agreements

PM Unassigned PH#
DM Unassigned PH#
EM Tom Dayak PH# (760) 872-0690
CM Roger Henderson PH# (661) 395-2569

Type Agency Name Date Amount

Program Information

XPM ☐ No APL ☐ No
List
Program Status Doc Yr
MINOR Active 2005
Prog Code Funds Req Date
201.120 5/2/2005
CTC Vote Date CTC Vote Amnt
5/7/2005 \$200
Component Funding
A

PMCS Milestone Information	Begin Project Report M040	PA & ED M200	Reg R/W M225	PS&E to Dist OE M377	District PS&E to HQ M380	R/W Cert M410	RTL M460	HQ Advertise M480	Appr Const Cont M500	Contract Accept M600
TARGET										
ACTUAL						4/29/2005				

Project Comments

14 Dist-EA PhaseCounty-Route-Post Mile PPNO Project Name
06-0A630_ 1 KER -58 - 105.5/ CACHE CREEK WEIGHT STATION
IMPROVEMENTS

Location Description

IN KERN COUNTY AT THE CACHE CREEK WEIGHT
STATION AT HIGHWAY 58. (KP 169.750)

Work Description

IMPROVING WEIGHT STATION.

Project Documents

Env State ☐ Act ☐
Env Federal ☐ Act ☐
PID Appr ☐
Project Rpt ☐

Right of Way Info

Parcels ☐ Utilities ☐ 0

Current Cost Estimate

Structure Est \$0
District Est \$260
Total Con Est \$260
R/W Est \$0

Agreements

PM Bill Moses PH# (559) 445-6514
DM Headquarters staff PH#
EM Gail Miller PH# (559) 243-8222
CM Roger Henderson PH# (661) 395-2569

Type Agency Name Date Amount

Program Information

XPM ☐ No APL ☒ Yes
List
Program Status Doc Yr
MINOR Active 2006
Prog Code Funds Req Date
201.321
CTC Vote Date CTC Vote Amnt
\$0
Component Funding
A , WIM

PMCS Milestone Information	Begin Project Report M040	PA & ED M200	Reg R/W M225	PS&E to Dist OE M377	District PS&E to HQ M380	R/W Cert M410	RTL M460	HQ Advertise M480	Appr Const Cont M500	Contract Accept M600
TARGET										
ACTUAL										

Project Comments



Caltrans Central Region Minor Status Report

PMCS Download 1/13/2006

15 Dist-EA PhaseCounty-Route-Post Mile PPNO Project Name
06-0A760_ 0 KER -58 - 138.7/ CONSTRUCT SEWER LINE FOR BORON
SRRA ON HWY 58

Location Description

ON RTE 58 NEAR BORON AT THE BORON SRRA EB
AND WB (KP 223.8)

Work Description

SEWER CONSTRUCTION

Program Information

XPM ☐ No APL ☒ Yes
List
Program Status Doc Yr
MINOR Active 2006
Prog Code Funds Req Date
201.250
CTC Vote Date CTC Vote Amnt
\$0
Component Funding
A

Project Documents

Env State ☐ Act ☐
Env Federal ☐ Act ☐
PID Appr ☐
Project Rpt ☐

Right of Way Info

Parcels ☐ Utilities ☐ 0

Current Cost Estimate

Structure Est \$0
District Est \$400
Total Con Est \$400
R/W Est \$0

Agreements

PM Unassigned PH#
DM Pending PH#
EM Gail Miller PH# (559) 243-8222
CM Unassigned PH#

Type	Agency Name	Date	Amount
------	-------------	------	--------

PMCS Milestone Information	Begin Project Report M040	PA & ED M200	Reg R/W M225	PS&E to Dist OE M377	District PS&E to HQ M380	R/W Cert M410	RTL M460	HQ Advertise M480	Appr Const Cont M500	Contract Accept M600
TARGET										
ACTUAL										

Project Comments

16 Dist-EA PhaseCounty-Route-Post Mile PPNO Project Name
09-32880_ 1 KER -178 - 90.4/ 92.3 SHOULDER WIDENING IN KERN CO ON HWY
178 NEAR SIERRA VISTA ROAD

Location Description

IN KERN COUNTY FROM 0.5 MI EAST OF SIERRA
VISTA ROAD TO BROADWAY STREET (KP
145.48/148.53)

Work Description

SHOULDER WIDENING

Program Information

XPM ☐ No APL ☒ Yes
List
Program Status Doc Yr
MINOR Active 2006
Prog Code Funds Req Date
201.310
CTC Vote Date CTC Vote Amnt
\$0
Component Funding
A

Project Documents

Env State ☐ Act ☐
Env Federal ☐ Act ☐
PID Appr ☐
Project Rpt ☐

Right of Way Info

Parcels ☐ Utilities ☐ 0

Current Cost Estimate

Structure Est \$0
District Est \$120
Total Con Est \$120
R/W Est \$0

Agreements

PM Unassigned PH#
DM Gurbhay Brar PH# (559) 230-3106
EM Gail Miller PH# (559) 243-8222
CM Roger Henderson PH# (661) 395-2569

Type	Agency Name	Date	Amount
------	-------------	------	--------

PMCS Milestone Information	Begin Project Report M040	PA & ED M200	Reg R/W M225	PS&E to Dist OE M377	District PS&E to HQ M380	R/W Cert M410	RTL M460	HQ Advertise M480	Appr Const Cont M500	Contract Accept M600
TARGET				3/1/2005		3/28/2005	4/1/2005	5/1/2005	6/1/2005	9/1/2005
ACTUAL						9/9/2005				

Project Comments



Caltrans Central Region Minor Status Report

PMCS Download 1/13/2006

17 Dist-EA PhaseCounty-Route-Post Mile PPNO Project Name
09-33190_ 1 KER -58 -M108.9/M10 WINDSCREEN INSTALLATIONS ON HWY 58
NEAR MOJAVE

Location Description
IN KERN COUNTY NEAR MOJAVE AT BUSINESS
ROUTE 58 WEST OVERCROSSING (KP 175.27)

Work Description
INSTALL WINDSCREENS

Project Documents

Env State ☐ Act ☐
Env Federal ☐ Act ☐
PID Appr ☐
Project Rpt ☐

Right of Way Info

Parcels ☐ Utilities ☐ 0

Current Cost Estimate

Structure Est \$0
District Est \$500
Total Con Est \$500
R/W Est \$0

Agreements

PM Unassigned PH#
DM Unassigned PH#
EM Unassigned PH#
CM Unassigned PH#

Type Agency Name Date Amount

Program Information

XPM ☐ No APL ☒ Yes
List
Program Status Doc Yr
MINOR Active 2007
Prog Code Funds Req Date
201.010
CTC Vote Date CTC Vote Amnt
\$0
Component Funding
A

PMCS Milestone Information	Begin Project Report M040	PA & ED M200	Reg R/W M225	PS&E to Dist OE M377	District PS&E to HQ M380	R/W Cert M410	RTL M460	HQ Advertise M480	Appr Const Cont M500	Contract Accept M600
TARGET										
ACTUAL										

Project Comments

18 Dist-EA PhaseCounty-Route-Post Mile PPNO Project Name
06-41470_ 0 KER -178 -72.8/73.1 WALKER PASS DRAINAGE

Location Description
NEAR WALKER PASS FROM 3.4 KM W TO 3.9 KM W
OF CHIMNEY CREEK RD (KP 117.2/117.6)

Work Description
RAISE GRADE AND CONSTRUCT A WATER
CUTOFF WALL

Project Documents

Env State ☐ Act ☐
Env Federal ☐ Act ☐
PID Appr ☐
Project Rpt ☐

Right of Way Info

Parcels ☐ Utilities ☐ 0

Current Cost Estimate

Structure Est \$0
District Est \$450
Total Con Est \$450
R/W Est \$0

Agreements

PM Judy Aguilar PH# (559) 243-3457
DM Michael Lim PH# (559) 230-3138
EM Gail Miller PH# (559) 243-8222
CM Roger Henderson PH# (661) 395-2569

Type Agency Name Date Amount

Program Information

XPM ☐ No APL ☒ Yes
List
Program Status Doc Yr
MINOR Active 2008
Prog Code Funds Req Date
201.150
CTC Vote Date CTC Vote Amnt
\$0
Component Funding
A

PMCS Milestone Information	Begin Project Report M040	PA & ED M200	Reg R/W M225	PS&E to Dist OE M377	District PS&E to HQ M380	R/W Cert M410	RTL M460	HQ Advertise M480	Appr Const Cont M500	Contract Accept M600
TARGET	7/1/2003	4/1/2007	5/1/2007	7/1/2007	9/1/2007	12/1/2007	12/1/2007	2/1/2008	2/1/2008	9/1/2009
ACTUAL										

Project Comments

MINOR B PROJECTS



Caltrans Central Region Minor Status Report

PMCS Download 1/13/2006

19 Dist-EA PhaseCounty-Route-Post Mile PPNO Project Name
09-33230_ 1 KER -58 - 139/ WATER WELL REHAB AT RTE 58 AT BORON
SRAA

Location Description

PM RTE 58 NEAR BORAON AT THE BORON SRAA
EB/WB (KP 223.7)

Work Description

EMERGENCY WELL REHAB

Program Information

XPM ☐ No APL ☐ No
List
Program Status Doc Yr
MINOR Active 2006
Prog Code Funds Req Date
201.250
CTC Vote Date CTC Vote Amnt
\$0
Component Funding
B

Project Documents

Env State ☐ Act ☐
Env Federal ☐ Act ☐
PID Appr ☐
Project Rpt ☐

Right of Way Info

Parcels ☐ Utilities ☐ 0

Current Cost Estimate

Structure Est \$0
District Est \$50
Total Con Est \$50
R/W Est \$0

Agreements

Type Agency Name Date Amount

PM John Fox PH# (760) 872-5207
DM Jeff Helmbolt PH# (760) 972-3325
EM Tom Dayak PH# (760) 872-0690
CM Roger Henderson PH# (661) 395-2569

PMCS Milestone Information	Begin Project Report M040	PA & ED M200	Reg R/W M225	PS&E to Dist OE M377	District PS&E to HQ M380	R/W Cert M410	RTL M460	HQ Advertise M480	Appr Const Cont M500	Contract Accept M600
TARGET										
ACTUAL										

Project Comments

MAINTENANCE PROJECTS



Caltrans Central Region Maintenance Status Report

PMCS Download 1/13/2006

20	Dist-EA Phase County-Route-Post Mile	Project Name
	06-48080 1 KER - 58 - 77/ 82.6	
Location Description		Work Description
IN KERN COUNTY NEAR KEENE FROM 0.1 KM WEST OF CALIENTE AND BEALVILLE ROAD TO TEHACHAPI CREEK BRIDGE OVERHEAD		CHIP SEAL
Project Documents		Right of Way Info
Env State <u>CE</u> Act <u> </u>		Parcels <u> </u> Utilities <u>0</u>
Env Federal <u> </u> Act <u> </u>		
PID Appr <u> </u>		
Project Rpt <u> </u>		
		Current Cost Estimate
		Structure Est <u>\$0</u>
		District Est <u>\$600</u>
		Total Con Est <u>\$600</u>
		<u>\$0</u>
Agreements		
PM Unassigned	PH# <u> </u>	Type <u>RR</u> Agency Name <u>UNION PACIFIC RR</u> Date <u>061803</u> Amount <u>\$0</u>
DM Unassigned	PH# <u> </u>	
EM Gail Miller	PH# <u>(559) 243-8222</u>	
CM Roger Henderson	PH# <u>(661) 395-2569</u>	

Program Information		
XPM <u>No</u>	APL <u>No</u>	List
Program	Status	Doc Yr
MAINTENANCE	Active	2003
Prog Code	Funds Req Date	
010.010		
CTC Vote Date	Prog FY	
Component	Funding	

PMCS Milestone Information	PA & ED M200	Bridge Site to Struc M221	Maps to Survey M224	Reg R/W M225	Struc PS&E to Dist M378	District PS&E to HQ M380	R/W Cert M410	RTL M460	HQ Advertise M480	Appr Const Cont M500	Contract Accept M600
TARGET	7/1/2003										
ACTUAL						7/3/2003	6/11/2003	7/2/2003	7/28/2003	3/17/2004	

Project Comments

21	Dist-EA Phase County-Route-Post Mile	Project Name
	06-0C350 1 KER - 14 - 35.8/ 40.2	PME CHIPS ON RTES KER 14, 155, AND 178
Location Description		Work Description
IN KERN COUNTY AT VARIOUS LOCATIONS		SEAL COAT
Project Documents		Right of Way Info
Env State <u> </u> Act <u> </u>		Parcels <u> </u> Utilities <u>0</u>
Env Federal <u> </u> Act <u> </u>		
PID Appr <u> </u>		
Project Rpt <u> </u>		
		Current Cost Estimate
		Structure Est <u>\$0</u>
		District Est <u>\$0</u>
		Total Con Est <u>\$0</u>
		<u>\$0</u>
Agreements		
PM Unassigned	PH# <u> </u>	Type <u> </u> Agency Name <u> </u> Date <u> </u> Amount <u> </u>
DM Unassigned	PH# <u> </u>	
EM Gail Miller	PH# <u>(559) 243-8222</u>	
CM Amrit Brar	PH# <u>(661) 720-0967</u>	

Program Information		
XPM <u>No</u>	APL <u>No</u>	List
Program	Status	Doc Yr
MAINTENANCE	Active	2005
Prog Code	Funds Req Date	
010.010		
CTC Vote Date	Prog FY	
Component	Funding	

PMCS Milestone Information	PA & ED M200	Bridge Site to Struc M221	Maps to Survey M224	Reg R/W M225	Struc PS&E to Dist M378	District PS&E to HQ M380	R/W Cert M410	RTL M460	HQ Advertise M480	Appr Const Cont M500	Contract Accept M600
TARGET											
ACTUAL						2/16/2005	12/2/2004	2/7/2005	3/14/2005	5/9/2005	

Project Comments



Caltrans Central Region Maintenance Status Report

PMCS Download 1/13/2006

22 Dist-EA Phase County-Route-Post Mile Project Name
06-0C430 1 KER - 58 -R139/R143.8 AR GGAC ON KER 58 NEAR BORAN REST
STOP

Location DescriptionIN KERN COUNTY NEAR BORON AT VARIOUS
LOCATIONS**Work Description**

RUBBERIZED ASPHALT CONCRETE OVERLAY

Program Information

XPM ☐ No APL ☐ No
List
Program Status Doc Yr
MAINTENANCE Active 2005
Prog Code Funds Req Date
010.010
CTC Vote Date Prog FY
Component Funding

Project Documents**Right of Way Info****Current Cost Estimate**

Env State ☐ Act ☐ Parcels ☐ Utilities ☐ 0 Structure Est \$0
Env Federal ☐ Act ☐ District Est \$0
PID Appr ☐ Total Con Est \$0
Project Rpt ☐ \$0

Agreements

PM Unassigned PH# ☐ Type ☐ Agency Name ☐ Date ☐ Amount ☐
DM Unassigned PH# ☐
EM Gail Miller PH# (559) 243-8222
CM Roger Henderson PH# (661) 395-2569

PMCS Milestone Information	PA & ED M200	Bridge Site to Struc M221	Maps to Survey M224	Reg R/W M225	Struc PS&E to Dist M378	District PS&E to HQ M380	R/W Cert M410	RTL M460	HQ Advertise M480	Appr Const Cont M500	Contract Accept M600
TARGET											
ACTUAL						1/24/2005	12/8/2004	1/6/2005	2/22/2005	4/18/2005	

Project Comments

23 Dist-EA Phase County-Route-Post Mile Project Name
06-49360 1 KER - 65 - 6.1/ 25.2

Location DescriptionIN KERN COUNTY NEAR BAKERSFIELD AT
VARIOUS LOCATIONS**Work Description**

CHIP SEAL AND DIGOUTS

Program Information

XPM ☐ No APL ☐ No
List
Program Status Doc Yr
MAINTENANCE Active 2005
Prog Code Funds Req Date
010.010
CTC Vote Date Prog FY
Component Funding

Project Documents**Right of Way Info****Current Cost Estimate**

Env State ☐ Act ☐ Parcels ☐ Utilities ☐ 0 Structure Est \$0
Env Federal ☐ Act ☐ District Est \$0
PID Appr ☐ Total Con Est \$0
Project Rpt ☐ \$0

Agreements

PM Unassigned PH# ☐ Type ☐ Agency Name ☐ Date ☐ Amount ☐
DM Unassigned PH# ☐
EM Gail Miller PH# (559) 243-8222
CM Roger Henderson PH# (661) 395-2569

PMCS Milestone Information	PA & ED M200	Bridge Site to Struc M221	Maps to Survey M224	Reg R/W M225	Struc PS&E to Dist M378	District PS&E to HQ M380	R/W Cert M410	RTL M460	HQ Advertise M480	Appr Const Cont M500	Contract Accept M600
TARGET											
ACTUAL						4/5/2005	4/4/2005	4/4/2005	5/2/2005	6/16/2005	

Project Comments
