



Daily Diary Report by Bid Item

Contract No.: 04-0120F4

Diary #: 070 Const Calendar Day: 275 Date: 10-Jun-2010 Thursday

Inspector Name: Bruce, Matt Title: Transportation Engineer

Inspection Type: Continuous

Shift Hours: 07:00 am 04:30 pm Break: 00:30 Over Time: 01:00

Federal ID:

Location:

Reviewer: Mathur, Lalit Approved Date: 08-Oct-10 Status: Approved

04-0120F4
 04-SF-80-13.2/13.9
 Self-Anchored
 Suspension Bridge

Weather

Temperature 7 AM 50 - 60 12 PM 60 - 70 4PM 50 - 60
 Precipitation 0.00" Condition Mostly sunny

Working Day If no, explain:

Diary: Dispute
Work description.
 - Continued to work on stressing paperwork and prepare for upcoming stressing operations.

04-0120F4 Bid Item: 034 X-W2C-BCT.034 E-W Line Cross Over W2 Cap Cap Beam Continuity Tendons
 SCHWAGER DAVIS INC.

Labor

Trade	Class	Name	RT Hrs	OT Hrs	DT Hrs	Total	Remarks	Dispute
Contractor: SCHWAGER DAVIS INC.								
Ironworker	JNM	Brian Nobile	0.00	0.00	0.00	0.00		<input type="checkbox"/>
Ironworker	JNM	Todd Blackwell	0.00	0.00	0.00	0.00		<input type="checkbox"/>
Ironworker	JNM	Bobby Almon	0.00	0.00	0.00	0.00		<input type="checkbox"/>
Ironworker	JNM	Bounthaby Singharath	0.00	0.00	0.00	0.00		<input type="checkbox"/>
Ironworker	FOR	Erin Jones	0.00	0.00	0.00	0.00		<input type="checkbox"/>
Ironworker	JNM	James Bond	0.00	0.00	0.00	0.00		<input type="checkbox"/>
Ironworker	JNM	Randy Hill	0.00	0.00	0.00	0.00		<input type="checkbox"/>
Ironworker	GEN	Ralph Craig	0.00	0.00	0.00	0.00		<input type="checkbox"/>

Diary: Dispute

Work description. 034 X-W2C-BCT.034
 - Pushed from strand packs number 8700, 8684, and 8170 into continuity tendons E30B to E42B except E41B.
 - Stressed continuity tendons E12A to E14A, E17A to E18A, E26A, E29A to E32A using the monostrand rams 6-8-134 and 6-8-0014 with gauge A for both rams. Lalit assisted me with the stressing operations inspection today.
 - Continued installing the anchorheads and wedges on both the dead and live ends of the E-Line continuity tendon strands previously placed.

The following is the list of equipment that SDI has onsite since it is not currently inputted into PMIV:

- Stressing Rams: 6-8-0014, 6-8-134, and CH600-8-109
- Hydraulic Pumps for Monostrand Rams: 2 units with no designated numbers on the equipment
- Hydraulic Pumps for Multistrand Rams: 1 unit with no designated numbers on the equipment
- Hydraulic Pump for Pushing Strand: HPU-D-110-3K-02
- Strand Pusher: No number designated on the equipment
- Grout Pump: No number designated on the equipment

Daily Diary Report by Bid Item

Job Name: 04-0120F4


Inspector Name: Bruce, Matt

Diary #: 070

Date: 10-Jun-2010 Thursday

- Refer to other Caltrans inspectors diaries for ABF operations and equipment at the W2 cap beam.

Attachment

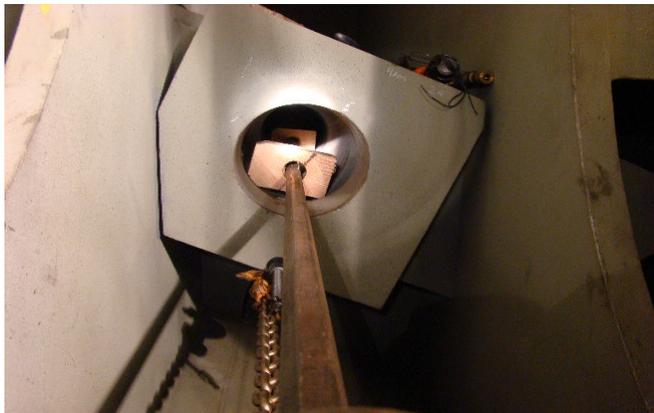

ABF continued to try and remove the wedged aluminum plate from the mandrel inside continuity tendon E41B in the W2 cap beam.



Stressing continuity tendon E13A from the live or west end of the W2 cap beam.
