



Devil's Slide/Hwy 1 Storm Repair

Daily Updates from Bijan Sartipi




Daily Update
July 18

Repair Work

Devil's Slide (post mile 39.14)

- Waler wall construction and tie back installation summary.

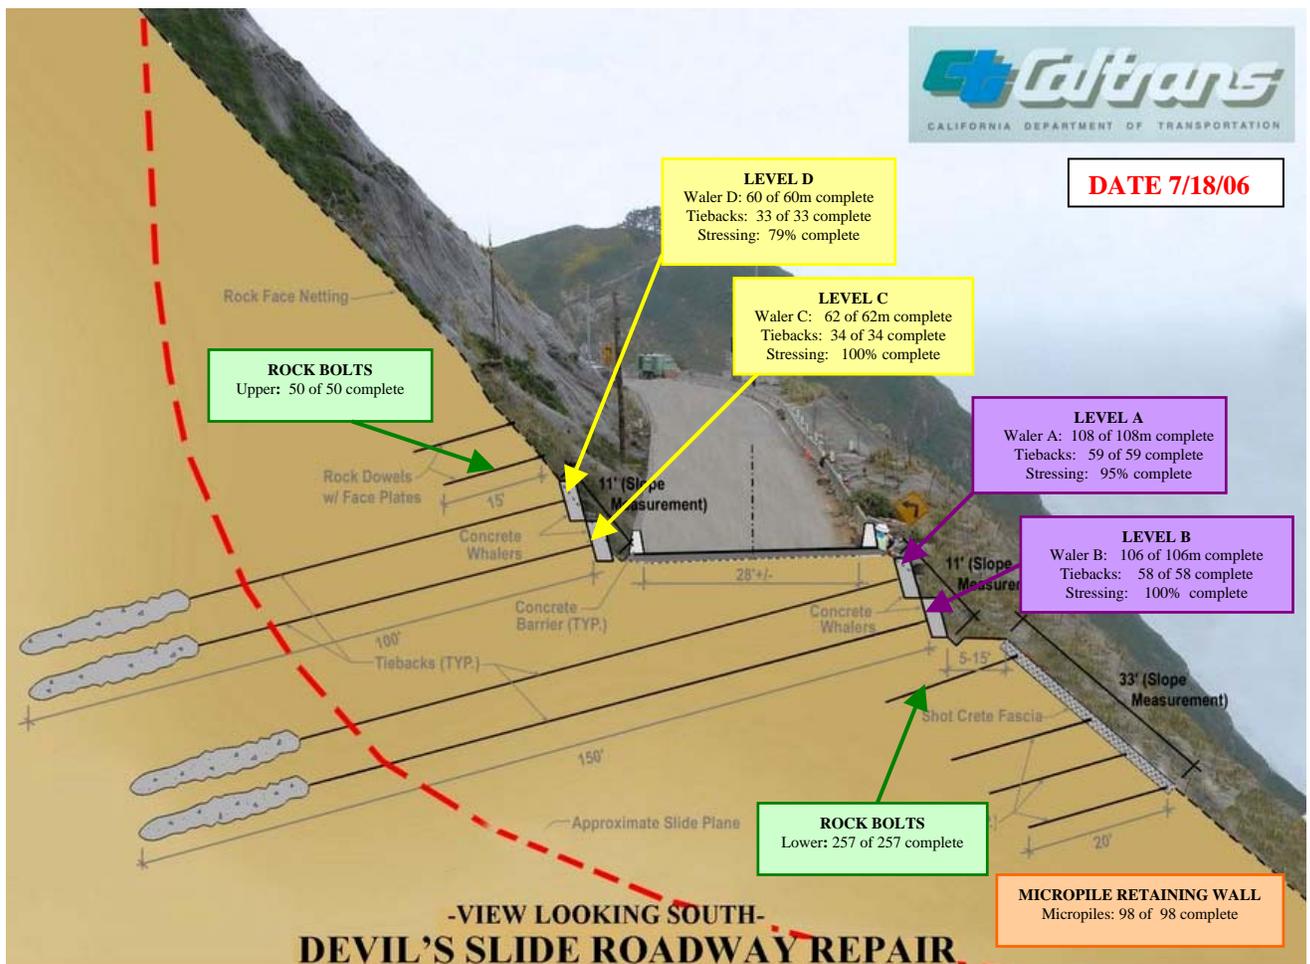

Notes: One micropile eliminated due to interference with drain for a total of 98.

- Level 'D' (upper level cliff side) – Cable stressing continued today. More of the temporary was removed.



Capping off completed tie back cables



Removing more of the temporary bench

Retaining (micropile) Wall

- Grading and clean up in preparation for forming the concrete cap.



A concrete cap will be formed over the micropiles

Drainage System

- The surface drain outfall pipe will be extended down the cliff to prevent erosion. Crews evaluated how to achieve this today.



Examining the steep drain outfall location
