



Certified Coatings Company
Member of the Muehlhan Group



April 8, 2008

CCC-ABF-LTR-000012

Page 1 of 2

American Bridge Company/Fluor Enterprises Inc.,
A joint Venture
375 Burma Road
Oakland, CA 94607

Attention: Sam Choy

Phone: (510) 808-4573

Fax: (510) 808-4601

Regarding: Revised Cost Impact for NOPC No. 5

Reference: SFOBB Self Anchored Suspension Span
Caltrans Contract No. 04-0120F4

Mr. Choy,

NOPC No. 5 will require an additional 211 meters of field welds to be blasted and painted. The welds will need to be painted on both sides creating 422 linear meters of weld. ABFJV will need to supply safe access to all weld locations on both girders at no cost to Certified Coating. We will require access suitable to construct containments on. The access will also need to safely hold painters and spent abrasive from abrasive blasting and water from washing.

The pricing for NOPC No. 5 is as follows:

Containment on Road Deck:

Labor to Set up, Dismantle, and Disposal
80 Hrs./Girder X 2 Girders @ \$73.68 = \$11,788.80

Containment for Bottom of Box Girder:

Labor to Set up, Dismantle, and Disposal
80 Hrs./Girder X 2 Girders @ \$73.68 = \$11,788.80

Partition Interior of Box Girder:

Labor to Build Partition
160 Hrs./Girder X 2 Girders @ \$73.68 = \$23,577.60

RECEIVED

APR 10 2008

AMERICAN BRIDGE/FLUOR

Certified Coatings Company — 1045 Detroit Avenue Concord, CA 94518
(925) 686-1550 - FAX (925) 671-7036 — e-mail: ccc@muehlhanusa.com

REC'D NOV-18 #007708

Abrasive Blast and Paint Welds:

Labor to Ventilate the Interior:
 206 Hrs. @ \$73.68 = \$15,178.08

Labor to abrasive blast and paint welds:
4,410 Hrs. @ \$73.68 = \$324,928.80

Labor Subtotal = \$340,106.88
 Markup X 1.28
 Labor Total = \$435,336.81

Materials:

Abrasive @ \$10.00/sack X 173 sacks = \$1,660.00
 Primer @ \$70/gal X 6 gal = \$420.00
 Finish @ \$88/gal X 4 gal = \$352.00
Containment - framing and tarps = \$6,000.00
 Material Subtotal = \$8,432.00
 Markup X 1.10
 Material Total = \$9,275.20

Equipment:

Dust Collector @ \$1,100/day X 22 days = \$24,200.00
 Markup X 1.10
 Equipment Total = \$26,620.00

Total Price for NOPC: = \$533,565.29

This work to accomplish NOPC No.5 will take about 40 working days to contain, set up equipment, abrasive blast, apply paint, remove containment and clean up.

The price for NOPC 5 is based on contract drawings. The actual lengths of the field welds or those shown on the construction or erection drawings may differ from those in the contract drawings. Should the difference be significant, we reserve the right to revise our price.

If you require additional information, please contact us at (925) 265-8818.

Sincerely,


 James Brockman
 Certified Coatings Company

RECEIVED
 APR 10 2008
 AMERICAN BRIDGE/FLUOR

Certified Coatings Company

NOPC 5

Corner Assembly Take Off

PP 112 to PP 116 Both East and West

Vertical Weld	2.5m X 14 panels X 2 girders =	70m
Upper Longitudinal Weld	30m X 2 girders =	60m
Lower Longitudinal Weld	30m X 2 girders =	60m
End Weld	5.3m X 2/girder X 2 girders =	21m
Total Weld Length		<u>211m</u>


Both sides of the weld will have to be abrasive blasted and primed.

211 meters of weld X 2 sides = 422 linear meters of abrasive blasting.

RECEIVED
APR 10 2008
AMERICAN BRIDGE/FLOOR



04	SF	8
<i>George</i>		
REGISTERED ENGINEER		
12-6-04		
PLANS APPROVAL DATE		
<i>The State of California or agents shall not be responsible for completeness of electrical sheet.</i>		
T.Y. LIN / MOFFATT 825 BATTERY STREET SAN FRANCISCO, CA		
<i>Caltrans now has a web site</i>		

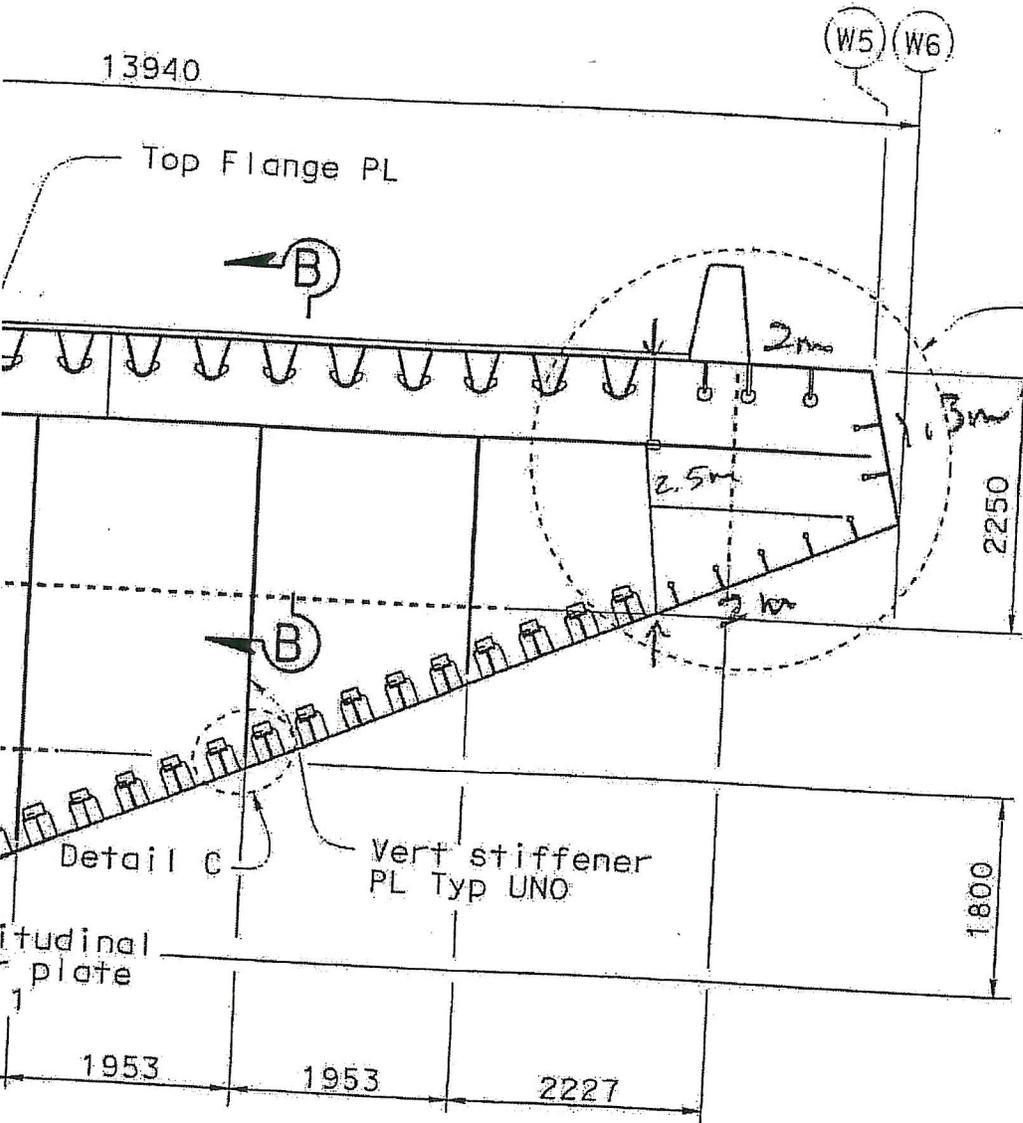

Detail A

Reference list
(see Note 4)

Floorbeam is located at Panel Points 115 and Intermediate Panel Points

Floorbeam at intermediate Panel Points 12.5, 13.5, 111.5, 112.5, 113.5

- For counterweight details, see "Details No.17" sheet.
- For "Typical Floorbeam Details" shall be detailed according to

5-20-20

"LEAVE-OUT" SECTION LIFT

