

Job Stamp 04-0120F4 SFOBB SAS

Const. Calendar:	483			
Project Work Day No.:	693			
Date	04/09/2008			
Inspectors	Start	09:20	Stop	12:00
Hours		12:30		14:30
Shift Hours		07:00		15:30

ASSISTANT RESIDENT ENGINEER'S **CONTRACTOR – ABFJV, Sub RPS and Conco**

Weather: Sunny with mild temperature - Hi 67 F Lo 48 F (per weather.com forecast)

Description of Operations @ W2 Cap Beam:

ABF

- Miscellaneous cleanup and material mobilization.
- Fabrication of west wall forms continues.
- Began installing form ties in the longitudinal diaphragm on the east section.
- Installed cooling pipes in the east wall.
- Continued east wall blockouts with shear keys on the north and south ends of pour 2.
- Surveyors set a string line at the top of concrete to assist RPS with placing vertical rebar for the transverse diaphragm. Many bars will have to be adjusted to achieve proper cover for the vertical bars.

CONCO

- Conducted a walk through with ABF for pour 2 still scheduled for May 6th.

RPS

- Began to adjust #25 and 29 vertical bars in the transverse diaphragm for the initial string line set by ABF surveyors. Worked on other items while ABF surveyors set the final line completed at the end of the day.
- Placed 4 #32 vertical T-Heads instead of 6 #29HV bars and 29HT01 bars in the northeast jacking frame support block section, see sheets 497S7R1 and 497S8R1.
- Placed 2x1-36L13T01** to 2x1-36L15T01** exterior face bars on the northwest wall, see sheets 492R2 495R2 for details.

Office Work:

- Attended Team Concrete meeting with ABF and TY-Lin at 8:00am.
- Reviewed plans for W2 cap beam.

Inspector:

Matt Bruce Matt Bruce Transportation Engineer (D)


REC'D #08 APR-19 #004278

EA	04-0120F4
Co-Rte-KP (PM)	SF-080-13.2/13.9 (8.2/8.7)
Structure Rep.	Rick Morrow



File Name:	DSC01365		
Date:	04-09-08	By Int:	D Chung
Description: Cooling pipes installed in the east wall.			

File Name:	DSC01368		
Date:	04-09-08	By Int:	M Bruce
Description: Jacking frame support block rebar placement.			

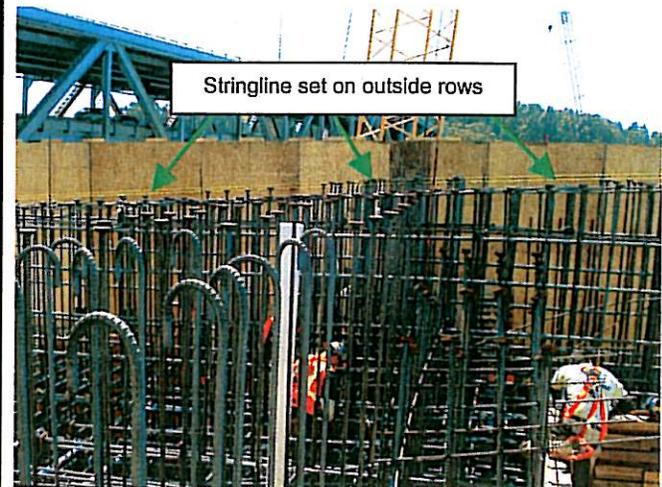

File Name:	DSC01369		
Date:	04-09-08	By Int:	M Bruce
Description: Stringline set by ABF surveyors for the transverse diaphragm.			
