

Job Stamp  
**04-0120F4**  
**SFOBB SAS**

Report No. 485  
Project Work Day No. 695  
Date 11-APR-2008  
Shift Hours Start 06:30 Stop 15:30

ASSISTANT RESIDENT ENGINEER'S **CONTRACTOR – ABFJV**

Weather: Clear, 52°-75°

EQUIPMENT AND/OR LABOR:			HOURS - ITEM NO.										REMARKS	
Equip. #	NO. MEN	DESCRIPTION (Of Equipment or Labor)	Item #8 - TOTAL HOURS											
D12-261	1	Manitowoc Crane	8											
L-270	-	D185Q Sullivan Air Compressor	IDLE											
39831 74-39831	2	Chevy 3500 Pick Up Truck	8										Traylor Dutra	
196	-	Power Generator	IDLE											
7-154	-	CAT-IT28B Loader	8											
246-01-6015	1	John Deer 270 Excavator	IDLE											
		9940 lbs Vertical Drill	IDLE											
DR-13	4	Man Basket Drill Platform	IDLE											
Traylor Dutra	1	Ron Lindsay (FOR)	8											
Traylor Dutra	1	Bill White (OE)	8											
Traylor Dutra	1	Ken White (OE)	8											
Traylor Dutra	1	Randall Lesley (PLDR)	8											
Patent	1	Dorian Chavez (FOR)	8											
Patent	1	Martin Sandoval (LBR)	8											
ABF	1	Katherin Quillen (Lead)	8											

**Description of Operation:**

- Field Visit, arrived 6:30AM
  - Foundation A1:
    - Patent arrived on site and completed scaffolding installation. It was greened tagged and signed off by midmorning. The hand rails at the W2 observation platform were cut around 1:00pm, the staircase is now ready for use.
    - Traylor Dutra staked out and installed forms for ratslab. They plan to pour on Monday.
    - Ron Lindsay informed me that he slipped and fell at the base of the scaffolding. He said there appears to be a natural runoff from the north face of the hillside that is accumulating right where the scaffolding steps off onto the W2 foundation. I informed Jason of the incident.
  - Foundation B-1:
    - Around 12:30pm Traylor Dutra continued excavating with use of the clam shell. Two workers guided the clam shell via tag lines and hand signals to the crane operator. Once too much

REC'D '08 JUN 28 #005237

spoils gathered on the platform, two workers went down and hand shoveled out the dirt into the crane suspended skip box.


- Foundation B-2:
  - Manual informed me he spoke with Brad Middleton last night and Drill Tech intends to test the battered micropiles on Monday.
- Sent in Sub 657R01

**Inspector:**

Gina Rizzardo



Transportation Engineer/Assistant Structure Rep.

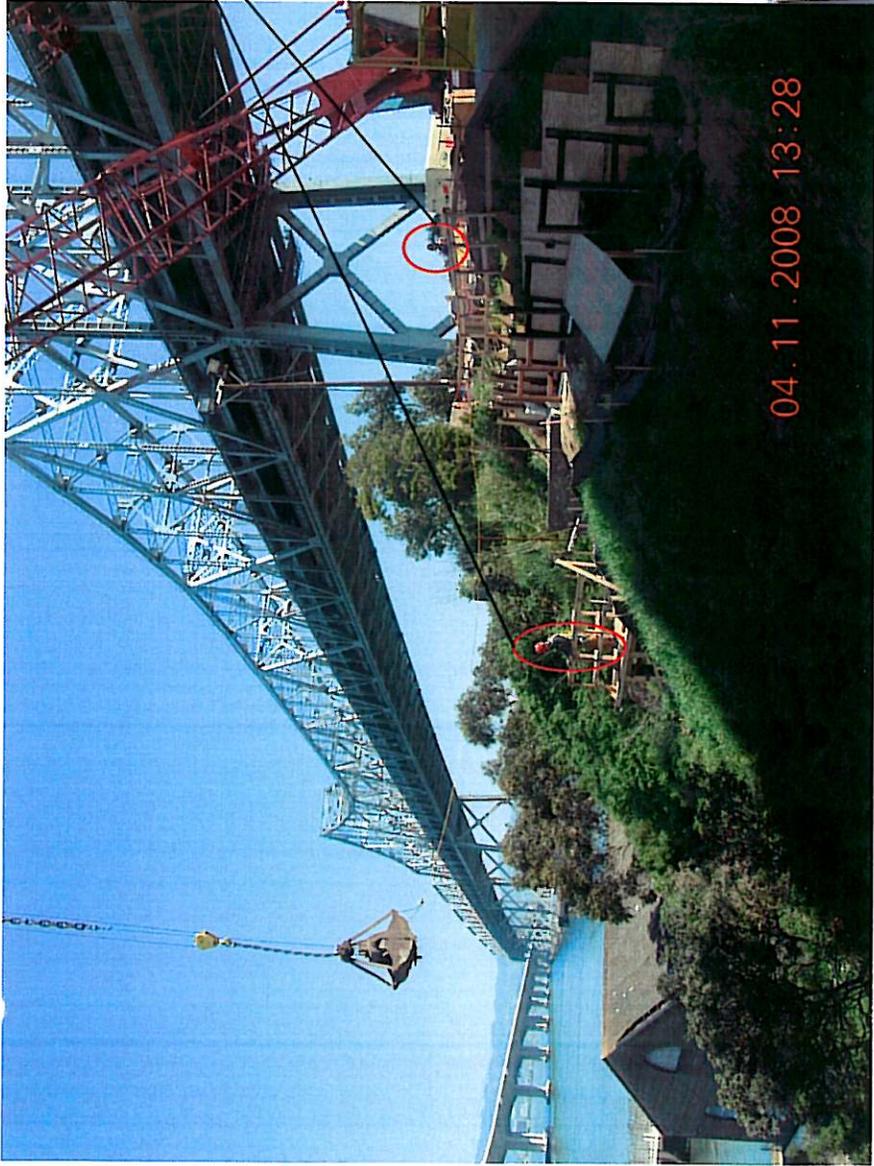

2 workers guided the clam shell to pick up spoils at B2

Spoils were hand shoveled out once platform reached capacity.

