



|                |                            |
|----------------|----------------------------|
| EA             | 04-0120F4                  |
| Co-Rte-KP (PM) | SF-080-13.2/13.9 (8.2/8.7) |
| Structure Rep. | Rick Morrow                |




|            |                       |         |         |
|------------|-----------------------|---------|---------|
| File Name: | Aug-8-2008 W2 Cap 003 |         |         |
| Date:      | 08-08-08              | By Int: | M Bruce |

Description: Ironworkers mobilizing #43 bars that were detailed in RFI 1464R01. ABF laborers can also be seen in the photo placing caps on the vertical dowels.

|            |                       |         |         |
|------------|-----------------------|---------|---------|
| File Name: | Aug-8-2008 W2 Cap 005 |         |         |
| Date:      | 08-08-08              | By Int: | M Bruce |

Description: Support frame built in the northeast quadrant for the vertically bundled #43 transverse bars in the top mat of pour 3.

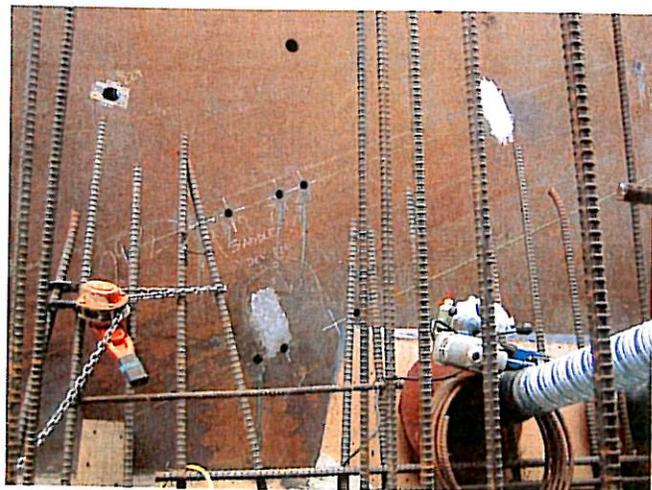

|            |                       |         |         |
|------------|-----------------------|---------|---------|
| File Name: | Aug-8-2008 W2 Cap 006 |         |         |
| Date:      | 08-08-08              | By Int: | M Bruce |

Description: Drilled holes in the W2W deviation saddle forms for the temporary support rods to be used for the saddle erection.

|            |                       |         |         |
|------------|-----------------------|---------|---------|
| File Name: | Aug-8-2008 W2 Cap 009 |         |         |
| Date:      | 08-08-08              | By Int: | M Bruce |

Description: Improper storage of bearing plates, trumpets and vertical rods. There is a significant amount of dirt on the material as well as built up rust on the plates. ABF has been informed in the past about this issue numerous times.
