INTERSTATE 5
CORRIDOR IMPROVEMENTS
Dr. Martin Luther King Jr. Boulevard/Charter Way to Hammer Lane:
Interstate 5 North Stockton Improvement Project
Interstate 5 Rehabilitation Project
Caltrans District 10

Fall 2015

Edmund G. Brown Jr., Governor
Malcolm Dougherty, Director

Volume 3, Issue 3

Caltrans would like to extend our appreciation to motorists and residents for their cooperation during the construction of the Interstate 5 (I-5) Corridor Improvement projects.

I-5 Projects in the Home Stretch

I-5 Rehabilitation Project

(Country Club Boulevard to Charter Way)

All elements of work are in their final stages between Charter Way and Smith Canal. Remaining work includes paving of the center median, and shoulders as well as striping. There will be an upcoming closure of the northbound Country Club Boulevard off-ramp in October and a final lane shift on both north and southbound I-5 lanes for striping. Message boards will be placed in strategic locations to alert drivers of any delays.

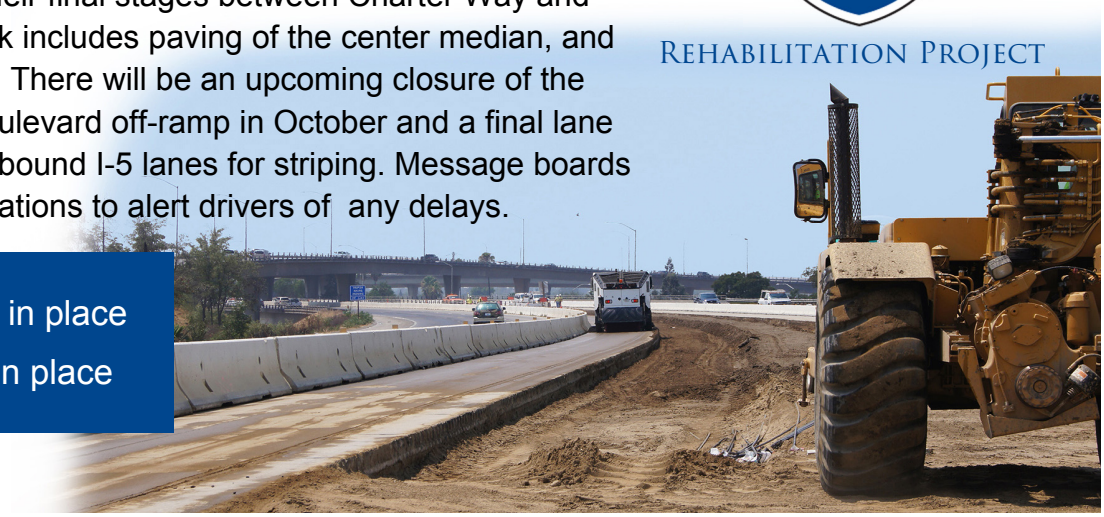

- Message signs will be in place
- 55 mph speed limits in place

The I-5 North Stockton Improvement Project

(Hammer Lane to Country Club Boulevard)

Stage I & II are complete and northbound road construction is finished. Stage III is 70% complete with only 50% of the west side retaining walls still to be completed. Stage IV will shift southbound traffic back to the southbound lanes. Crews will then remove temporary barriers, construct permanent median barrier, install final signing and striping.

INTERSTATE 5 REHABILITATION PROJECT

The I-5 Rehabilitation Project will occur in four stages:

Stage 1: Caltrans will close the northbound and southbound #1 (left) lane, widen the median and construct concrete median barriers.

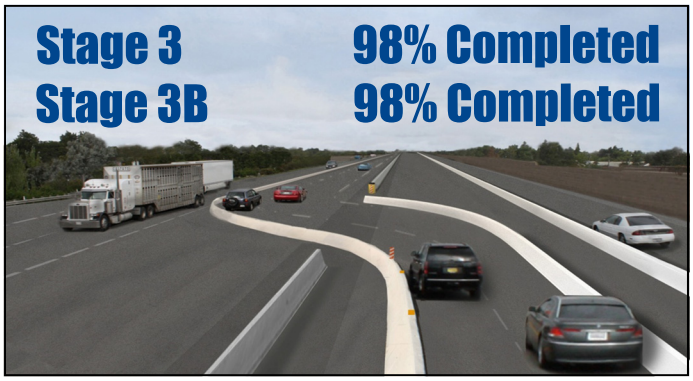

Stage III: Shifts northbound traffic from Pershing Avenue to Country Club Boulevard to the southbound lanes. Crews will work on the northbound #1 (left), #2 (middle) and #3 (right) lanes. Stage 3B northbound traffic shift from Charter Way to Pershing Avenue.

Stage II: K-Rail (concrete temporary dividers) will be placed between the northbound and southbound #3 (middle right), #4 (right) lanes to reconstruct the #4 lane, auxiliary lanes and shoulders. This stage includes some ramps to be closed. All ramp work will be completed in this stage.

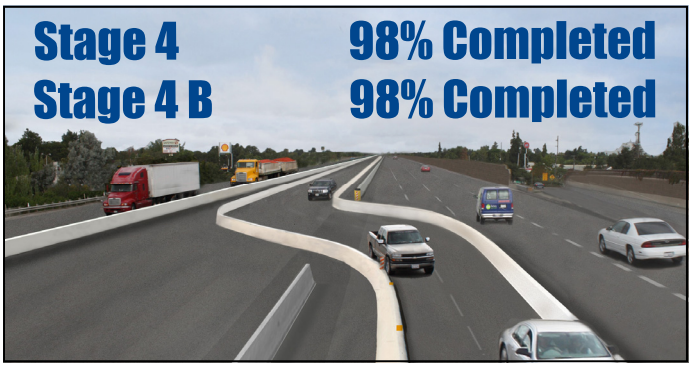

Stage IV: Will shift southbound traffic from Country Club Boulevard to Pershing Avenue northbound lanes. Crews will work on the southbound #1 (left), #2 (middle) and #3 (right) lanes. Stage 4B southbound traffic shift from Pershing Avenue to Charter Way.

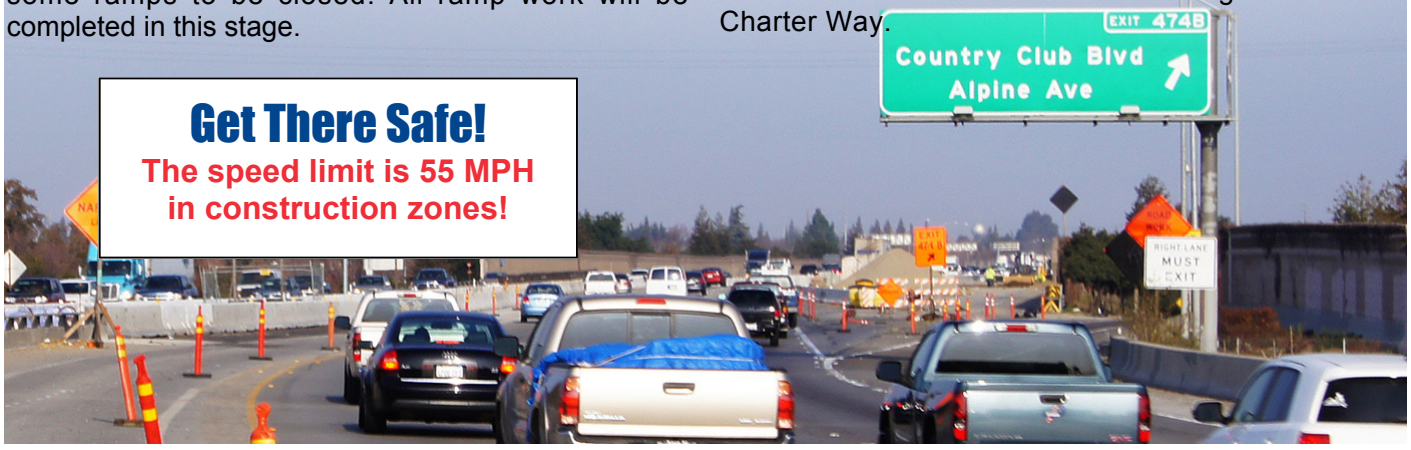

Get There Safe!

The speed limit is 55 MPH in construction zones!

The I-5 North Stockton Widening Project will occur in four stages:

Stage 1

Shift traffic to outside freeway barriers. Widen the median of the freeway and bridges. Construct retaining walls along the northbound shoulder between March Lane and Hammer Lane. 1.5 to 2 year construction period. Stage 1 construction began in August 2011, completed in summer 2013.

Stage 3

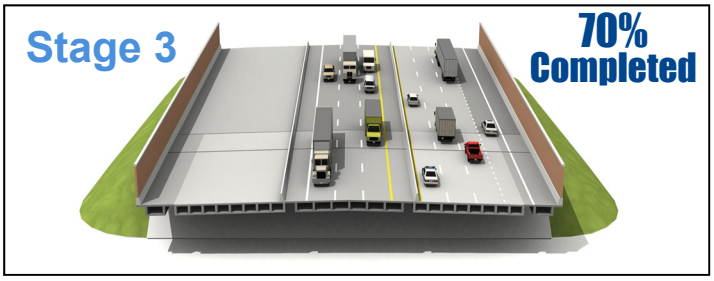

Shifting of the southbound traffic to median. 3 travel lanes will remain open in each direction. Replace southbound freeway pavement. Construct outside auxiliary lanes and soundwalls.

Stage 2

Shift northbound traffic to median. 3 travel lanes will remain open in each direction. Replace northbound freeway pavement. Construct outside auxiliary lanes and soundwalls. One year period, completed in early 2015.

Stage 4

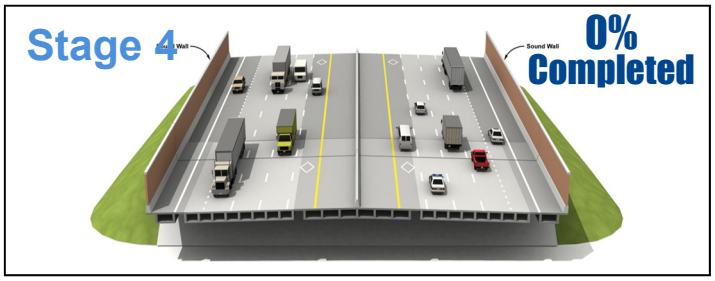

Shift southbound traffic back to southbound lanes. Remove temporary barriers, construct permanent median barrier. Final signing and striping.

Thanks For Your Cooperation!

Upon completion, the Interstate 5 North Stockton Improvement Project will reduce congestion, improve commute times and make a quieter, more efficient freeway for California drivers.

Temporary Closure of the Northbound I-5 Country Club Boulevard Off-Ramp

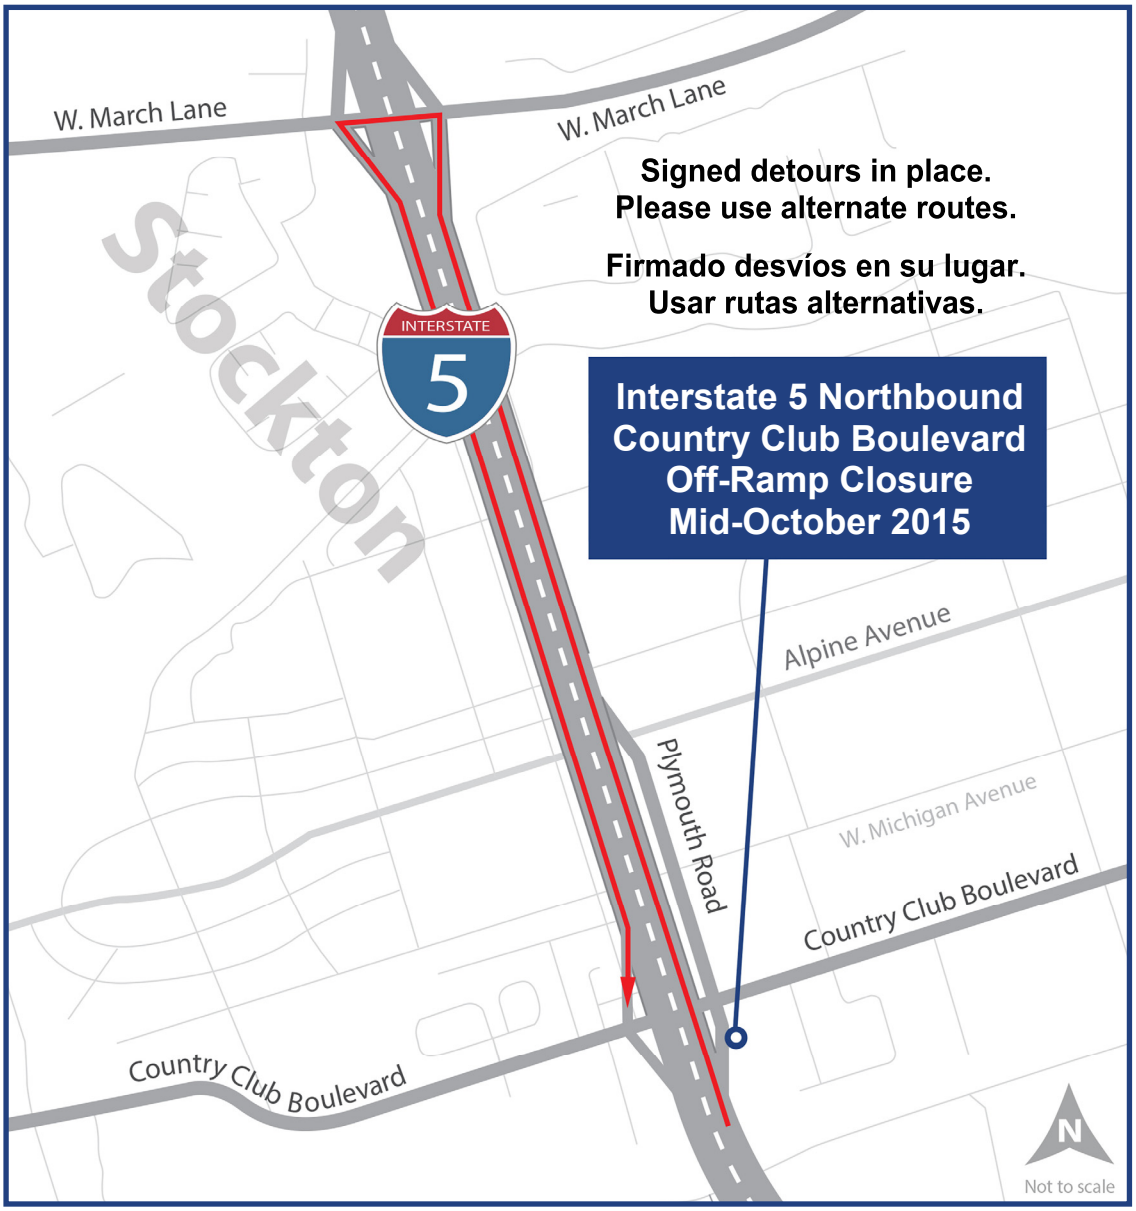

Closure dates are approximate. Please check the Caltrans Quickmap website at **http://quickmap.dot.ca.gov/**, or call **1-800-427-7623**, for the most up to date information.

✓ Work scheduled is subject to change due to traffic incidents, weather, availability of equipment and/or materials and construction related issues.

Copyright 2015, Caltrans District 10, Stockton, California

Follow

Caltrans DISTRICT 10

facebook

twitter

Project partners:

CITY OF STOCKTON

SJCOG MEASURE K KEEPS US MOVING

Caltrans

Contact:

Caltrans District 10
Public Information Office
P.O. Box 2048
Stockton, CA 95201

Hotline: (209) 948-7977

Fax: (209) 948-3895

E-mail:
District10PublicAffairs
@dot.ca.gov

SLOW FOR THE CONE ZONE CALTRANS

MOVE OVER
