Planned Improvements for State Route 12 Through Solano County Between Suisun City and Rio Vista

Planned Improvements: Location, Description and Projected Timeline

East of Walters Rd. to Shiloh Rd.
PM 7.9 to PM 13.6
Summer 2007:
Install concrete barrier and shoulder rumble strips
Summer 2008:
Bridge rail upgrades, pavement repair and intersection improvements

Shiloh Rd. to Currie Rd.
PM 13.6 to PM 20.6
Summer 2007:
Install center line channelizers
Summer 2008:
Roadway re-alignment, profile correction, shoulder widening, center line & shoulder rumble strips, intersection improvements and extended passing lanes

Currie Rd. to Azevedo Rd.
PM 20.6 to PM 22.6
Spring 2007:
Install center line channelizers and center line & shoulder rumble strips

Azevedo Rd. to Liberty Island Rd.
PM 22.7 to PM 23.7
Spring 2007
Install center line channelizers and center line rumble strips
Summer 2010:
Widen shoulders and install shoulder rumble strips

Liberty Island Rd. to Drouin Dr.
PM 23.7 to PM 25.6
Spring 2007:
Install center line channelizers and center line rumble strips

Immediate improvements: Separation of two-way traffic by concrete barrier

Immediate improvements planned from east of Walters Rd. to Shiloh Rd.

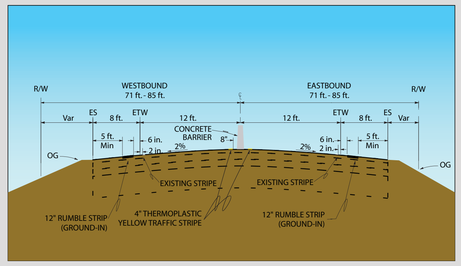

Immediate improvements: Channelized two-way traffic

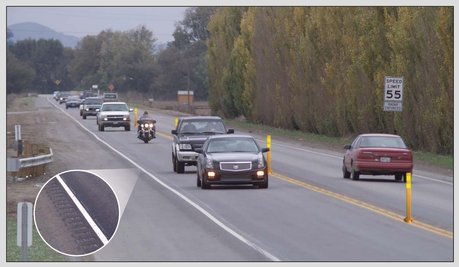

Immediate improvements planned between Currie Rd. and Drouin Dr.

Center line and/or shoulder rumble strips; locations vary

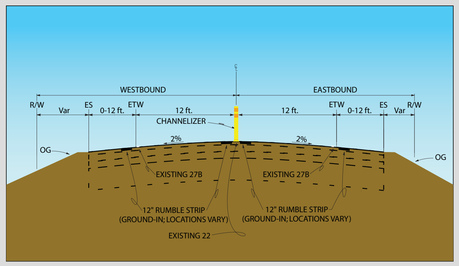

Long term improvements planned between Shiloh Rd. and Currie Rd. (Summer 2008)

Roadway re-alignment



Profile correction



Outside shoulder widening & AC overlay

Roadway between Azevedo Rd. and Liberty Island Rd. will have shoulder rumble strip only.
