STATE OF CALIFORNIA
DEPARTMENT OF TRANSPORTATION

Form HC-10A (Rev. 6/80)

Job Stamp					
04-0120F4	Construction Calendar	392			
SFOBB SAS	Project working days no.	602			
	Date	01/09/2008			
	Inspectors Hours	Start	7:30	Stop	13:00
	Shift Hours	Start	6:30	Stop	15:00

Description of Operation:

- See Lalit Mathur's diary for ABF labor, equipment, materials, weather, and comments.

- Daily activity of Regional Steel (R.S.) and ABF
  - R.S. continued to place B1 longitudinal bars.
  - R.S. placed hoops at W2E columns.
  - R.S. starts placing L and T bars at W2E columns.

Fig. 1

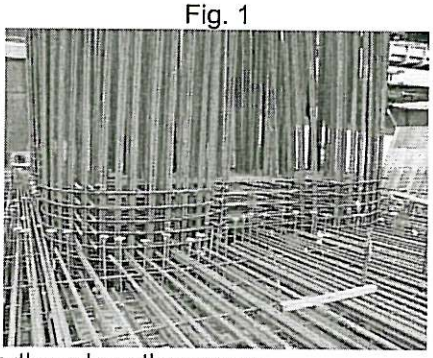

  - R.S. worked on the skin bars at north and south corners.

Fig. 2

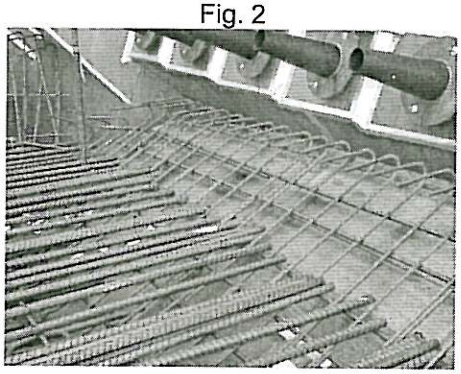

- Note
  - Observed the demonstration of hydraulic lift for contractors.

Fig. 3

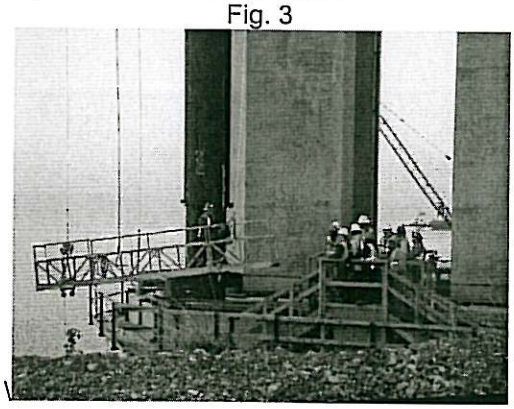

REC'D '08 FEB-23 #003577

- Discussed with Pamela Gagnier regarding T and L bars. See Pam Gagnier's diary for detailed information on them, e.g. conversation with T.Y. Lin designer and decision made.
- See Matt Bruce's diary for detailed activities and comments related to post-tensioning and other issues.
- See Pamela Gagnier's diary for detailed conversation with the contractors and decision made.
- Continued to review the plan and write a diary after 13:00 (see Matt and Pamela's diaries for field activities after 13:00.

➢ Punch list
- ~~3 full-length transverse bars (B2) need to be pulled up.~~
- ~~B2 full-length transverse bars need to be torqued. Each bar has 2 couplers~~.
- ~~6 short transverse bars (B2) need to be pulled up~~.
- ~~1 full-length transverse bar (B3) at west corner needs to be pulled up~~.
- The B1 transverse bar at east corner need to be replaced due to a mechanical coupler (See diary dated Jan. 3)

Inspector:

SeongHyeok Song _____ Trans Engineer (C)/Asst. Struct. Rep
