STATE OF CALIFORNIA	Job Stamp	7-day Const. Calendar	Day No. 481
DEPARTMENT OF TRANSPORTATION	SFOBB SAS	Project Work Day No.	Day No. 681
Form HC-10A (Rev. 6/80)	04-0120F4	Date	**04/07/2008**

Inspectors Hours Start 0700 Stop 1530

Shift Hours Start 0630 Stop 1500

ASSISTANT RESIDENT ENGINEER'S

CONTRACTOR – ABFJV

EQUIPMENT AND/OR LABOR:

Equip. #	NO. MEN	DESCRIPTION (Of Equipment or Labor) Regional Steel	HOURS - ITEM NO. 48 – Bar Reinforcing Steel (Bridge)									IDLE OR DOWN	REMARKS Name	Contractor
1	1	Superintendent	8										Gaige, Lance	RSC
2	1	Foreman	0										Van Brusselen, Jon	RSC
3	1	Ironworker	0										Jobe, Jason	RSC
4	1	Ironworker	8										Manzano, Jose	RSC
5	1	Ironworker	8										Lopez, Jorge	RSC
6	1	Ironworker	8										Greenlee, Tim	RSC
7	1	Ironworker	0										Rodriguez, Ernesto	RSC
8	1	Ironworker	0										Gomez, Daniel	RSC
9	1	Ironworker	0										Balderrama, Julio	RSC
10	1	Ironworker	0										Ortiz, Roberto	RSC
11	1	Ironworker	0										Mortenson, Kurt	RSC
12	1	Ironworker	0										Bell, Joe	RSC
14	1	Ironworker	0										Stockton, Luke	RSC
15	1	Ironworker	8										Quiroz, Victor	RSC

Weather: Sunny, hazy, mild, wet ground, Hi 60 F Lo 46 F.

Description of Operation:

ABF

See L. Mathur's diary for labor, equipment and daily activities. Also see M. Bruce's diary for additional comments.

Daily for Regional Steel

Finished installing east wall external horizontal #36L13-L8T91/92 transverse rebar.
Finished installing east wall interior horizontal #36L13-L8T81 transverse rebar.
Installed 4 #36L8T40/T41 bars in transverse wall because originally fabricated short (did not extend 1500mm into mass concrete).
Finished installing horizontal ties in east wall.

REC'D '08 MAY-31 #004967

Started installing #25L9-L15L20 rebar in the longitudinal wall.
See M. Bruce & D. Chung diaries for additional comments.

NOTES:

- ABF was burglarized over the weekend. Thieves took copper wiring out of the electrical panels and some employees tools. No power today on the jobsite.
- RSC (Lance) is refusing to install L14 transverse bar to external east wall per agreement made when RSC did not include L14 in pour 1.

Inspector:

Pamela Gagnier _____ Trans Engineer (C)/Asst. Struct. Rep

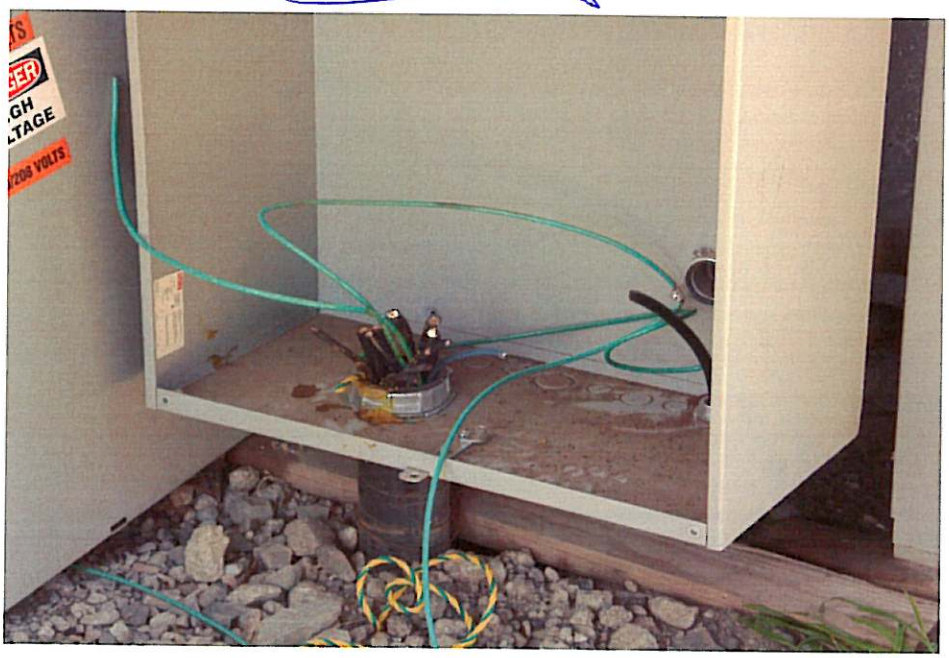

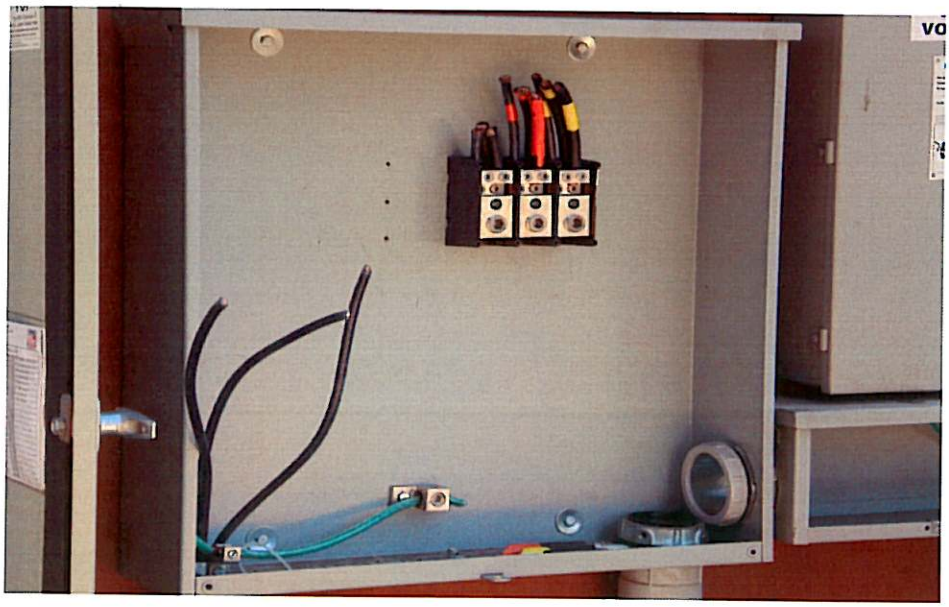

Burglarized electrical cabinets.

Finished east wall south and north quads. #36L14 bar still not installed.

#25L9-L15L20 rebar in the longitudinal wall.
