STATE OF CALIFORNIA
DEPARTMENT OF TRANSPORTATION
CP-CEM 4601 (Rev. 4/99) (Old HC-10A)

TOLL PROGRAM/DIST. 4 CONSTR.

Job Stamp:
04-SF-80-13.2/13.9 04-0120F4
SFOBB SAS
San Francisco Co. in San Francisco
Fm 0.6 km to 1.3 km East of Yerba Buena
Tunnel East Portal

Report No. **46.B**

Date the Shift Began: 7/1/08

☐ NIGHTWORK TUESDAY

Shift Hrs	Start		Stop	
Engineer's Hrs	Start	7:00	Stop	15:30

ASSISTANT RESIDENT ENGINEER'S DAILY BRIDGE REPORT

Location:	W2 Cap Beam	7-day const. cal.:	566	Weather:	overcast
Remark:	lost deck	Project work day:	776		

Description of Operation:
ABF - continued to build formwork for southeast void/continue with supports for void formwork in northeast void.
RPS - begin T bars in column cage area at W2E

HOURS - ITEM NO.							
ITEM NO. >>	38	48	133				IDLE OR DOWN/ ELSEWHERE
	Structural Concrete, Bridge	Bar Reinforcing Steel (Bridge)	Construction Surveying				
EQUIPMENT AND/OR LABOR: EQPT. NO. / NO. MEN / DESCRIPTION (Of Equipment or Labor)	RT	RT	RT				< RT/OT

CONTRACTORS		
Prime	American Bridge / Fluor JV	(P)
Sub #1	Regional	(1)
Sub #2		(2)
Sub #3		(3)
Sub #4		(4)
Sub #5		(5)

REMARKS		
Name	Classification	Prime / Sub

For equipment and personnel hours, please see LALIT MATHUR'S diaries.

ABF placed panels down for the void formwork at the southeast void (DSC02073).
Work continues mobilizing supports for the lost deck in northeast void.
RPS has begun placing transverse bars (T-bars) in W2E (DSC02075).

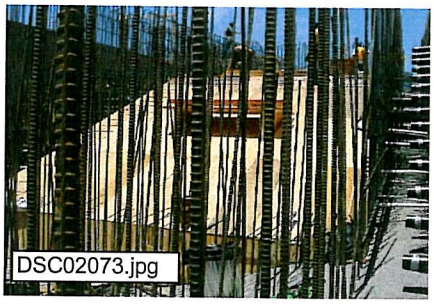
DSC02073.jpg

DSC02075.jpg

Materials:

Insp. Hrs.	
REG: 8.0	INTERMITTENT
OT:	INSPECTION

RECD 08 OCT 08 #007101

DAVID CHUNG — TE/CT
Title
