STATE OF CALIFORNIA
DEPARTMENT OF TRANSPORTATION
CP-CEM 4601 (Rev. 4/99) (Old HC-10A)

TOLL PROGRAM/DIST. 4 CONSTR.

Job Stamp:
04-SF-80-13.2/13.9 04-0120F4
SFOBB SAS
San Francisco Co. in San Francisco
Fm 0.6 km to 1.3 km East of Yerba Buena
Tunnel East Portal

Report No.	7-day const. cal.:	706	
	Project work day:	916	
Date the Shift Began:	11/18/08		
☐ NIGHTWORK	TUESDAY		
Shift Hrs	Start 7:00	Stop	15:30
Engineer's Hrs	Start 7:00	Stop	15:30

46.B

ASSISTANT RESIDENT ENGINEER'S DAILY BRIDGE REPORT

Location: W2 Cap Beam		Weather: clear
Remark: ironwork/formwork		Hi 65F/Lo 48F

Description of Operation:
ABF - begin sandblasting top of concrete (starting at southeast corner)
- continue bracing off forms at north end of cap beam in preparation for pour 5

RPS - continue ironwork for pour 5

RECD *09 JAN 06 #008235

HOURS - ITEM NO.							
ITEM NO. >>	38	48	133				
	Structural Concrete, Bridge	Bar Reinforcing Steel (Bridge)	Construction Surveying				IDLE OR DOWN/ ELSEWHERE
EQUIPMENT AND/OR LABOR: EQPT. NO. / NO. MEN / DESCRIPTION (Of Equipment or Labor)	RT	RT	RT				< RT/OT
For ABF equipment/personnel hours, please see Pamela Gagnier's and Lalit Mathur's diaries.							

CONTRACTORS		
Prime	American Bridge / Fluor JV	(P)
Sub #1	Regional	(1)
Sub #2		(2)
Sub #3		(3)
Sub #4		(4)
Sub #5		(5)

REMARKS		
Name	Classification	Prime / Sub

Checked monthly estimate for items 38 (structural concrete, bridge), item 48 (steel reinforcing), item 133 (construction surveying).

ABF has started sandblasting the top of concrete to remove the curing compound (DSC02630). They started at the southeast corner of the pour (DSC02636). Standing at a distance to avoid the sand, they appear to be covering every square inch - off the concrete and ducts.
ABF has started placing cooling pipes within the pour 5 area (DSC02642).

I have not yet surveyed the cracks for width. The sandblasting operation had just begun this morning and they have not yet covered enough area to do this safely.

RPS continue to place duct and reinforcement.

DSC02630.jpg

DSC02632.jpg

DSC02633.jpg

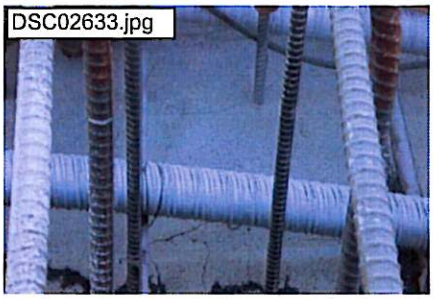

DSC02636.jpg

DSC02642.jpg

Materials:

Insp. Hrs.	
REG: 8.0	INTERMITTENT INSPECTION
OT:	

David Chung — TE/CT
Title

46-02
