STATE OF CALIFORNIA
DEPARTMENT OF TRANSPORTATION

Form HC-10A (Rev. 6/80)

Job Stamp
04-0120F4
SFOBB SAS

Const. Calendar Day No 873
Project Work Day No. 1083
Date 05/04/2009

Shift Hours Start 7.00 Stop 5:30
Inspector Shift 7:00 AM to 5:00 PM

ASSISTANT STRUCTURAL REPRESENTATIVE.

CONTRACTOR – ABFJV

EQUIPMENT AND/OR LABOR:

Equip. #	NO. MEN	DESCRIPTION (Of Equipment or Labor) 1	HOURS - ITEM NO. Regular	Over Time		Surveying						IDLE OR DOWN	REMARKS Name	Contractor
		Temp tower and trusses												
		Iron Worker Foreman	8	2									Ed Meyer	ABF/ JV
		Iron Worker App.	8	2									Matthew Cochran	ABF/ JV
		Iron Worker Jrny	8	2									Stanley Dalie	ABF/ JV
		Iron Worker Jrny	8	2									Jerry Kubala	ABF/ JV
		Iron Worker Jrny	8	2									Kevin Ratcliffe	ABF/ JV
		Iron Worker Foreman	8	2									Carlos Valverde	ABF/ JV
		Iron Worker Jrny	8	2									Steven Batiste	ABF/ JV
		Iron Worker Jrny	8	2									Josue Galvan	ABF/ JV
		Iron Worker Jrny	8	2									Gabriel Rios	ABF/ JV
		Iron Worker Jrny												
		Iron Worker Foreman	8	2									James Sturgeon	ABF/ JV
		Iron Worker	8	2									Matt Chamberlain	ABF/ JV
		Iron Worker App. Mechanic	8	2									Ronald Dameral	ABF/ JV
		Iron Worker App.	8	2									Ethan Kent	ABF/ JV
		Iron Worker Jrny	8	2									Serina Lafleur	ABF/ JV
		Iron Worker Jrny	8	2									Casey Lux	ABF/ JV
		Iron Worker Jrny	8	2									Mike Maday	ABF/ JV
		Iron Worker Jrny	8	2									Barry Rothman	ABF/ JV
		Iron Worker Jrny	-----	2									Wes Woodring	ABF/ JV
		Iron Worker Foreman	8	2									David Lucero	ABF/ JV
		Iron Worker Jrny	8	2									Brian Benson	ABF/ JV
		Iron Worker Jrny	8	2									Aaron Kent	ABF/ JV
		Iron Worker Jrny	8	2									Jose Meza Amaya	ABF/ JV
		Iron Worker Jrny	8	2									Obra Paulk	ABF/ JV
		Crane Operator	8	2									Rodney Anderson	ABF/ JV
		Crane Operator	8	2									Ernie Hamilton	ABF/ JV
		Crane Operator	8	2									Mike Klien	ABF/ JV
		Oiler	8	2									Daniel Martinez	ABF/ JV
		Oiler	8	2									Chriss Rayne	ABF/ JV
		Deck Eng.	8	2									Theo Rohr	ABF/ JV
		Deck Eng.		2									Dick Shafer	

REC'D '09 MAY-14 #009617

		Iron worker Foreman	8										Frank Brajkovich	ABF/ JV
		Iron worker Jrny	8										R. Clayborn	ABF/ JV
		Iron worker Jrny	8										D. Bazewicz	ABF/ JV
		Iron worker Jrny	8										Rory Hogan	ABF/ JV
		Iron worker Jrny	8										Robert Johnson	ABF/ JV
		Iron worker Jrny	8										Al McDaniel	ABF/ JV
		Iron worker Jrny	8										Salvador Sandoval	ABF/ JV
		Iron worker Jrny	8										Harold W. Wheeler	ABF/ JV
		Iron worker Jrny	8										James Zhen	ABF/ JV
		Iron worker App.	8										Todd Jackson	ABF/ JV
		Iron worker App.	8										Ryan Lockwood	ABF/ JV
		Iron worker App.	8										Jeremy Dolman	ABF/ JV
240ft boom	1	Ringer barge I												ABF/ JV
260ft boom	1	Ringer barge II												ABF/ JV
	2	Man lift												ABF/ JV
	2	Welding machine												ABF/ JV
58084	1	RT 160 crane												ABF/ JV
6- 18-4293, 4217	2	IR Compressor												ABF/ JV
549 07 5006	1	Generator												ABF/ JV
	1	Forklift												ABF/ JV
Welar I, II, XII	3	Barge												ABF/ JV
KRS 180-8, 318	2	Barge												ABF/ JV
TEC 35, 36, 27	3	Barge												ABF/ JV
YC -1333	1	Barge												ABF/ JV
OC 260, 261, 262, 265	4	Barge												ABF/ JV

Weather: Cloudy, 65 F

Description of Operation:

Temporary tower

1. Assembling connection plate to tower frame segments (columns and bracings) for tower erection continued today.
2. Welding 10" x 6" x ½" steel plates to tower legs for installing ladders lifelines.
3. Installing ladders and lifelines continued.

Trusses

1. Torquing bolts of upper and lower chords and bracing members of truss from tower B to tower D of W line
2. Erection of walkways on both side of truss between frame F1 and frame F1 C or PP – W14 and PP – W 15. Field splices W6.
3. Installing cradle supports (hat) on truss from tower B to tower D of W line continued today.
4. Installing connection plates at both side of Lower chords of truss segments S8E and S9E.
5. Picking truss segment S7E from barge OC – 260 with Shear Leg. Removing Barge OC – 260 from under the truss segment S7E. Moving barge 261 loaded with assembled truss segments S8E and S9E and line up with segment S7E. Aligning and Bolting splice connection plates to the end vertical bracing members, upper and lower chord members of truss segment S9E of E line for field splice13.
6. Drilling holes on erected truss' gusset plates (field splice 11) and installing bolts at S6E truss continued today.
7. Snug tightening of installed bolts at S6E truss connections. Drilling holes for horizontal bracing members, vertical bracings gusset plates are not drilled yet, these parts will be drilled after truss segment S6E surveyed and adjusted to its final position.

Miscellaneous

Additional Work on/off site:

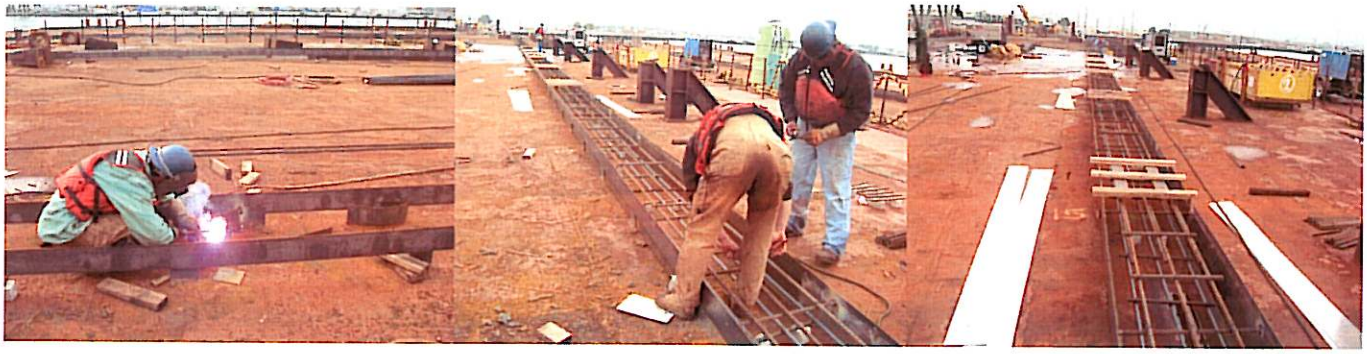

1. Ironworkers are welding forms on barge OC -265 and OC – 262 to prepare it for concrete pad for OBG segments.
2. Setting rebar inside the form for concrete pour.
3. I worked 2.0 hours overtime to cover contractor operation.

Inspector:

Masoud Modanlou _____ Trans Engineer (C)/Asst. Struct. Rep
