STATE OF CALIFORNIA
DEPARTMENT OF TRANSPORTATION

Form HC-10A (Rev. 6/80)

Job Stamp
04-0120F4
SFOBB SAS

Const. Calendar Day No 957
Project Work Day No. 1167
Date 07/27/2009
Shift Hours Start 6:30 Stop 3:30
Inspector Shift 7:00 AM to 3:30 PM

ASSISTANT STRUCTURAL REPRESENTATIVE.

CONTRACTOR – ABFJV

EQUIPMENT AND/OR LABOR:

Equip #	NO. MEN	DESCRIPTION (Of Equipment or Labor) 1	HOURS - ITEM NO. Regular	Over Time		Surveying					IDLE OR DOWN	REMARKS Name	Contractor
		Temp tower and trusses											
		Iron Worker Foreman	8									Ed Meyer	ABF/ JV
		Iron Worker App.	8									Matthew Cochran	ABF/ JV
		Iron Worker Jrny	8									Stanley Dalie	ABF/ JV
		Iron Worker Jrny	8									Jerry Kubala	ABF/ JV
		Iron Worker Jrny	8									Kevin Ratcliffe	ABF/ JV
		Iron Worker App.										Chris Biskner	ABF/ JV
		Iron Worker Foreman	8									Carlos Valverde	ABF/ JV
		Iron Worker Jrny	8									Steven Batiste	ABF/ JV
		Iron Worker App.	8									Jose Morales	ABF/ JV
		Iron Worker Jrny	8									James Wilkerson	ABF/ JV
		Iron Worker Jrny	8									Josue Galvan	ABF/ JV
		Iron Worker Jrny	8									Gabriel Rios	ABF/ JV
		Iron Worker Foreman	8									James Sturgeon	ABF/ JV
		Iron Worker										Troy Christianson	ABF/ JV
		Iron Worker	8									Matt Chamberlain	ABF/ JV
		Iron Worker App. Mechanic										Ronald Dameral	ABF/ JV
		Iron Worker App.	8									Ethan Kent	ABF/ JV
		Iron Worker Jrny	8									Serina Lafleur	ABF/ JV
		Iron Worker Jrny	8									Casey Lux	ABF/ JV
		Iron Worker Jrny	8									Mike Maday	ABF/ JV
		Iron Worker Jrny	8									Barry Rothman	ABF/ JV
		Iron Worker Jrny	-----									Wes Woodring	ABF/ JV
		Iron Worker Foreman	8									David Lucero	ABF/ JV
		Iron Worker Jrny	8									Brian Benson	ABF/ JV
		Iron Worker Jrny	8									Aaron Kent	ABF/ JV
		Iron Worker Jrny	8									Jose Meza Amaya	ABF/ JV
		Iron Worker Jrny	8									Obra Paulk	ABF/ JV
		Crane Operator	8									Rodney Anderson	ABF/ JV
		Crane Operator	8									Ernie Hamilton	ABF/ JV
		Crane Operator	8									Mike Klein	ABF/ JV

RECD '09 AUG 28 #010301

		Oiler	8										Daniel Martinez	ABF/ JV
		Oiler	8										Chris Rayne	ABF/ JV
		Deck Eng.	8										Theo Rohr	ABF/ JV
		Deck Eng.	8										Dick Shafer	
		Iron worker Foreman	8										Frank Brajkovich	ABF/ JV
		Iron worker Jrny	8										R. Clayborn	ABF/ JV
		Iron worker Jrny	8										D. Bazewicz	ABF/ JV
		Iron worker Jrny	6										Rory Hogan	ABF/ JV
		Iron worker Jrny	8										Robert Johnson	ABF/ JV
		Iron worker Jrny	8										Al McDaniel	ABF/ JV
		Iron worker Jrny											Rick Royal	ABF/ JV
		Iron worker Jrny	8										Salvador Sandoval	ABF/ JV
		Iron worker Jrny	8										Harold W. Wheeler	ABF/ JV
		Iron worker Jrny	8										James Zhen	ABF/ JV
		Iron worker App.											Todd Jackson	ABF/ JV
		Iron worker App.											Ryan Lockwood	ABF/ JV
		Iron worker App.											Jeremy Dolman	ABF/ JV
240ft boom	1	Ringer barge I												ABF/ JV
260ft boom	1	Ringer barge II												ABF/ JV
481 93 5006 481 40 7013	2	Man lift												ABF/ JV
	2	Welding machine												ABF/ JV
58084	1	RT 160 crane												ABF/ JV
6- 18-4293, 4217	2	IR Compressor												ABF/ JV
549 07 5006	1	Generator												ABF/ JV
412 10 7101 417 40 5029	1	Forklift												ABF/ JV
Wetar I, II, XII	3	Barge												ABF/ JV
KRS 180-8, 318	2	Barge												ABF/ JV
TEC 35, 36, 27	3	Barge												ABF/ JV
YC -1333	1	Barge												ABF/ JV
OC 260, 261, 262, 265	4	Barge												ABF/ JV

Weather: Overcast, Sunny, 60 F

Description of Operation:

.**Trusses**

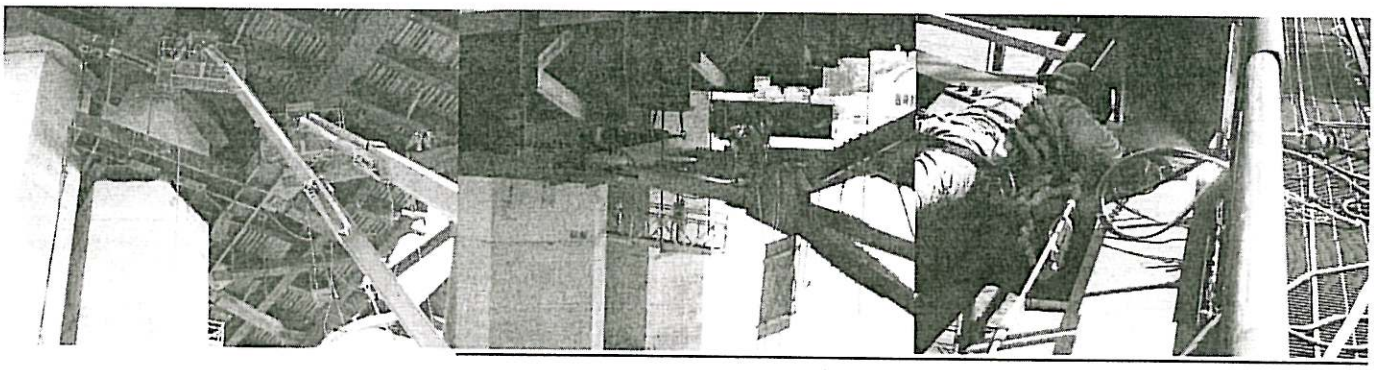

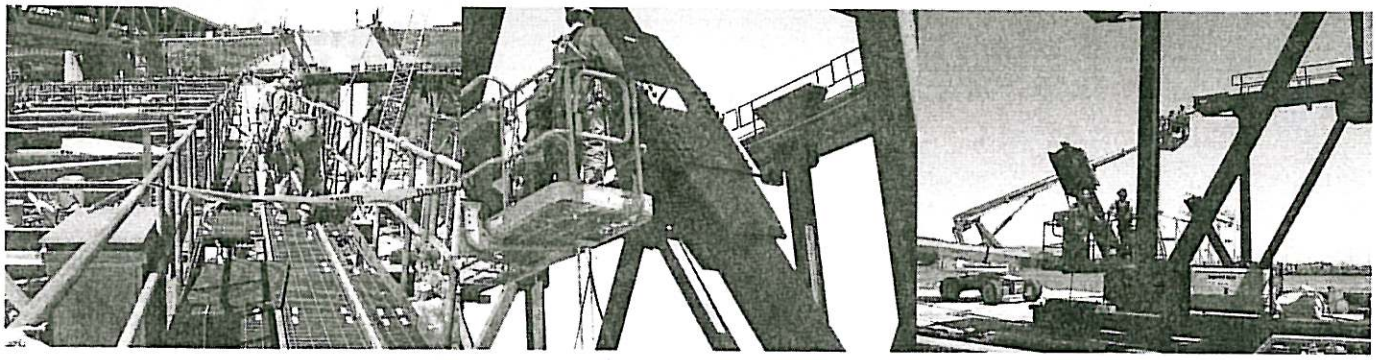

1. Torquing of bolts of beams connecting truss to collar at W2 north pier column.
2. ABF surveyors are checking the truss and temporary towers alignment. .
3. Welding stiffeners under the pedestals in W line.
4. Lowering walkway across the truss at E line to make enough clearance for OBG cradle and pushing frame.
5. Gluing neoprene pad to pedestals.
6. Installing a pair of hydraulic jacks on the lower chords of truss segment # 10, for field splicing E15 according to submittal 1279, drawing DE631D.
7. Splicing truss segment # 10 and # 11, E line, at berth 7.
8. Bolting and snug tightening and torquing bolts at field splice E 16.
9. Installing connection plate to truss segment # 11, W line, for future splicing, at berth 7.
10. Welding stainless steel plate under the OBG cradles are in progress.

Miscellaneous

Additional Work on/off site:

1. Sorting bolts to be used for splicing truss sections.
2. Downloading of tower H sections from the barge for pre assembling.
3. Miscellaneous works.

Inspector:

Masoud Modanlou _____ Trans Engineer (C)/Asst. Struct. Rep
