STATE OF CALIFORNIA
DEPARTMENT OF TRANSPORTATION

Form HC-10A (Rev. 6/80)

Job Stamp
04-0120F4
SFOBB SAS

Const. Calendar Day No 973
Project Work Day No. 1183
Date 08/12/2009

Shift Hours Start 6:30 Stop 3:30
Inspector Shift 7:00 AM to 3:30 PM

ASSISTANT STRUCTURAL REPRESENTATIVE.

CONTRACTOR – ABFJV

EQUIPMENT AND/OR LABOR:

Equip #	NO. MEN	DESCRIPTION (Of Equipment or Labor)	HOURS - ITEM NO. 1 Regular	Over Time		Surveying						IDLE OR DOWN	REMARKS Name	Contractor
		Temp tower and trusses												
		Iron Worker Foreman	8										Ed Meyer	ABF/ JV
		Iron Worker App.	8										Matthew Cochran	ABF/ JV
		Iron Worker Jrny	8										Stanley Dalie	ABF/ JV
		Iron Worker Jrny	8										Jerry Kubala	ABF/ JV
		Iron Worker Jrny	8										Kevin Ratcliffe	ABF/ JV
		Iron Worker App.	8										Chris Biskner	ABF/ JV
		Iron Worker Foreman											Carlos Valverde	ABF/ JV
		Iron Worker Jrny											Steven Batiste	ABF/ JV
		Iron Worker App.											Jose Morales	ABF/ JV
		Iron Worker Jrny											James Wilkerson	ABF/ JV
		Iron Worker Jrny											Josue Galvan	ABF/ JV
		Iron Worker Jrny											Gabriel Rios	ABF/ JV
		Iron Worker Foreman	8									1	James Sturgeon	ABF/ JV
		Iron Worker	8									1	Troy Christianson	ABF/ JV
		Iron Worker	8									1	Matt Chamberlain	ABF/ JV
		Iron Worker App. Mechanic	8									1	Ronald Dameral	ABF/ JV
		Iron Worker App.	8									1	Paul Good	ABF/ JV
			8									1	Eduardo Jimenez	
		Iron Worker Jrny	8									1	Serina Lafleur	ABF/ JV
		Iron Worker Jrny	8									1	Casey Lux	ABF/ JV
		Iron Worker Jrny	8									1	Mike Maday	ABF/ JV
		Iron Worker Jrny	8									1	Barry Rothman	ABF/ JV
		Iron Worker Jrny	8									1	Jaime Baragan	ABF/ JV
		Iron Worker Foreman	8									1	David Lucero	ABF/ JV
		Iron Worker Jrny	8									1	Matt Holt	ABF/ JV
		Iron Worker Jrny	8									1	James Laahs	ABF/ JV
		Iron Worker Jrny	8									1	Aaron Kent	ABF/ JV
		Iron Worker Jrny	8									1	Jose Meza Amaya	ABF/ JV
		Iron Worker Jrny	8									1	Obra Paulk	ABF/ JV
		Crane Operator	8										Rodney Anderson	ABF/ JV

RECD H:31 OCT-06 #011070

		Crane Operator	8										Ernie Hamilton	ABF/ JV
		Crane Operator	8										Mike Klein	ABF/ JV
		Oiler	8										Daniel Martinez	ABF/ JV
		Oiler	8										Chris Rayne	ABF/ JV
		Deck Eng.	8										Theo Rohr	ABF/ JV
		Deck Eng.	8										Dick Shafer	ABF/ JV
		Iron worker Foreman	8										Frank Brajkovich	ABF/ JV
		Iron worker Jrny	8										R. Clayborn	ABF/ JV
		Iron worker Jrny	8										D. Bazewicz	ABF/ JV
		Iron worker Jrny	8										Rory Hogan	ABF/ JV
		Iron worker Jrny	8										Al McDaniel	ABF/ JV
		Iron worker Jrny	8										Salvador Sandoval	ABF/ JV
		Iron worker App.	8										Jeremy Dolman	ABF/ JV
240ft boom	1	Ringer barge I												ABF/ JV
260ft boom	1	Ringer barge II												ABF/ JV
481 93 5006 481 40 7013	2	Man lift												ABF/ JV
	2	Welding machine												ABF/ JV
58084	1	RT 160 crane												ABF/ JV
6- 18-4293, 4217	2	IR Compressor												ABF/ JV
549 07 5006	1	Generator												ABF/ JV
412 10 7101 417 40 5029	1	Forklift												ABF/ JV
Wetar I, II, XII	3	Barge												ABF/ JV
KRS 180-8, 318	2	Barge												ABF/ JV
TEC 35, 36, 27	3	Barge												ABF/ JV
YC 1333	1	Barge												ABF/ JV
OC 260, 261, 262, 265	4	Barge												ABF/ JV

Weather: Overcast, Sunny, 60 F

Description of Operation:

.**Trusses**

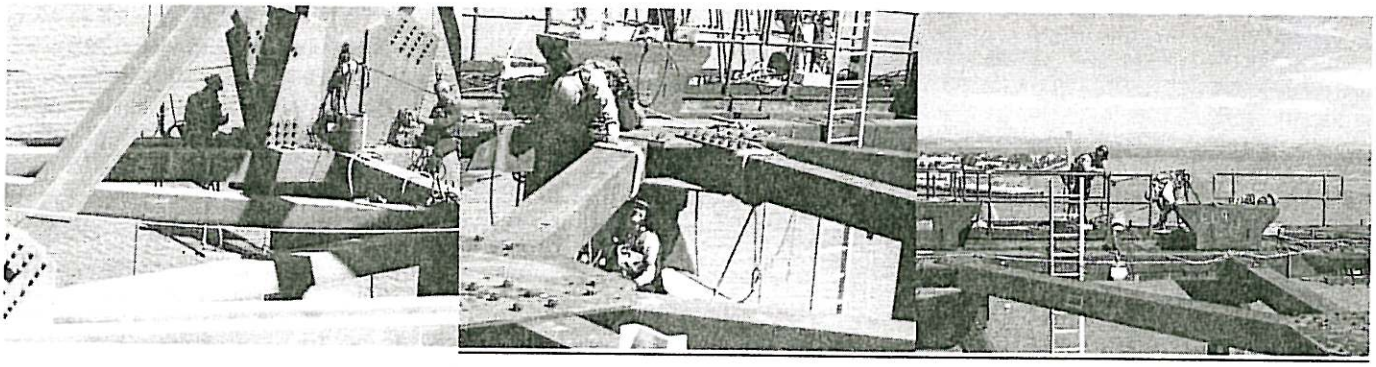

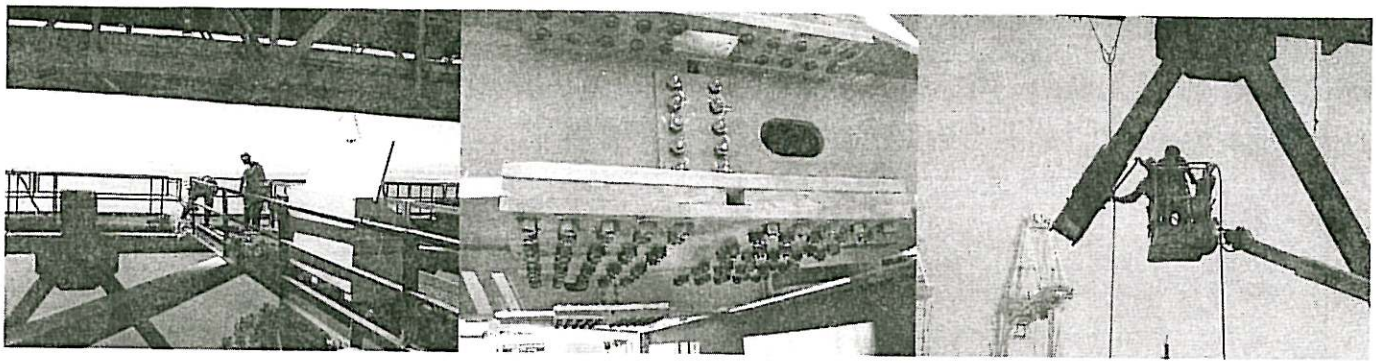

1. Drilling holes in connection plates joining truss to tower D W line
2. Bolting and sung tightening of bolts in connection plates between tower d and truss at W line.
3. Installing walkway grating in E line truss at field splice 15.
4. Bolting and sung tightening of bolts on upper and lower chords cross bracing members.
5. Welding angle iron 25 X 25 X 4 mm and small plates on top of pedestal to secure the neoprene pad at W line.
6. Repair work on pushing sled.
7. Swapping bolts at segment # 14 (tower H) bolting and snug tightening of bolts at berth 7.
8. Bolting the diagonal splicing members in truss segment # 13 at berth 7.
9. Installing splicing plates at the end of truss segments chords at berth 7.
10. Welding stainless steel plate under the OBG cradles are in progress.

Miscellaneous

Additional Work on/off site:

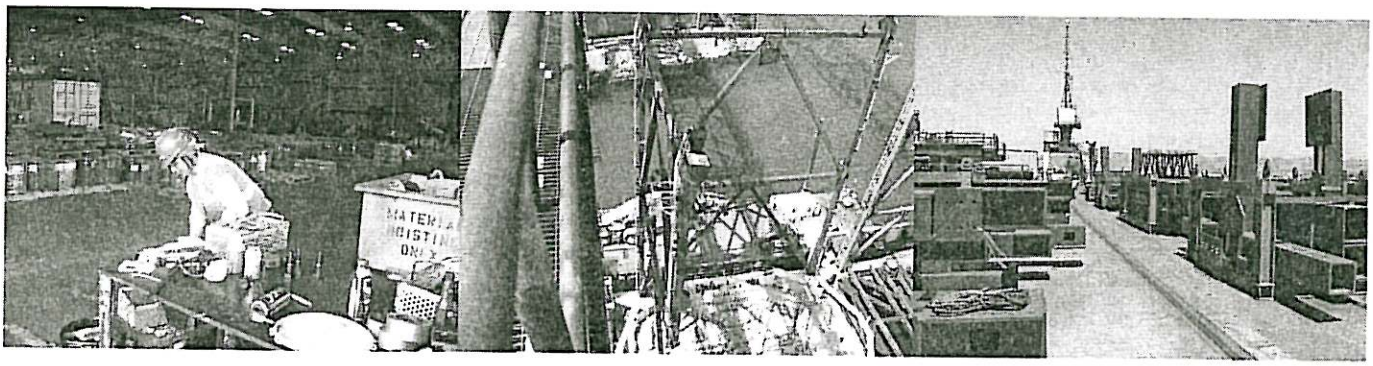

1. Sorting bolts to be used for splicing truss sections.
2. Erection of T1 erection tower continued today.
3. Miscellaneous works.

Inspector:

Masoud Modanlou _____ Trans Engineer (C)/Asst. Struct. Rep
