STATE OF CALIFORNIA
DEPARTMENT OF TRANSPORTATION

Form HC-10A (Rev. 6/80)

Job Stamp
04-0120F4
SFOBB SAS

Const. Calendar Day No 987
Project Work Day No. 1197
Date 08/26/2009

Shift Hours Start 6:30 Stop 3:30
Inspector Shift 7:00 AM to 3:30 PM

ASSISTANT STRUCTURAL REPRESENTATIVE.

CONTRACTOR – ABFJV

EQUIPMENT AND/OR LABOR:

Equip. #	NO MEN	DESCRIPTION (Of Equipment or Labor)	HOURS - ITEM NO.										REMARKS	
		1	Regular	Over Time		Surveying						IDLE OR DOWN	Name	Contractor
		Temp tower and trusses												
		Iron Worker Foreman	8										Ed Meyer	ABF/ JV
		Iron Worker App.	8										Matthew Cochran	ABF/ JV
		Iron Worker Jrny	8										Stanley Dalie	ABF/ JV
		Iron Worker Jrny	8										Jerry Kubala	ABF/ JV
		Iron Worker Jrny	8										Kevin Ratcliffe	ABF/ JV
		Iron Worker App.	8										Chris Biskner	ABF/ JV
		Iron Worker Foreman											Carlos Valverde	ABF/ JV
		Iron Worker Jrny											Steven Batiste	ABF/ JV
		Iron Worker App.											Jose Morales	ABF/ JV
		Iron Worker Jrny											James Wilkerson	ABF/ JV
		Iron Worker Jrny											Josue Galvan	ABF/ JV
		Iron Worker Jrny											Gabriel Rios	ABF/ JV
		Iron Worker Foreman	8									1	James Sturgeon	ABF/ JV
		Iron Worker	8									1	Troy Christianson	ABF/ JV
		Iron Worker	8									1	Matt Chamberlain	ABF/ JV
		Iron Worker App. Mechanic	8									1	Ronald Dameral	ABF/ JV
		Iron Worker App.	8									1	Paul Good	ABF/ JV
			8									1	Eduardo Jimenez	
		Iron Worker Jrny	8									1	Serina Lafleur	ABF/ JV
		Iron Worker Jrny	8									1	Casey Lux	ABF/ JV
		Iron Worker Jrny	8									1	Mike Maday	ABF/ JV
		Iron Worker Jrny	8									1	Barry Rothman	ABF/ JV
		Iron Worker Jrny	8									1	Jaime Baragan	ABF/ JV
		Iron Worker Foreman	8									1	David Lucero	ABF/ JV
		Iron Worker Jrny	8									1	Matt Holt	ABF/ JV
		Iron Worker Jrny	8									1	James Laahs	ABF/ JV
		Iron Worker Jrny	8									1	Aaron Kent	ABF/ JV
		Iron Worker Jrny	8									1	Jose Meza Amaya	ABF/ JV
		Iron Worker Jrny	8									1	Obra Paulk	ABF/ JV
		Crane Operator	8										Rodney Anderson	ABF/ JV

RECD H31 OCT-06 H011079

		Crane Operator	8										Ernie Hamilton	ABF/ JV
		Crane Operator	8										Mike Klein	ABF/ JV
		Oiler	8										Daniel Martinez	ABF/ JV
		Oiler	8										Chris Rayne	ABF/ JV
		Deck Eng.	8										Theo Rohr	ABF/ JV
		Deck Eng.	8										Dick Shafer	ABF/ JV
		Iron worker Foreman	8										Frank Brajkovich	ABF/ JV
		Iron worker Jrny	8										R. Clayborn	ABF/ JV
		Iron worker Jrny	8										D. Bazewicz	ABF/ JV
		Iron worker Jrny	8										Rory Hogan	ABF/ JV
		Iron worker Jrny	8										Al McDaniel	ABF/ JV
		Iron worker Jrny	8										Salvador Sandoval	ABF/ JV
		Iron worker App.	8										Jeremy Dolman	ABF/ JV
240ft boom	1	Ringer barge I												ABF/ JV
260ft boom	1	Ringer barge II												ABF/ JV
481 93 5006 481 40 7013	2	Man lift												ABF/ JV
	2	Welding machine												ABF/ JV
58084	1	RT 160 crane												ABF/ JV
6- 18-4293, 4217	2	IR Compressor												ABF/ JV
549 07 5006	1	Generator												ABF/ JV
412 10 7101 417 40 5029	1	Forklift												ABF/ JV
Wetar I, II XII	3	Barge												ABF/ JV
KRS 180-5, 316	2	Barge												ABF/ JV
TEC 35, 36, 27	3	Barge												ABF/ JV
YC 1333	1	Barge												ABF/ JV
OC 260, 261, 262, 265	4	Barge												ABF/ JV

Weather: Overcast, Sunny, 67 F

Description of Operation:

.<u>Trusses</u>

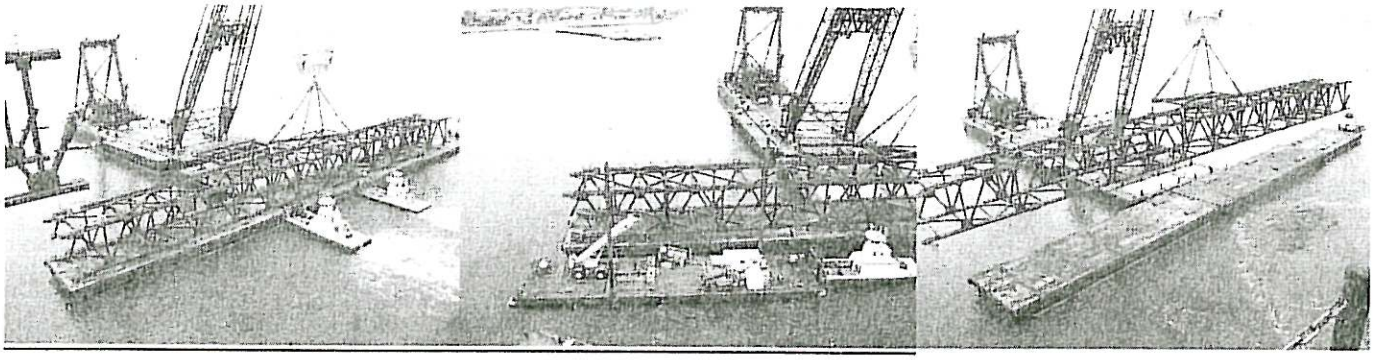

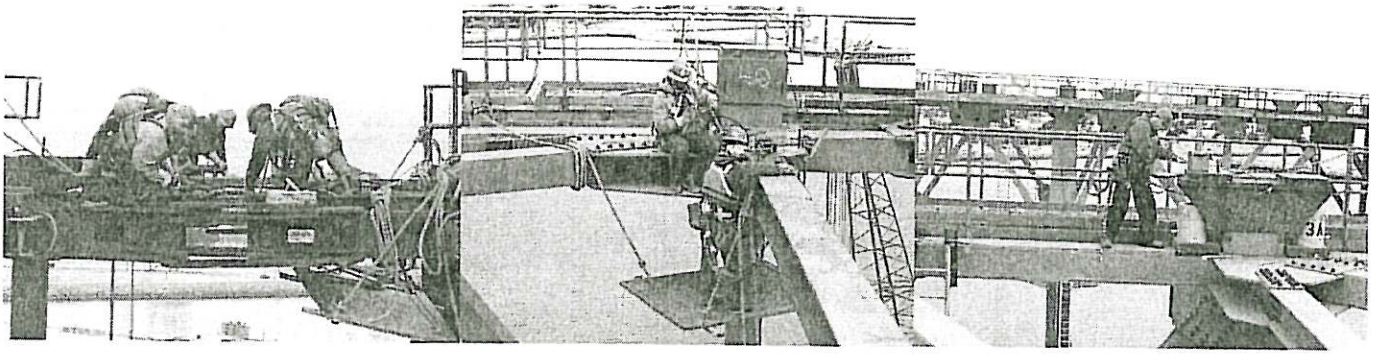

1. Pulling back the OBG cradle L1 E to its original position on E line truss, this cradle was used for testing the pushing sled.
2. Drilling holes in cross beam connection plate for bolting it to truss gusset plate. The holes in this beam were not aligned with holes of connection plate.
3. Erection of pre assembled truss segments # 9, #10 and #11 started at 6.00 am by positioning 3 barges in front of Shear Leg to provide enough room for barges loaded with truss segment from tower F to tower G. After hooking the Shear Leg picking frame with truss pad eyes lifting truss started at about 8.00 am but, lifted truss was not balanced after lifting about 10 ft, Shear leg set the truss back to its original position on the barges, to balance the truss for erection iron worker removed one of the three concrete blocks from the top of truss at the east end of segment 9. At about 11.00am pre assembled truss segments were aligned with the hammerhead (segment # 8) and driving drifting pin and bolting started for field splice W13.
4. Drilling holes on top flange of OBG cradle # L4 W for installation of OBG pedestals in berth 7.
5. Coring into the E2 footing concrete for installation of tower H anchor bolts.

Miscellaneous

Additional Work on/off site:

1. Sorting bolts to be used for splicing truss sections.
2. Miscellaneous works.

Inspector:

Masoud Modanlou _____ Trans Engineer (C)/Asst. Struct. Rep
