STATE OF CALIFORNIA
DEPARTMENT OF TRANSPORTATION

Form HC-10A (Rev. 6/80)

Job Stamp
04-0120F4
SFOBB SAS

Const. Calendar Day No 1010
Project Work Day No. 1220
Date 09/18/2009

Shift Hours Start 6:30 Stop 3:30
Inspector Shift 7:00 AM to 3:30 PM

ASSISTANT STRUCTURAL REPRESENTATIVE.

CONTRACTOR – ABFJV

EQUIPMENT AND/OR LABOR:

Equip. #	NO. MEN	DESCRIPTION (Of Equipment or Labor) 1	HOURS - ITEM NO. Regular	Over Time		Surveying						IDLE OR DOWN	REMARKS Name	Contractor
		Temp tower and trusses												
		Iron Worker Foreman	8										Ed Meyer	ABF/ JV
		Iron Worker App.	8										Matthew Cochran	ABF/ JV
		Iron Worker Jrny	8										Stanley Dalie	ABF/ JV
		Iron Worker Jrny	8										Jerry Kubala	ABF/ JV
		Iron Worker Jrny	8										Kevin Ratcliffe	ABF/ JV
		Iron Worker App.	8										Chris Biskner	ABF/ JV
		Iron Worker Foreman											Carlos Valverde	ABF/ JV
		Iron Worker Jrny											Steven Batiste	ABF/ JV
		Iron Worker App.											Jose Morales	ABF/ JV
		Iron Worker Jrny											James Wilkerson	ABF/ JV
		Iron Worker Jrny											Josue Galvan	ABF/ JV
		Iron Worker Jrny											Gabriel Rios	ABF/ JV
		Iron Worker Foreman	8										James Sturgeon	ABF/ JV
		Iron Worker	8										Matt Chamberlain	ABF/ JV
		Iron Worker App. Mechanic	8										Ronald Dameral	ABF/ JV
		Iron Worker	8										Eduardo Jimenez	
		Iron Worker Jrny	8										Casey Lux	ABF/ JV
		Iron Worker Jrny	8										Mike Maday	ABF/ JV
		Iron Worker Jrny	8										Barry Rothman	ABF/ JV
		Iron Worker Jrny	8										Jaime Baragan	ABF/ JV
		Iron Worker Foreman	8										David Lucero	ABF/ JV
		Iron Worker Jrny	8										Matt Holt	ABF/ JV
		Iron Worker Jrny	8										James Laahs	ABF/ JV
		Iron Worker Jrny	8										Aaron Kent	ABF/ JV
		Iron Worker Jrny	8										Jose Meza Amaya	ABF/ JV
		Iron Worker Jrny	8										Obra Paulk	ABF/ JV
		Crane Operator	8										Rodney Anderson	ABF/ JV
		Crane Operator	8										Ernie Hamilton	ABF/ JV
		Crane Operator	8										Mike Klein	ABF/ JV
		Oiler	8										Daniel Martinez	ABF/ JV

REC'D HJL OCT 06 #011094

		Oiler	8										Chris Rayne	ABF/ JV
		Deck Eng.	8										Theo Rohr	ABF/ JV
		Deck Eng.	8										Dick Shafer	ABF/ JV
		Iron worker Foreman	8										Frank Brajkovich	ABF/ JV
		Iron worker Jrny	8										D. Bazewicz	ABF/ JV
		Iron worker Jrny	8										Rory Hogan	ABF/ JV
		Iron worker Jrny	8										Salvador Sandoval	ABF/ JV
		Iron worker App.	8										Jeremy Dolman	ABF/ JV
240ft boom	1	Ringer barge I												ABF/ JV
260ft boom	1	Ringer barge II												ABF/ JV
481 93 5006 481 40 7013	2	Man lift												ABF/ JV
	2	Welding machine												ABF/ JV
58084	1	RT 160 crane												ABF/ JV
6- 18-4293, 4217	2	IR Compressor												ABF/ JV
549 07 5006	1	Generator												ABF/ JV
412 10 7101 417 40 5029	1	Forklift												ABF/ JV
Wetar I, II, XII	3	Barge												ABF/ JV
KRS 180-8, 318	2	Barge												ABF/ JV
TEC 35, 36, 27	3	Barge												ABF/ JV
YC -1333	1	Barge												ABF/ JV
OC 260, 261, 262, 265	4	Barge												ABF/ JV

Weather: Sunny, 70 F

Description of Operation:

Trusses

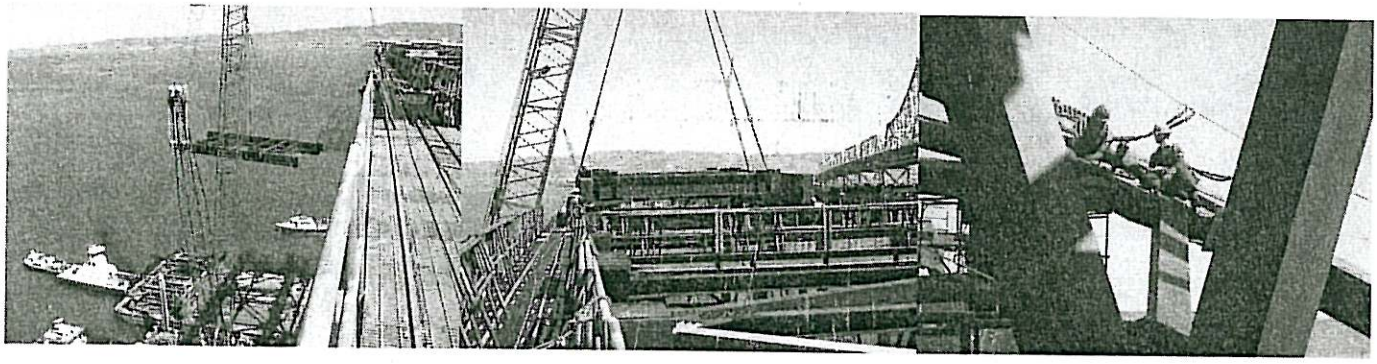

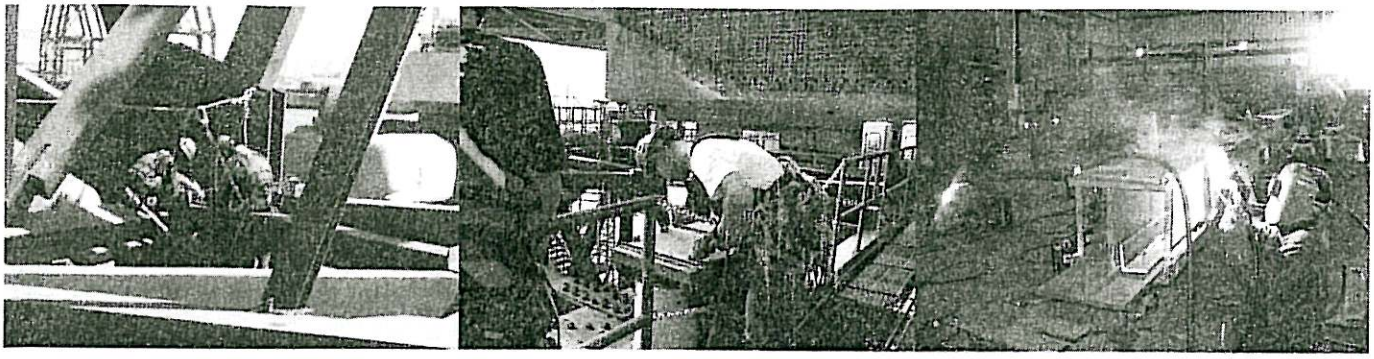

1. Using ringer barge crane picking OBG cradle WL1 from material barge and placing it on top of W line truss for pushing test. For this testing ABF is going to use the same pushing frame (sled) used to push cradle in E line
2. Bolting and snug tightening of bolts and torquing top and bottom bracing beams in truss segment 13 and 14.
3. Bolting and snug tightening of bolts and torquing bolts in frame 4 in truss segments 13 and 14.
4. Installing walkway beams at field splice E 18.
5. Installing walkway grating and bolting them.
6. Installing walkway across on top of truss segment 12.
7. Welding a new piece on build up cross beam PP – E40 is in progress.
8. Welding angle iron 25 X 25 X 4mm on top of pedestals to hold the neoprene pad in W line.
9. Setting neoprene pads on top of OBG cradle pedestal and bolting them with welded angle irons.
10. Jacking and shimming of OBG cradle pedestals at W line truss.
11. Removal of epoxy glue from the top of OBG pedestals, these epoxy were applied on top of OBG pedestal to glue the neoprene to restrain the movement of neoprene while pushing the cradle toward the W2.

Miscellaneous

Additional Work on/off site:

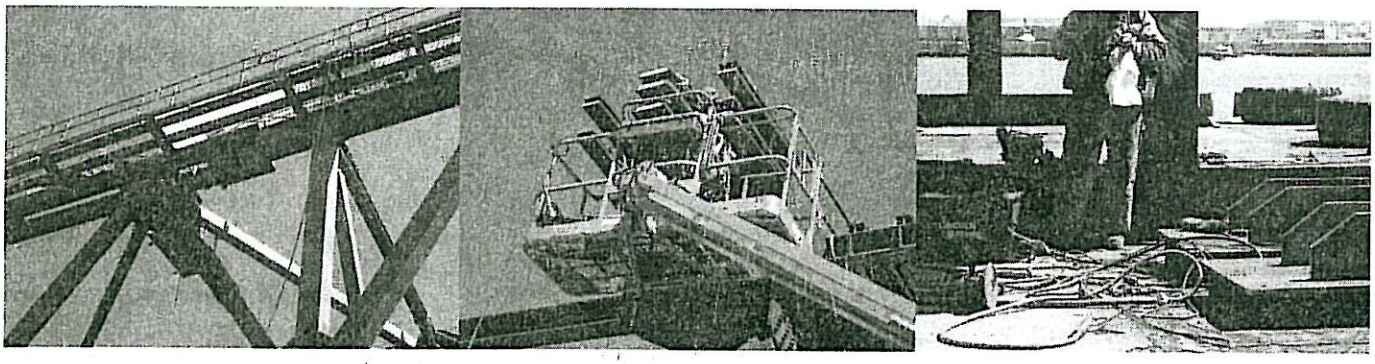

1. Sorting bolts to be used for splicing truss sections.
2. Welding diaphragm (stiffener) plates between the chords of truss segment 12. These plates are welded under the pedestal hats.
3. Welding steel plate with stiffeners to the column of supper structure built on barge for supporting T1 tower erection gantry.
4. Preparation of tower H columns by removing the temporary splicing bolts for permanent splicing in progress.
5. Miscellaneous works.

Inspector:

Masoud Modanlou _____ Trans Engineer (C)/Asst. Struct. Rep
