DEPARTMENT OF TRANSPORTATION
DIVISION OF ENGINEERING SERVICES
Office of Structural Materials
Quality Assurance and Source Inspection

Bay Area Branch
690 Walnut Ave.St. 150
Vallejo, CA 94592-1133
(707) 649-5453
(707) 649-5493

Contract #: 04-0120F4
Cty: SF/ALA Rte: 80 PM: 13.2/13.9
File #: 69.28

WELDING INSPECTION REPORT

Resident Engineer: Pursell, Gary
Address: 333 Burma Road
City: Oakland, CA 94607

Report No: WIR-001586
Date Inspected: 29-Jan-2008

Project Name: SAS Superstructure
Prime Contractor: American Bridge/Fluor Enterprises, a JV
Contractor: Zhenhua Port Machinery Company, Ltd (ZPMC), Changxing Island

OSM Arrival Time: 700
OSM Departure Time: 1700
Location: Shanghai, China

CWI Name:	N/A			**CWI Present:**	☑ Yes	☐ No	
Inspected CWI report:	☑ Yes	☐ No	☐ N/A	**Rod Oven in Use:**	☑ Yes	☐ No	☐ N/A
Electrode to specification:	☑ Yes	☐ No	☐ N/A	**Weld Procedures Followed:**	☑ Yes	☐ No	☐ N/A
Qualified Welders:	☑ Yes	☐ No	☐ N/A	**Verified Joint Fit-up:**	☑ Yes	☐ No	☐ N/A
Approved Drawings:	☑ Yes	☐ No	☐ N/A	**Approved WPS:**	☑ Yes	☐ No	☐ N/A
				Delayed / Cancelled:	☐ Yes	☑ No	☐ N/A

Bridge No: 34-0006
Component: OBG

Summary of Items Observed:

This Quality Assurance (QA) Inspector observed various fabrication and welding practices at Zhenhua Port Machinery Company (ZPMC) on Changxing Island in Shanghai, China today for the Self Anchored Suspension Bridge for San Francisco, California.

Orthotropic Bridge Girder (OBG)

In Bay 1 this QA Inspector observed the milling of plate edges, beveling of partial joint penetration (PJP) preparations, machining of 2 millimeter radius on edges of plates and drilling of bolt holes using hardened washer guides of un-bent closed u-rib plates. This QA Inspector also witnessed the simultaneous bending of the close u-rib panels in compliance with the special provisions. This QA Inspector observe ZMPC welder Gong Zhi Wu, welder identification 059405 fillet welding continuity panel 630 millimeter from the end of closed u-ribs U-031 & U-022. The weld number was DP-057-001-040 and some of the essential welding variables were checked and found to be as follows: voltage 25.3 and amperage 194.

WELDING INSPECTION REPORT

(Continued Page 2 of 2)

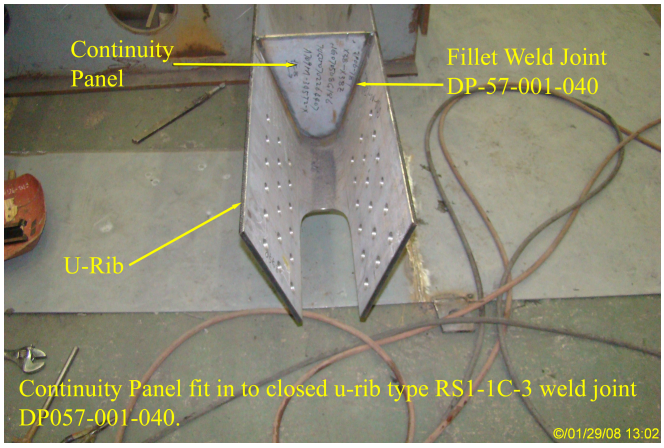

Summary of Conversations:

No conversations held today.

Comments

This report is for the purpose of determining conformance with the contract documents and is not for the purpose of making repair or fit for purpose recommendations. Should you require recommendations concerning repairs or remedial efforts please contact Mazen Wahbeh, (818) 292-0659, who represents the Office of Structural Materials for your project.

Inspected By:	Berger,Bruce	Quality Assurance Inspector
Reviewed By:	Cochran,Jim	QA Reviewer
