DEPARTMENT OF TRANSPORTATION
DIVISION OF ENGINEERING SERVICES
Office of Structural Materials
Quality Assurance and Source Inspection

Bay Area Branch
690 Walnut Ave.St. 150
Vallejo, CA 94592-1133
(707) 649-5453
(707) 649-5493

Contract #: 04-0120F4
Cty: SF/ALA Rte: 80 PM: 13.2/13.9
File #: 69.28

WELDING INSPECTION REPORT

Resident Engineer: Pursell, Gary
Address: 333 Burma Road
City: Oakland, CA 94607

Report No: WIR-011134
Date Inspected: 29-Dec-2009

Project Name: SAS Superstructure
Prime Contractor: American Bridge/Fluor Enterprises, a JV
Contractor: Zhenhua Port Machinery Company, Ltd (ZPMC), Changxing Island

OSM Arrival Time: 645
OSM Departure Time: 1845
Location: Shanghai, China

CWI Name: You Qi Guo.

Inspected CWI report:	☐ Yes	☑ No	☐ N/A	**CWI Present:**	☑ Yes	☐ No	
Electrode to specification:	☑ Yes	☐ No	☐ N/A	**Rod Oven in Use:**	☐ Yes	☐ No	☑ N/A
Qualified Welders:	☑ Yes	☐ No	☐ N/A	**Weld Procedures Followed:**	☑ Yes	☐ No	☐ N/A
Approved Drawings:	☑ Yes	☐ No	☐ N/A	**Verified Joint Fit-up:**	☑ Yes	☐ No	☐ N/A
				Approved WPS:	☑ Yes	☐ No	☐ N/A
				Delayed / Cancelled:	☐ Yes	☑ No	☐ N/A

Bridge No: 34-0006
Component: Tower Components

Summary of Items Observed:

On this date Caltrans OSM Quality Assurance (QA) Inspector, Amit K. Juvekar, was present during the times noted above for observations relative to the work being performed.

This QA Inspector observed the following work in progress:

Heavy Dock(Tower Assembly), South Tower, Lift 1, Skin E, Bearing Stiffener(Inside Tower).
FCAW welding of Partial Penetration weld joint (PJP) weld joint SSD1-SA16F/G-85; located on Heavy Dock(Tower Assembly), South Tower, Lift 1, Skin E. Welders are identified as 057180; ZPMC Quality Control Inspector (QC) is identified as You Qi Gou. The welding variables recorded by Quality Control Inspector (QC) appeared to comply with the Applicable WPS: WPS-B-T-2333-TC-P4-F.

Heavy Dock(Tower Assembly), South Tower, Lift 1, Skin A, Bearing Stiffener(Inside Tower).
FCAW welding of Partial Penetration weld joint (PJP) weld joint SSD1-SA15D/F-2; located on Heavy Dock(Tower Assembly), South Tower, Lift 1, Skin A. Welders are identified as 040338; ZPMC Quality Control Inspector (QC) is identified as You Qi Gou. The welding variables recorded by Quality Control Inspector (QC) appeared to comply with the Applicable WPS: WPS-B-T-2333-TC-P4-F.

Heavy Dock(Tower Assembly), South Tower, Lift 1, Skin B, Bearing Stiffener(Inside Tower).
FCAW welding of Partial Penetration weld joint (PJP) weld joint SSD1-SA18-10; located on Heavy Dock(Tower Assembly), South Tower, Lift 1, Skin B. Welders are identified as 069043; ZPMC Quality Control Inspector (QC) is identified as You Qi Gou. The welding variables recorded by Quality Control Inspector (QC)

appeared to comply with the Applicable WPS: WPS-B-T-2333-TC-P4-F.

Heavy Dock(Tower Assembly), South Tower, Lift 1, Skin D, Bearing Stiffener(Inside Tower).

FCAW welding of Partial Penetration weld joint (PJP) weld joint SSD1-SA40B/E-14, 8; located on Heavy Dock(Tower Assembly), South Tower, Lift 1, Skin D. Welders are identified as 047876, 068994; ZPMC Quality Control Inspector (QC) is identified as You Qi Gou. The welding variables recorded by Quality Control Inspector (QC) appeared to comply with the Applicable WPS: WPS-B-T-2333-TC-P4-F.

Heavy Dock(Tower Assembly), South Tower, Lift 1, Skin C, Bearing Stiffener(Outside Tower).

FCAW welding of Partial Penetration weld joint (PJP) weld joint SSD1-SA17F/G-71, 73; located on Heavy Dock(Tower Assembly), South Tower, Lift 1, Skin C. Welders are identified as 066236, 066733; ZPMC Quality Control Inspector (QC) is identified as You Qi Gou. The welding variables recorded by Quality Control Inspector (QC) appeared to comply with the Applicable WPS: WPS-B-T-2333-TC-P4-F.

Heavy Dock(Tower Assembly), South Tower, Lift 1, Skin A, Bearing Stiffener(Outside Tower).

FCAW welding of Partial Penetration weld joint (PJP) weld joint SSD1-SA111B/H-9; located on Heavy Dock(Tower Assembly), South Tower, Lift 1, Skin A. Welders are identified as 070046; ZPMC Quality Control Inspector (QC) is identified as You Qi Gou. The welding variables recorded by Quality Control Inspector (QC) appeared to comply with the Applicable WPS: WPS-B-T-2333-TC-P4-F.

Heavy Dock(Tower Assembly), West Tower, Lift 1, Skin B, Bearing Stiffener(Inside Tower).

FCAW welding of Partial Penetration weld joint (PJP) weld joint WSD1-SA279-4, 6, 12, 15; located on Heavy Dock(Tower Assembly), West Tower, Lift 1, Skin B. Welders are identified as 053486, 047701, 202821, 092218; ZPMC Quality Control Inspector (QC) is identified as You Qi Gou. The welding variables recorded by Quality Control Inspector (QC) appeared to comply with the Applicable WPS: WPS-B-T-2333-TC-P4-F.

Unless otherwise noted, all work observed on this date appeared to generally comply with applicable contract documents.

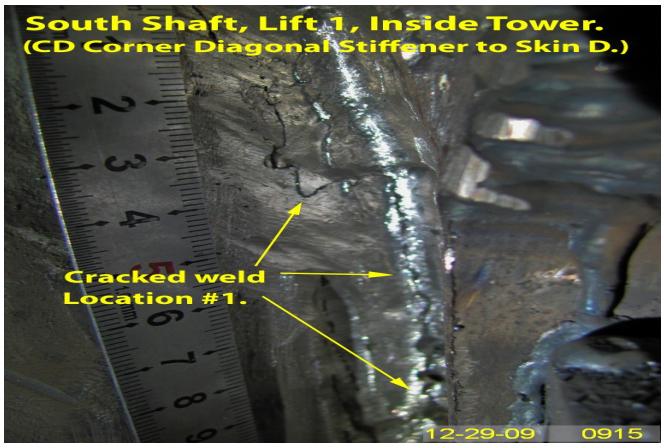

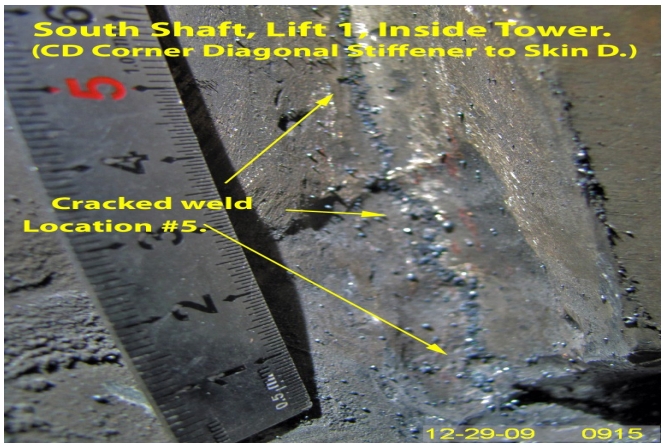

WELDING INSPECTION REPORT

(Continued Page 3 of 3)

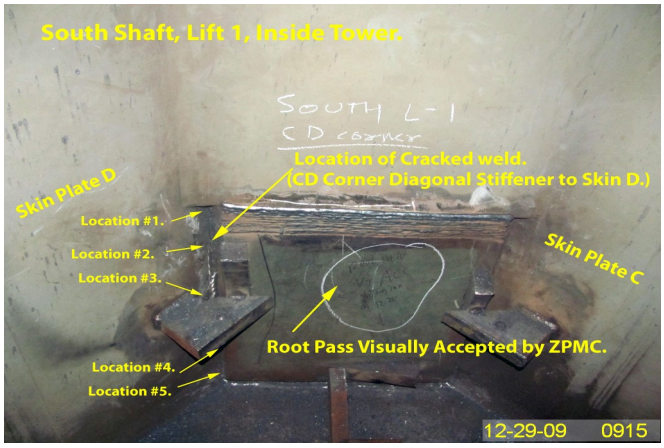

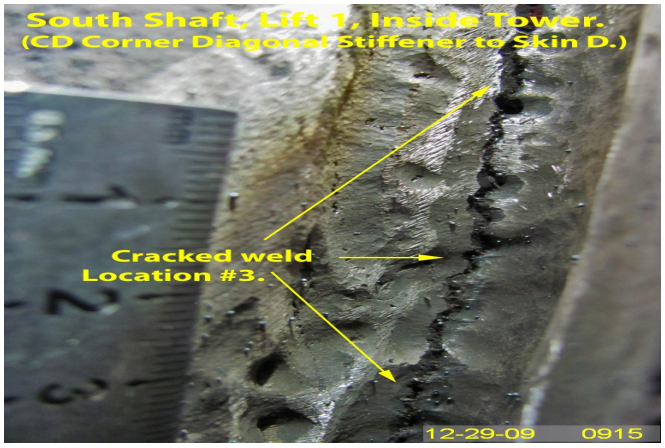

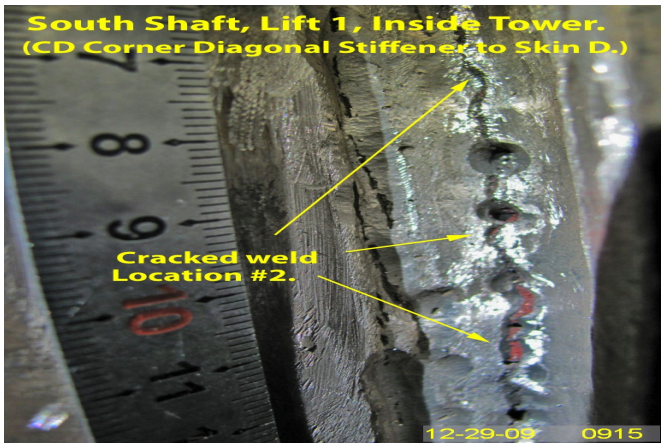

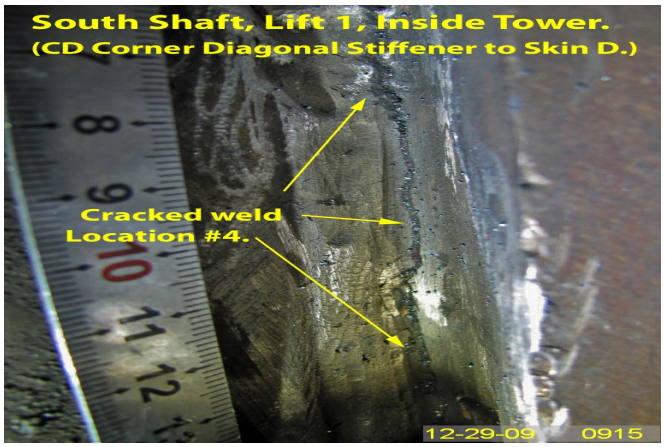

Summary of Conversations:

No relevant conversations.

Comments

This report is for the purpose of determining conformance with the contract documents and is not for the purpose of making repair or fit for purpose recommendations. Should you require recommendations concerning repairs or remedial efforts please contact Serge Sinevod, 13482570045, who represents the Office of Structural Materials for your project.

Inspected By:	Juvekar,Amit	Quality Assurance Inspector
Reviewed By:	Clifford,William	QA Reviewer
