DEPARTMENT OF TRANSPORTATION
DIVISION OF ENGINEERING SERVICES
Office of Structural Materials
Quality Assurance and Source Inspection

Bay Area Branch
690 Walnut Ave.St. 150
Vallejo, CA 94592-1133
(707) 649-5453
(707) 649-5493

Contract #: 04-0120F4
Cty: SF/ALA Rte: 80 PM: 13.2/13.9
File #: 1.28

WELDING INSPECTION REPORT

Resident Engineer: Casey, William
Address: 333 Burma Road
City: Oakland, CA 94607

Report No: WIR-026403
Date Inspected: 22-Sep-2011

Project Name: SAS Superstructure
Prime Contractor: American Bridge/Fluor Enterprises, a JV
Contractor: American Bridge/Fluor Enterprises, a JV

OSM Arrival Time: 700
OSM Departure Time: 1530
Location: Job Site

CWI Name:	As noted below		**CWI Present:**	☑ Yes	☐ No
Inspected CWI report:	☐ Yes	☐ No ☑ N/A	**Rod Oven in Use:**	☑ Yes	☐ No ☐ N/A
Electrode to specification:	☑ Yes	☐ No ☐ N/A	**Weld Procedures Followed:**	☑ Yes	☐ No ☐ N/A
Qualified Welders:	☑ Yes	☐ No ☐ N/A	**Verified Joint Fit-up:**	☐ Yes	☐ No ☑ N/A
Approved Drawings:	☑ Yes	☐ No ☐ N/A	**Approved WPS:**	☑ Yes	☐ No ☐ N/A
			Delayed / Cancelled:	☐ Yes	☑ No ☐ N/A

Bridge No: 34-0006
Component: OBG Components

Summary of Items Observed:

Quality Assurance Inspector (QA) William Clifford was at the American Bridge/Fluor (ABF) job site at Yerba Buena Island in California between the times noted above in order to monitor Quality Control functions and the in process work being performed by ABF personnel. The following items were observed:

East Line

This QA randomly observed ABF/JV qualified welder Fred Kaddu #2188 performing Shielded Metal Arc Welding (SMAW) with 5/32" diameter E7018H4R electrode and implementing Caltrans approved Welding Procedure Specification (WPS) ABF-WPS-D15-1050A-CU. This was a Complete Joint Penetration (CJP) weld on a 14mm plate insert at the “A” deck to close the lifting lug deck penetration holes. This work was located at E3-PP114-L#4 and was performed in the flat position from the top of the “A” deck plate.

During welding, ABF Quality Control (QC) Fred Vonhoff was noted monitoring the welding parameters. Welding parameters were recorded as (A=159).

This QA randomly observed ABF/JV qualified welder Jorge Lopez #6149 performing Shielded Metal Arc Welding (SMAW) with 5/32”" diameter E7018H4R electrode and implementing Caltrans approved Welding Procedure Specification (WPS) ABF-WPS-D15-1050A-CU. The joint being welded was a 14mm plate insert at the “A” deck to close the lifting lug deck penetration holes. This work was located at E4-PP111-L#2 and was performed in the flat position from the top of the “A” deck plate.

During welding, ABF Quality Control (QC) Fred Vonhoff was noted monitoring the welding parameters.

WELDING INSPECTION REPORT

(Continued Page 2 of 2)

Welding parameters were recorded as (A=156).

Approximately:
14:00 this QA observed an approximate 2.5mm offset in the plate alignment of the transverse stiffener at location 8E-PP61.5-E5 NW. QC Salvador Marino noted this offset in a report issued for Magnetic Particle testing he had performed earlier on this date. For further information please review photographs filed with this report.

Unless otherwise noted, all work observed on this date appeared to generally comply with applicable contract documents.

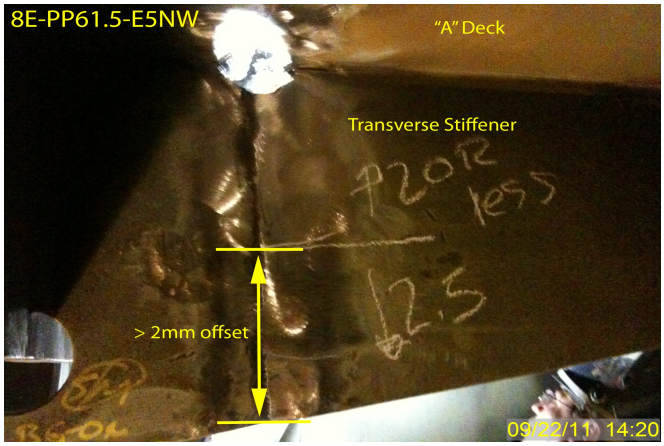

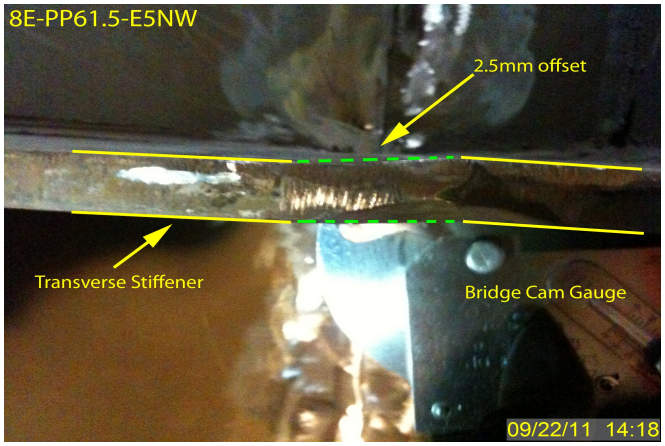

Summary of Conversations:
No relevant conversations.

Comments
This report is for the purpose of determining conformance with the contract documents and is not for the purpose of making repair or fit for purpose recommendations. Should you require recommendations concerning repairs or remedial efforts please contact SMR Nina Choy (510) 385-5910, who represents the Office of Structural Materials for your project.

Inspected By:	Clifford,William	Quality Assurance Inspector
Reviewed By:	Levell,Bill	QA Reviewer
