STATE OF CALIFORNIA	Job Stamp	7-day Const. Calendar	Day No. 967
DEPARTMENT OF TRANSPORTATION	SFOBB SAS	Project Work Day No.	Day No. 1167
Form HC-10A (Rev. 6/80)	04-0120F4	Date	**08/06/2009**

Inspectors Hours	Start	0700	Stop	1530
Shift Hours	Start	0700	Stop	1530

ASSISTANT RESIDENT ENGINEER'S

THANH V LE

CONTRACTOR – ABFJV

EQUIPMENT AND/OR LABOR:

Equip. #	NO. MEN	DESCRIPTION (Of Equipment or Labor)	HOURS - ITEM NO. Regular	OT								IDLE OR DOWN	REMARKS Name	Contractor
		Iron worker Foreman	8	0									E.J Meyer III	ABF/JV
		Iron worker Jrny	8	0									Chris Biskner	ABF/JV
		Iron worker Jrny	8	0									Stanley Dalie	ABF/JV
		Iron worker Jrny	8	0									Kevin Ratcliffe	ABF/JV
		Iron worker Jrny	8	0									Mathew Cochran	ABF/JV
		Iron worker Jrny	8	0									Jerry Kubala	ABF/JV
		Iron worker Jrny	0	0									Paul Good	ABF/JV
		Iron worker Jrny	0	0									Serina Lafeur	ABF/JV
		OE	8	0									Mike Klein	ABF/JV
		OE	8	0									Daniel Martinez	ABF/JV
		Shear Leg barge												ABF/JV
		Ringer barge I												ABF/JV
		Ringer barge II												ABF/JV
		Welding machine												ABF/JV
		RT 160 crane												ABF/JV
		IR Compressor												ABF/JV
1700 tons	1	Generator												
240ft boom	1	Forklift												
260ft boom	1	Barge												
	2	Barge												
58084	1	Barge												
6 18 4293,4217	2	Barge												
549 07 5006	1	Barge												
412 10 7101 417 40 5029	1	Man lift												
Welar I,II,XII	3													
KRS 180 8 318	2													
TEC 35,36,27	3													
YC 1333	1													

REC'D '09 AUG 28 #010846

OC 260, 261, 262,265	4													
481 93 5006 481 40 7013	2													

Weather: Partly Cloudy Hi 67 °F, Lo 46 °F.

Description of Operation:

1. Erection Tower and trusses.

Activities:

1. Office work:
   - Review plans, special provisions, RFI and ABF submittals for TT trusses.
2. Field work:
   - Iron worker crew continued bolting on the FS E15 to E17 trusses.
   - Welding defects on three B1 beams at driving frame of TTD had been repaired.Pending for QA/QC documentation to clear this issue.
3. Conversation and discussion:

4. Overtime reason:

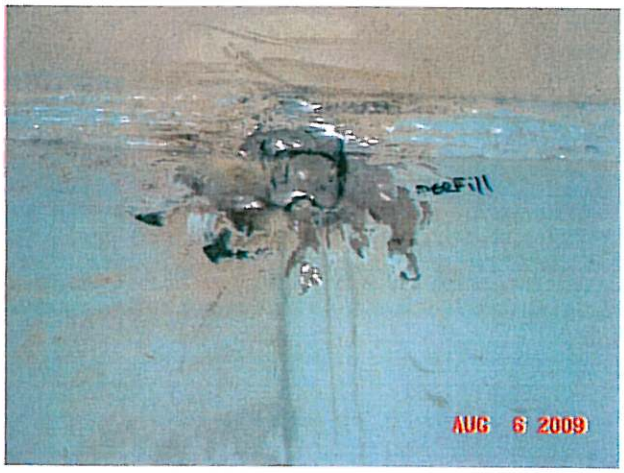

Repaired welds on B1 beams at TTD

Repaired welds on B1 beams at TTD

Thanh V Le _____ Trans Engineer (D)/Asst. Struct. Rep
